
Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

PUBLIC DISCLOSURE

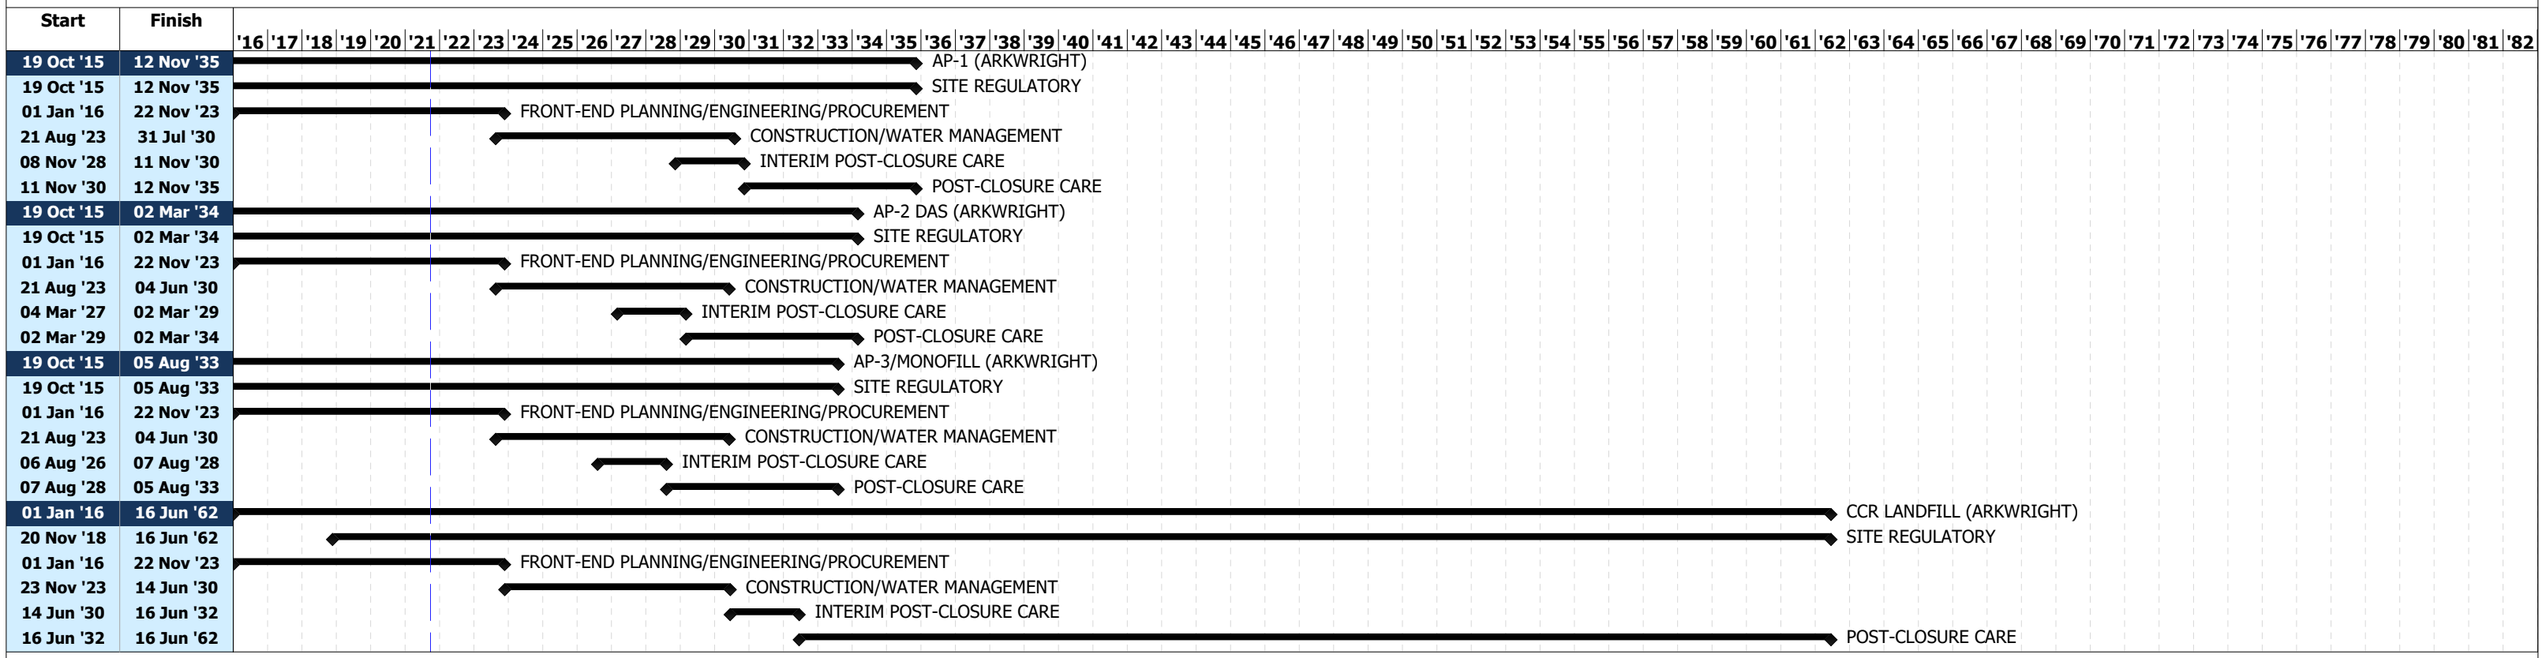


Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

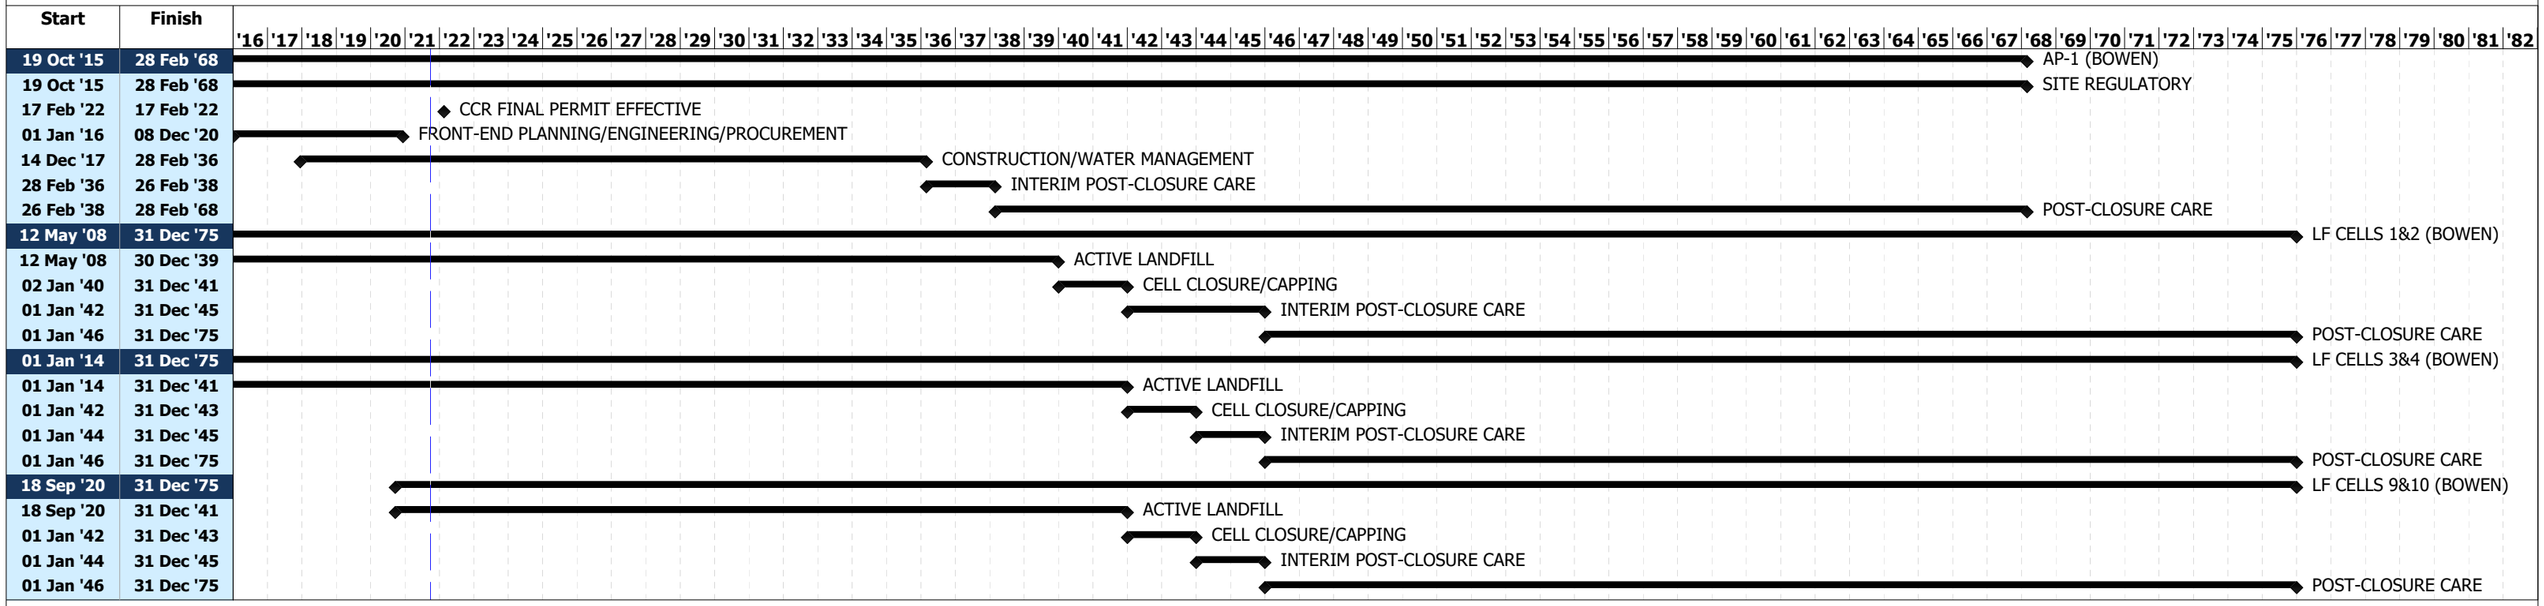

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
19 Oct '15	14 Oct '43	AP-B/AP-C/AP-D (BRANCH)
19 Oct '15	14 Oct '43	SITE REGULATORY
01 Jan '16	28 Jun '23	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
01 Mar '19	13 Oct '36	CONSTRUCTION/WATER MANAGEMENT
14 Oct '36	14 Oct '38	INTERIM POST-CLOSURE CARE
14 Oct '38	14 Oct '43	POST-CLOSURE CARE
19 Oct '15	10 Sep '43	AP-E (BRANCH)
19 Oct '15	10 Sep '43	SITE REGULATORY
01 Jan '16	28 Jun '23	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
01 Mar '19	07 Sep '36	CONSTRUCTION/WATER MANAGEMENT
10 Sep '36	10 Sep '38	INTERIM POST-CLOSURE CARE
10 Sep '38	10 Sep '43	POST-CLOSURE CARE
01 Jan '16	19 Aug '69	BRANCH LF
28 Feb '17	19 Aug '69	SITE REGULATORY
01 Jan '16	22 Jul '25	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
22 Aug '22	18 Aug '37	CONSTRUCTION/WATER MANAGEMENT
19 Aug '37	19 Aug '39	INTERIM POST-CLOSURE CARE
19 Aug '39	19 Aug '69	POST-CLOSURE CARE

'16 '17 '18 '19 '20 '21 '22 '23 '24 '25 '26 '27 '28 '29 '30 '31 '32 '33 '34 '35 '36 '37 '38 '39 '40 '41 '42 '43 '44 '45 '46 '47 '48 '49 '50 '51 '52 '53 '54 '55 '56 '57 '58 '59 '60 '61 '62 '63 '64 '65 '66 '67 '68 '69 '70 '71 '72 '73 '74 '75 '76 '77 '78 '79 '80 '81 '82

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

These changes will include, but are not limited to, the start date for construction/water management activities moving out beyond August 2022 for the Branch landfill.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
19 Oct '15	03 Mar '32	AP-1 (HAMMOND)
19 Oct '15	03 Mar '32	SITE REGULATORY
22 Jun '20	22 Jun '20	CCR FINAL PERMIT EFFECTIVE
01 Jan '16	30 Jun '21	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
11 Jan '21	04 Mar '25	CONSTRUCTION/WATER MANAGEMENT
04 Mar '25	04 Mar '27	INTERIM POST-CLOSURE CARE
04 Mar '27	03 Mar '32	POST-CLOSURE CARE
19 Oct '15	30 Jan '31	AP-2 (HAMMOND)
19 Oct '15	30 Jan '31	SITE REGULATORY
22 Jun '20	22 Jun '20	CCR FINAL PERMIT EFFECTIVE
01 Jan '16	30 Jun '21	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
11 Jan '21	25 Jan '24	CONSTRUCTION/WATER MANAGEMENT
25 Jan '24	30 Jan '26	INTERIM POST-CLOSURE CARE
02 Feb '26	30 Jan '31	POST-CLOSURE CARE
19 Oct '15	03 Jan '52	AP-3 (HAMMOND)
19 Oct '15	03 Jan '52	SITE REGULATORY
12 Jul '21	12 Jul '21	CCR DRAFT PERMIT
01 Jan '16	25 May '16	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
26 May '16	28 Apr '22	CONSTRUCTION/WATER MANAGEMENT
13 Nov '18	31 Dec '21	INTERIM POST-CLOSURE CARE
03 Jan '22	03 Jan '52	POST-CLOSURE CARE
19 Oct '15	21 May '38	AP-4 (HAMMOND)
19 Oct '15	21 May '38	SITE REGULATORY
27 Jan '21	27 Jan '21	CCR FINAL PERMIT EFFECTIVE
19 Oct '15	19 Dec '25	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
11 Jan '21	21 May '31	CONSTRUCTION/WATER MANAGEMENT
21 May '31	20 May '33	INTERIM POST-CLOSURE CARE
20 May '33	21 May '38	POST-CLOSURE CARE
19 Oct '15	05 Nov '63	HUFFAKER (HAMMOND)
19 Oct '15	05 Nov '63	SITE REGULATORY
01 Jan '16	07 Dec '23	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
22 Dec '21	09 Nov '31	CONSTRUCTION/WATER MANAGEMENT
04 Nov '25	04 Nov '33	INTERIM POST-CLOSURE CARE
04 Nov '33	05 Nov '63	POST-CLOSURE CARE

'16 '17 '18 '19 '20 '21 '22 '23 '24 '25 '26 '27 '28 '29 '30 '31 '32 '33 '34 '35 '36 '37 '38 '39 '40 '41 '42 '43 '44 '45 '46 '47 '48 '49 '50 '51 '52 '53 '54 '55 '56 '57 '58 '59 '60 '61 '62 '63 '64 '65 '66 '67 '68 '69 '70 '71 '72 '73 '74 '75 '76 '77 '78 '79 '80 '81 '82

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

These changes will include, but are not limited to, the extension of the end of construction/water management activities and updates to IPCC/PCC start and end dates for Hammond AP-3.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant


Start	Finish	'16	'17	'18	'19	'20	'21	'22	'23	'24	'25	'26	'27	'28	'29	'30	'31	'32	'33	'34	'35	'36	'37	'38	'39	'40	'41	'42	'43	'44	'45	'46	'47	'48	'49	'50	'51	'52	'53	'54	'55	'56	'57	'58	'59	'60	'61	'62	'63	'64	'65	'66	'67	'68	'69	'70	'71	'72	'73	'74	'75	'76	'77	'78	'79	'80	'81	'82
19 Oct '15	20 Nov '52	GRUMMAN RD. (KRAFT)		

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
19 Oct '15	23 Feb '55	AP-1 (MCDONOUGH)
19 Oct '15	23 Feb '55	SITE REGULATORY
01 Jan '16	11 Nov '21	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
18 Jan '16	24 Feb '23	CONSTRUCTION/WATER MANAGEMENT
24 Feb '23	24 Feb '25	INTERIM POST-CLOSURE CARE
24 Feb '25	23 Feb '55	POST-CLOSURE CARE
19 Oct '15	17 Aug '54	AP-2/AP-3/AP-4 (MCDONOUGH)
19 Oct '15	17 Aug '54	SITE REGULATORY
01 Jan '16	12 Feb '16	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
19 Jan '16	15 Aug '22	CONSTRUCTION/WATER MANAGEMENT
15 Aug '22	14 Aug '24	INTERIM POST-CLOSURE CARE
14 Aug '24	15 Aug '29	POST-CLOSURE CARE - MCDONOUGH AP-2
14 Aug '24	17 Aug '54	POST-CLOSURE CARE - MCDONOUGH AP-3/AP-4

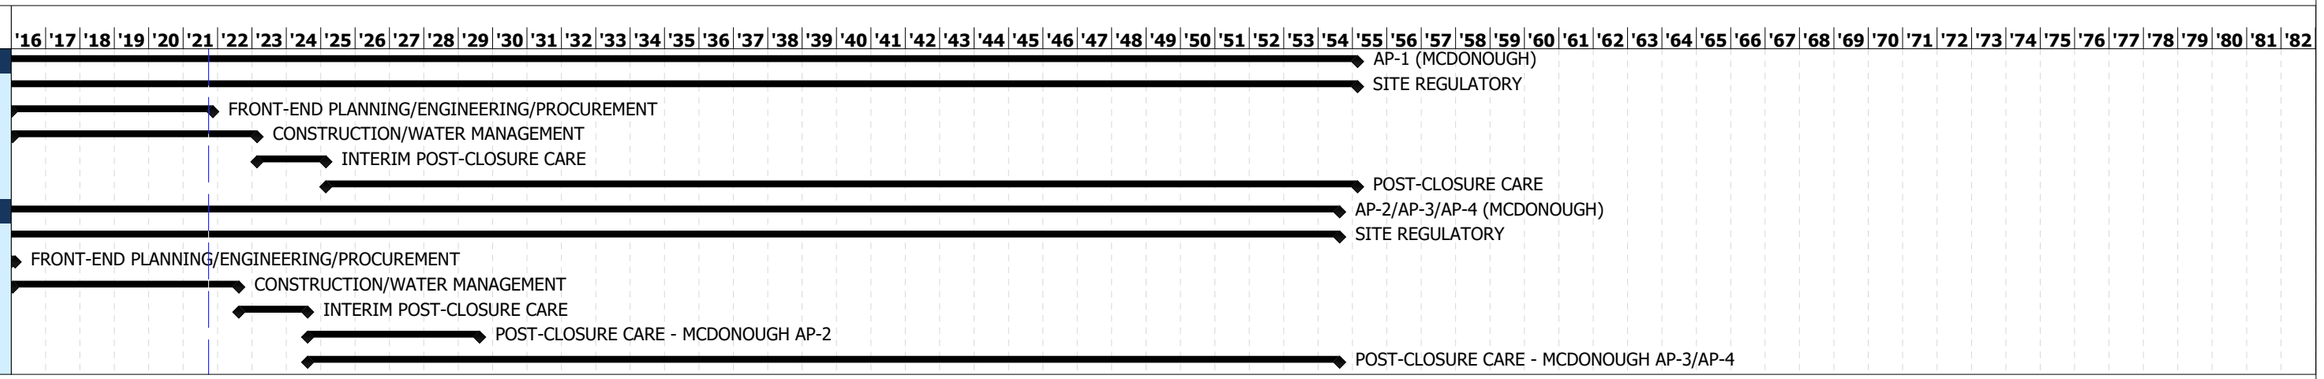


Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

These changes will include, but are not limited to, updates to the end of construction/water management activities and IPCC/PCC start and end dates for McDonough AP-1 and AP-2/3/4.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

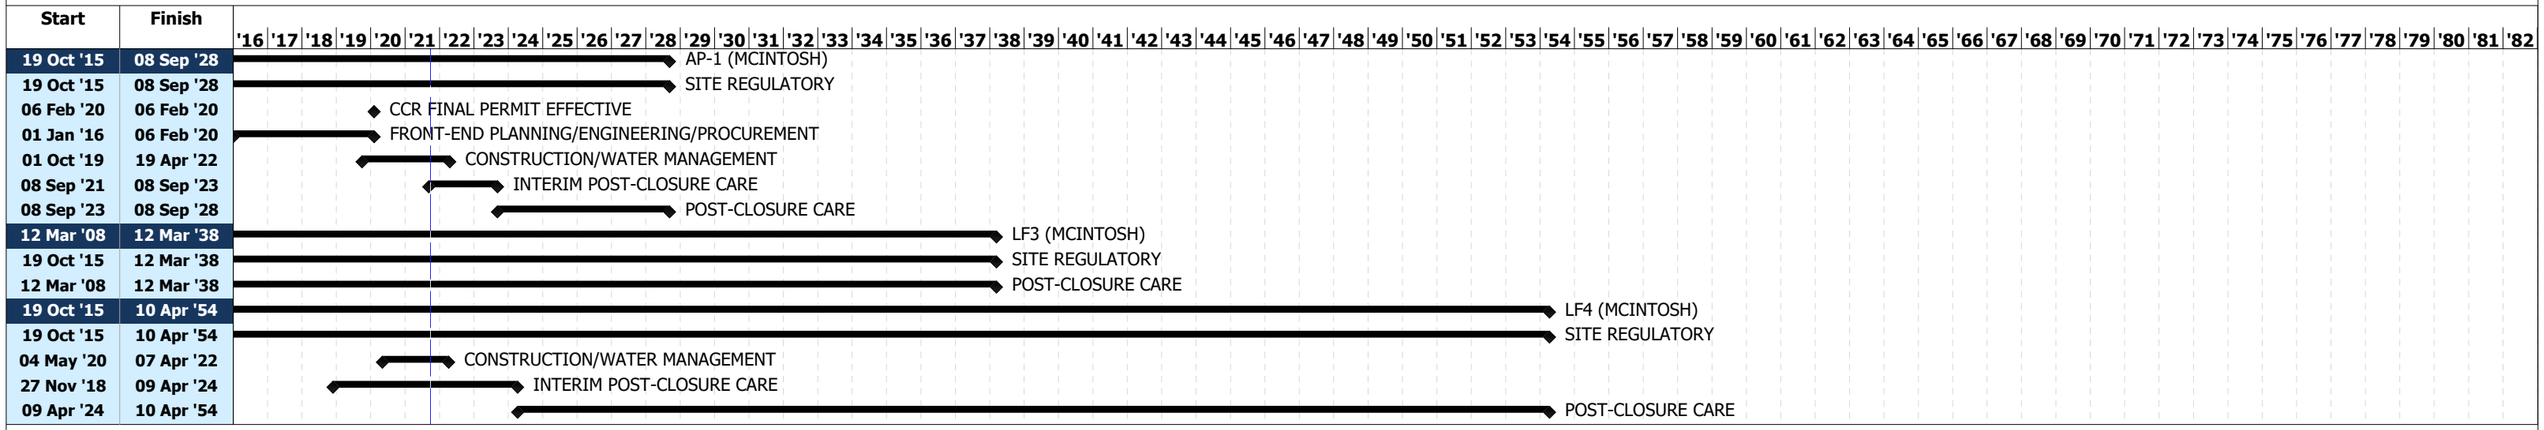

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.


These changes will include, but are not limited to, updates to the end of construction/water management activities and IPCC/PCC start and end dates for McIntosh AP-1.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	Gantt
19 Oct '15	21 Jul '36	AP-1 (MCMANUS)
19 Oct '15	21 Jul '36	SITE REGULATORY
18 Jun '21	18 Jun '21	CCR FINAL PERMIT EFFECTIVE
01 Jan '16	08 Dec '16	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
22 Jan '16	28 Jul '20	CONSTRUCTION/WATER MANAGEMENT
25 Nov '19	20 Jul '21	INTERIM POST-CLOSURE CARE
20 Jul '21	21 Jul '36	POST-CLOSURE CARE




Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
19 Oct '15	26 May '34	AP-1/AP-2/AP-A (MITCHELL)
19 Oct '15	26 May '34	SITE REGULATORY
28 Jun '22	28 Jun '22	CCR FINAL PERMIT EFFECTIVE
01 Jan '16	19 Feb '21	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
17 Sep '19	24 May '27	CONSTRUCTION/WATER MANAGEMENT
25 May '27	25 May '29	INTERIM POST-CLOSURE CARE
25 May '29	25 May '34	POST-CLOSURE CARE



Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.


These changes include, but are not limited to, inclusion of the CCR Final Permit Effective milestone.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
19 Oct '15	18 Apr '64	AP-1 (SCHERER)
19 Oct '15	18 Apr '64	SITE REGULATORY
01 Jan '16	09 Sep '22	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
04 Jun '21	19 Apr '32	CONSTRUCTION/WATER MANAGEMENT
21 Apr '32	20 Apr '34	INTERIM POST-CLOSURE CARE
20 Apr '34	18 Apr '64	POST-CLOSURE CARE
02 Jan '20	31 Dec '75	LF CELL 1 (SCHERER)
02 Jan '20	31 Dec '41	ACTIVE LANDFILL
01 Jan '42	31 Dec '43	CELL CLOSURE/CAPPING
01 Jan '44	31 Dec '45	INTERIM POST-CLOSURE CARE
01 Jan '46	31 Dec '75	POST-CLOSURE CARE
02 Jan '20	31 Dec '75	PAC/ASH CELL (SCHERER)
02 Jan '20	31 Dec '26	ACTIVE LANDFILL
01 Jan '27	31 Dec '28	CELL CLOSURE/CAPPING
01 Jan '29	31 Dec '45	INTERIM POST-CLOSURE CARE
01 Jan '46	31 Dec '75	POST-CLOSURE CARE

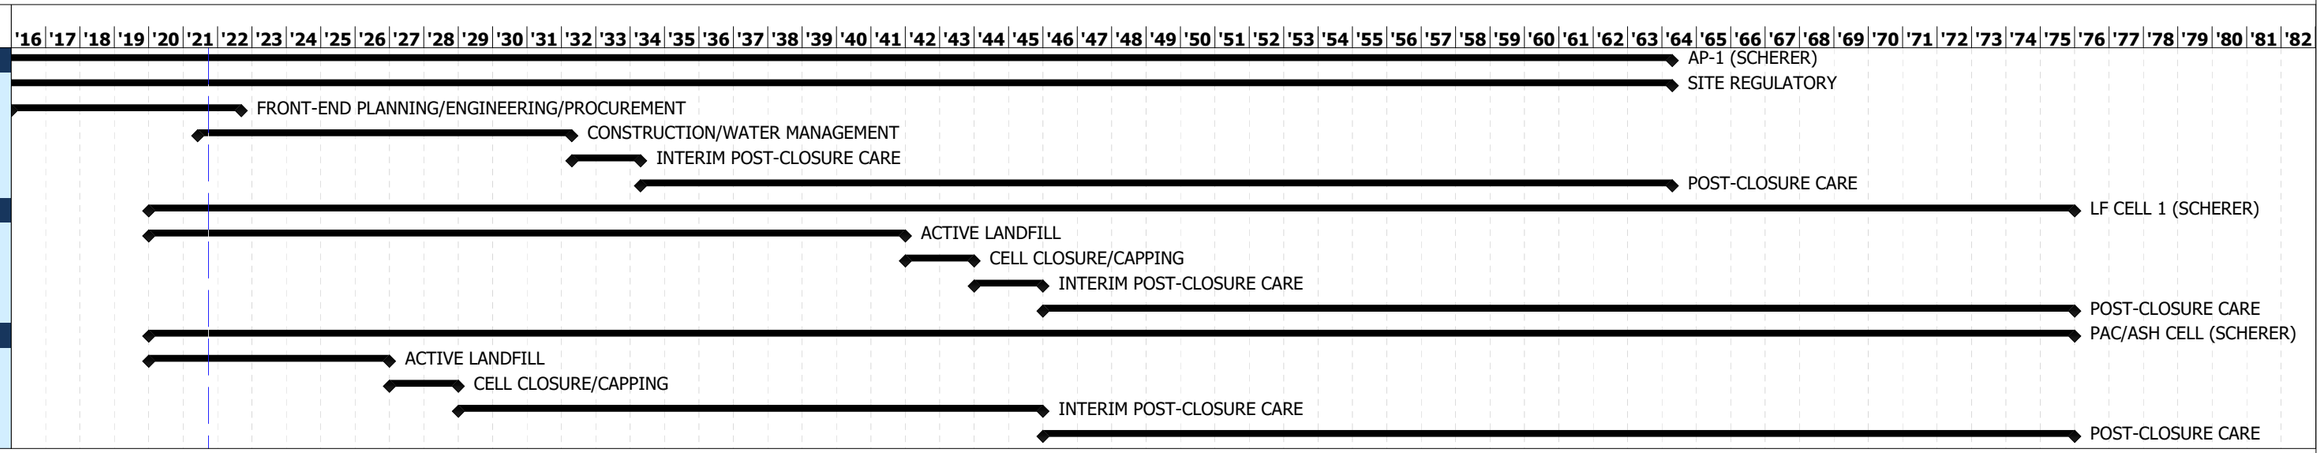

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.


Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

PUBLIC DISCLOSURE

Start	Finish	Plant
19 Oct '15	03 Nov '39	AP-1 (WANSLEY)
19 Oct '15	03 Nov '39	SITE REGULATORY
01 Jan '16	16 Apr '25	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
19 Apr '21	02 Nov '32	CONSTRUCTION/WATER MANAGEMENT
03 Nov '32	02 Nov '34	INTERIM POST-CLOSURE CARE
02 Nov '34	03 Nov '39	POST-CLOSURE CARE
01 Jul '22	08 May '65	LF CELLS 1 - 4 (WANSLEY)
01 Jul '22	15 May '30	ACTIVE LANDFILL
16 May '30	07 May '33	CELL CLOSURE/CAPPING
08 May '33	07 May '35	INTERIM POST-CLOSURE CARE
08 May '35	08 May '65	POST-CLOSURE CARE

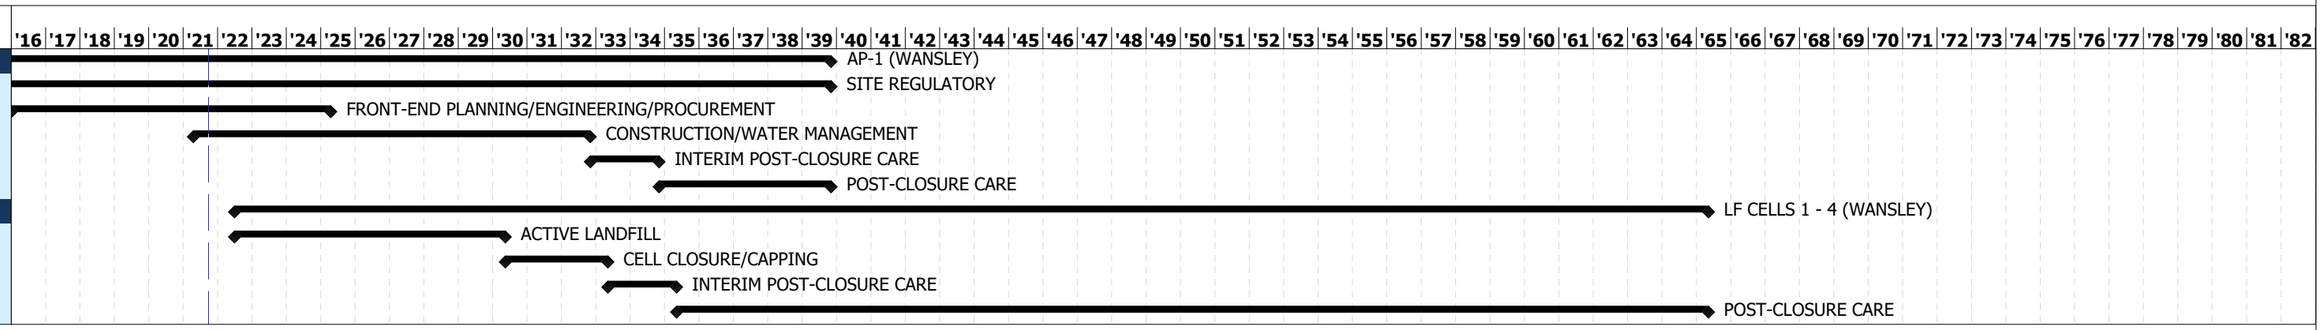

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

Georgia Power

Ash Pond Closure Portfolio

Gantt Chart by Plant

Start	Finish	
04 May '15	09 Mar '27	AP-1 (YATES)
19 Oct '15	09 Mar '27	SITE REGULATORY
06 Jan '22	06 Jan '22	CCR FINAL PERMIT EFFECTIVE
04 May '15	21 Jul '16	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
04 May '15	31 Dec '21	CONSTRUCTION/WATER MANAGEMENT
27 Nov '19	10 Mar '22	INTERIM POST-CLOSURE CARE
10 Mar '22	09 Mar '27	POST-CLOSURE CARE
19 Oct '15	01 Aug '29	AP-2 (YATES)
19 Oct '15	01 Aug '29	SITE REGULATORY
01 Jan '16	20 Nov '19	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
05 Sep '19	21 Oct '22	CONSTRUCTION/WATER MANAGEMENT
01 Aug '22	01 Aug '24	INTERIM POST-CLOSURE CARE
01 Aug '24	01 Aug '29	POST-CLOSURE CARE
19 Oct '15	23 Dec '54	AP-3/AP-B/AP-B'/AP-A (YATES)
19 Oct '15	23 Dec '54	SITE REGULATORY
01 Jan '16	30 Apr '18	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
19 Aug '16	23 Dec '22	CONSTRUCTION/WATER MANAGEMENT
23 Dec '22	23 Dec '24	INTERIM POST-CLOSURE CARE
23 Dec '24	23 Dec '54	POST-CLOSURE CARE
22 Jul '15	02 Feb '27	GYPSUM LF (YATES)
22 Jul '15	02 Feb '27	SITE REGULATORY
05 Jan '22	05 Jan '22	CCR FINAL PERMIT EFFECTIVE
19 Jan '17	02 Feb '22	INTERIM POST-CLOSURE CARE
03 Feb '22	02 Feb '27	POST-CLOSURE CARE
29 May '15	01 Jan '55	R-6/AP-C (YATES)
29 May '15	01 Jan '55	SITE REGULATORY
29 May '15	21 Jul '16	FRONT-END PLANNING/ENGINEERING/PROCUREMENT
29 May '15	29 Nov '22	CONSTRUCTION/WATER MANAGEMENT
30 Nov '22	31 Dec '24	INTERIM POST-CLOSURE CARE
01 Jan '25	01 Jan '55	POST-CLOSURE CARE

'16 '17 '18 '19 '20 '21 '22 '23 '24 '25 '26 '27 '28 '29 '30 '31 '32 '33 '34 '35 '36 '37 '38 '39 '40 '41 '42 '43 '44 '45 '46 '47 '48 '49 '50 '51 '52 '53 '54 '55 '56 '57 '58 '59 '60 '61 '62 '63 '64 '65 '66 '67 '68 '69 '70 '71 '72 '73 '74 '75 '76 '77 '78 '79 '80 '81 '82

Note: This schedule forecast is consistent with the April 2022 Environmental Compliance Strategy update in Docket No. 44160; the Company is currently reviewing all years in its CCR ARO estimates and expects updates by year-end.

These changes include,but are not limited to, updates to the end of construction/water management activities and IPCC/PCC start and end dates for Yates AP-1, AP-2, and the Gypsum LF.
