

Georgia Power

Activity ID	Start	Finish
Arkwright CCR	19-Oct-15 A	05-Feb-63
AP-1	19-Oct-15 A	29-Jul-37
Site Regulatory	19-Oct-15 A	29-Jul-37
Front End Planning	01-Jan-16 A	27-Jun-25
Construction	21-Aug-23	23-Apr-31
IPCC	28-Jul-30	28-Jul-32
PCC	28-Jul-32	29-Jul-37
AP-2 DAS	19-Oct-15 A	19-Nov-35
Site Regulatory	19-Oct-15 A	19-Nov-35
Front End Planning	01-Jan-16 A	14-Jul-25
Construction	21-Aug-23	23-Apr-31
IPCC	14-Nov-28	16-Nov-30
PCC	16-Nov-30	17-Nov-35
CCRLF/AP-3/Monofill	01-Jan-16 A	05-Feb-63
Site Regulatory	20-Nov-18 A	05-Feb-63
Front End Planning	01-Jan-16 A	14-Jul-25
Construct/Active/Close&Cap	11-Aug-25	23-Apr-31
IPCC	03-Feb-31	04-Feb-33
PCC	04-Feb-33	05-Feb-63

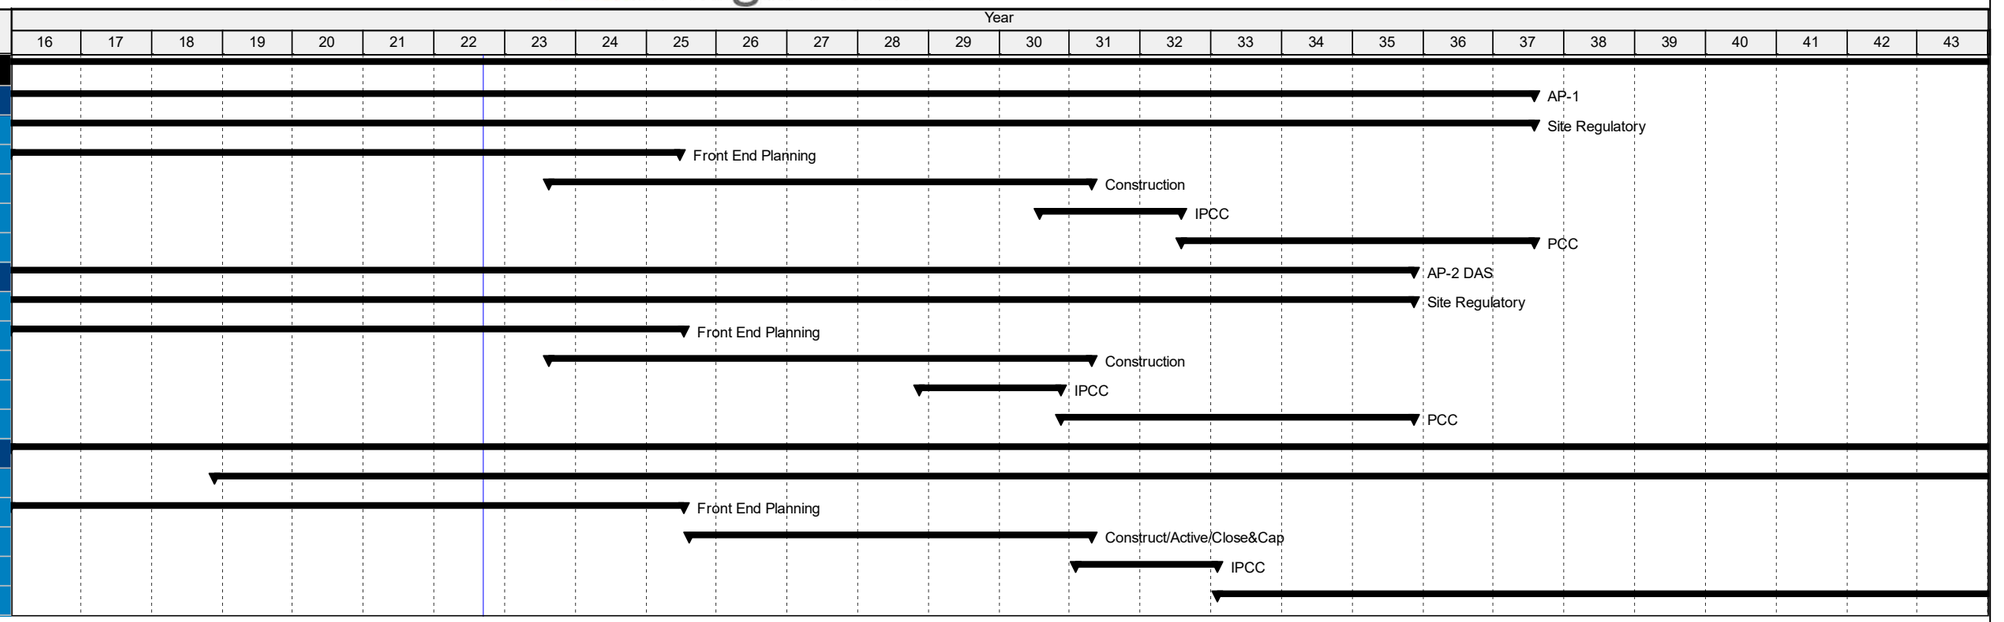

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.


Activity ID	Start	Finish
Bowen CCR	12-May-08 A	01-Jan-72
AP-1	19-Oct-15 A	07-Jul-66
Site Regulatory	19-Oct-15 A	07-Jul-66
CCR Final Permit Effective	17-Feb-22 A	17-Feb-22 A
Front End Planning	01-Jan-16 A	08-Dec-20 A
Construction	14-Dec-17 A	15-Dec-34
IPCC	06-Jul-34	04-Jul-36
PCC	04-Jul-36	06-Jul-66
Bowen Landfill	12-May-08 A	01-Jan-72
Site Regulatory	12-May-08 A	01-Jan-72
CCR Final Permit Effective	08-Dec-22	08-Dec-22
LF Cells 1&2	12-May-08 A	01-Jan-72
Active Landfill	12-May-08 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 3&4	01-Jan-14 A	01-Jan-72
Active Landfill	01-Jan-14 A	31-Dec-38
Cell Closure/Capping	01-Jan-39	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 5&6	17-Oct-22	01-Jan-72
Construct/Active for Closure	17-Oct-22	31-Dec-38
Cell Closure/Capping	01-Jan-39	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 9&10	18-Sep-20 A	01-Jan-72
Active Landfill	18-Sep-20 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72

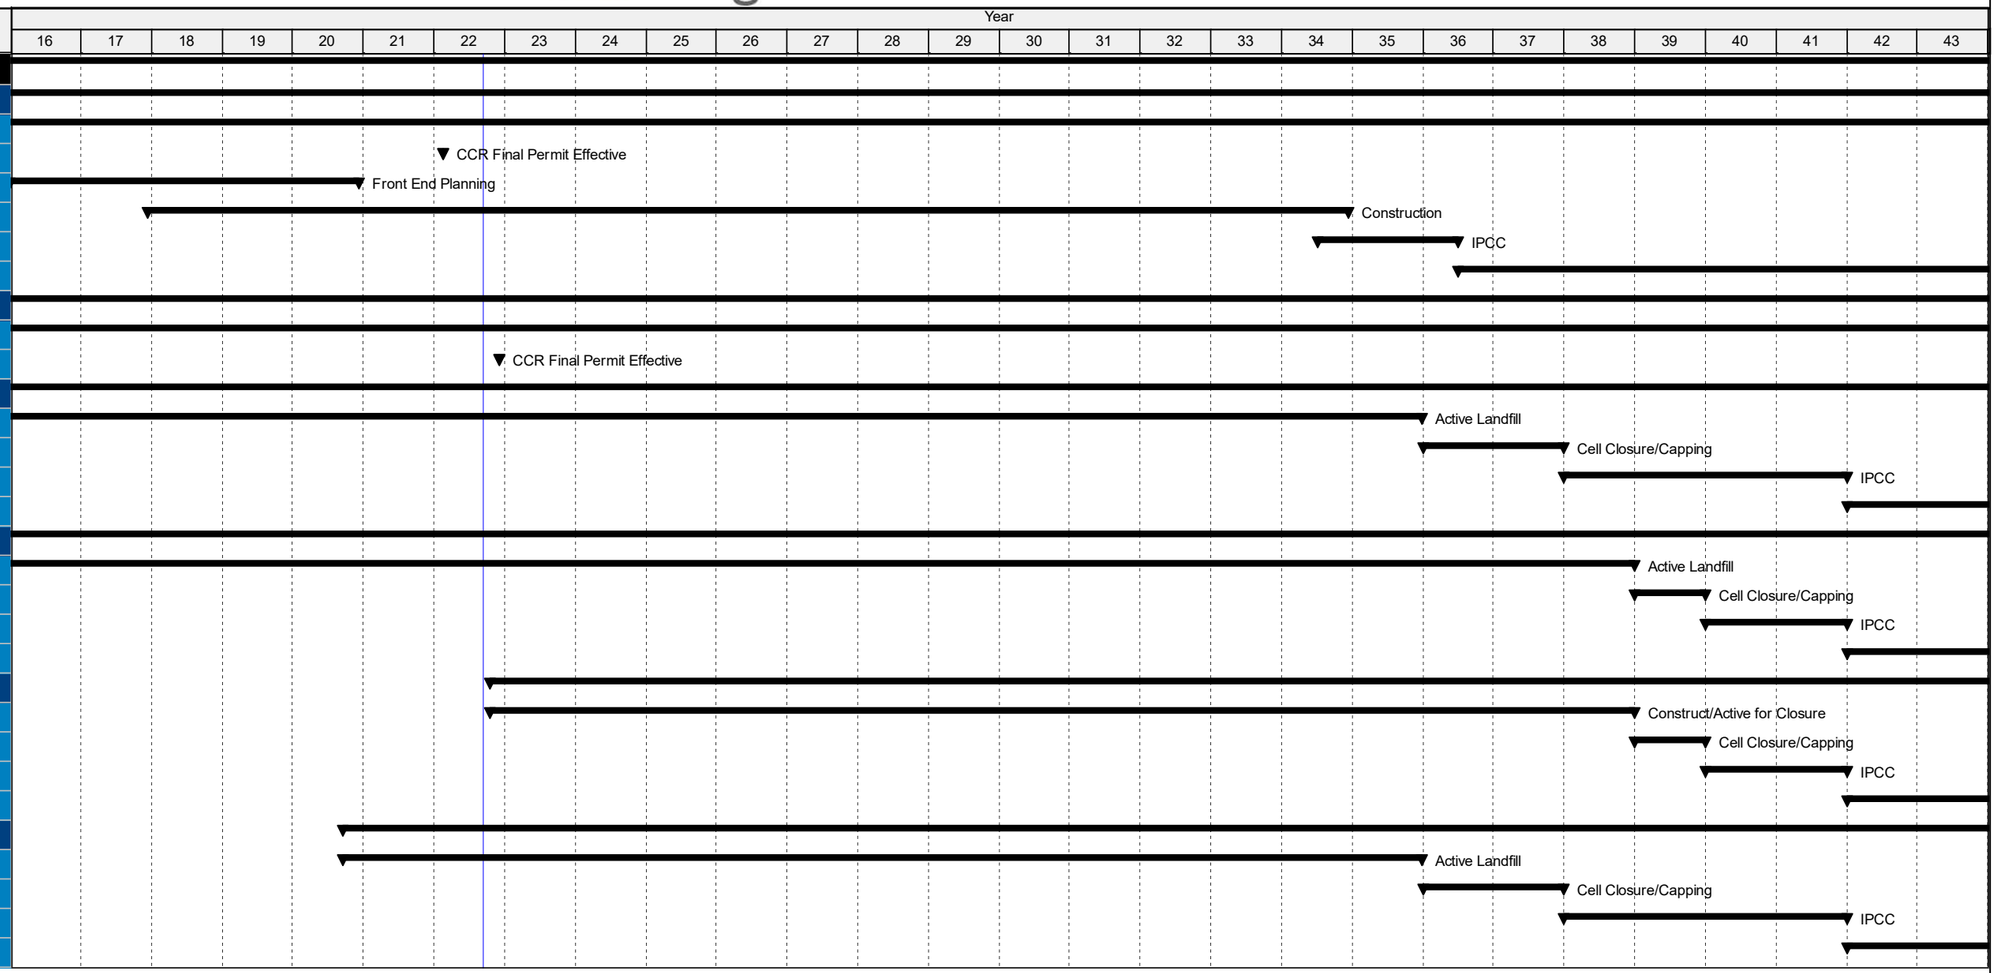

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.


Georgia Power

Activity ID	Start	Finish
Branch CCR	19-Oct-15 A	16-Aug-69
AP-B/AP-C/AP-D	19-Oct-15 A	11-Jun-43
Site Regulatory	19-Oct-15 A	11-Jun-43
Front End Planning	01-Jan-16 A	15-May-24
Construction	01-Mar-19 A	20-Oct-36
IPCC	09-Jun-36	10-Jun-38
PCC	11-Jun-38	11-Jun-43
AP-E	19-Oct-15 A	31-Dec-41
Site Regulatory	19-Oct-15 A	31-Dec-41
Front End Planning	01-Jan-16 A	15-May-24
Construction	01-Mar-19 A	27-Oct-36
IPCC	27-Dec-34	30-Dec-36
PCC	31-Dec-36	31-Dec-41
Branch LF	01-Jan-16 A	16-Aug-69
Site Regulatory	28-Feb-17 A	16-Aug-69
CCR Final Permit Effective	25-Jan-23	25-Jan-23
Front End Planning	01-Jan-16 A	22-Jul-25
Construct/Active/Close&Cap	27-Feb-23	14-Aug-37
IPCC	17-Aug-37	16-Aug-39
PCC	17-Aug-39	16-Aug-69

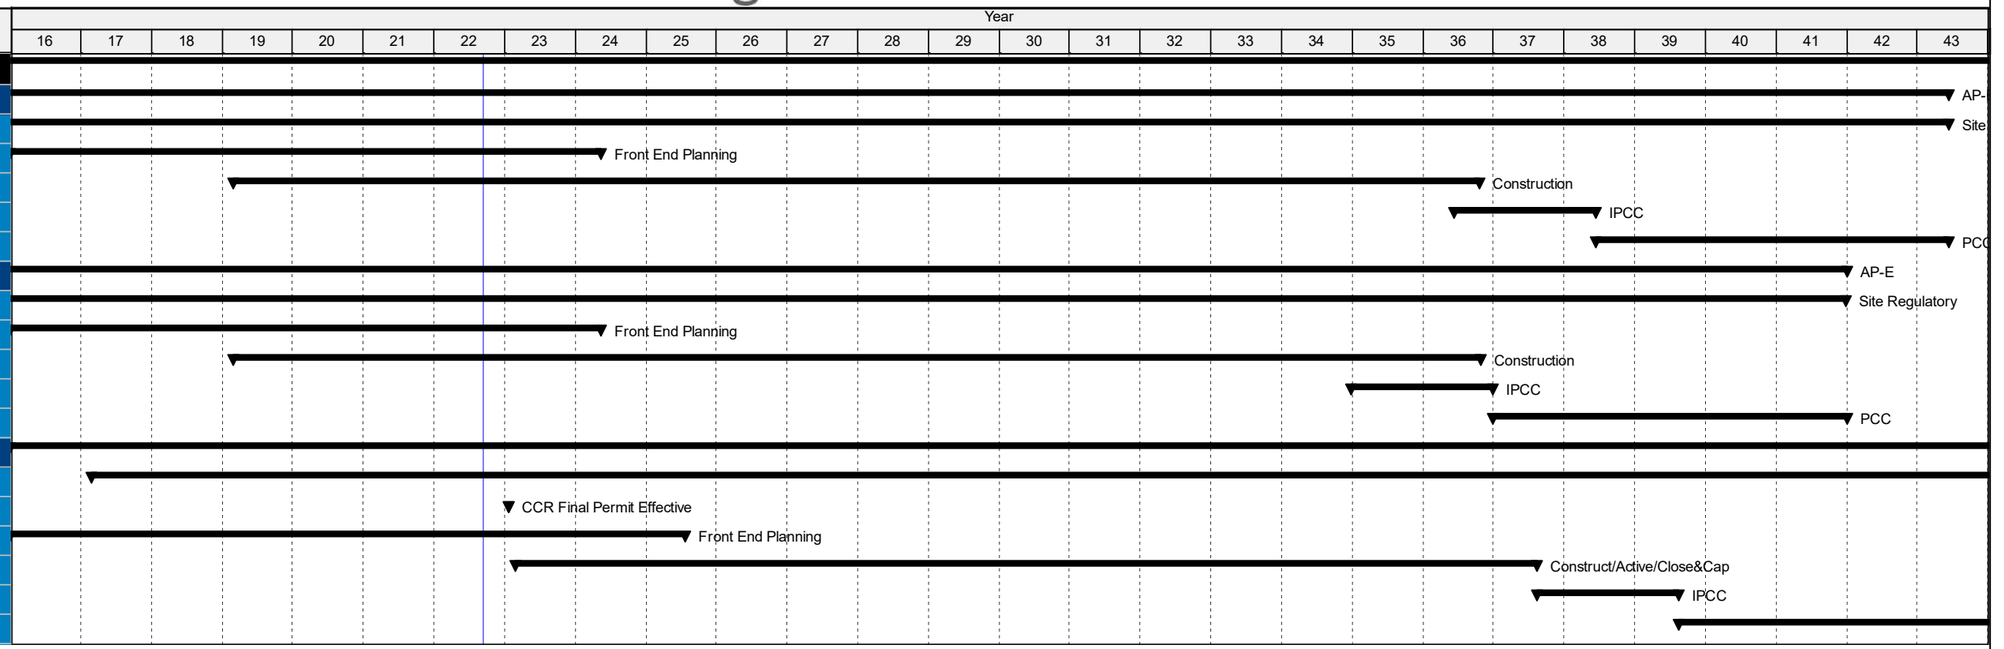

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.


Activity ID	Start	Finish
Hammond CCR	01-Jan-08 A	30-Sep-64
AP-1	19-Oct-15 A	01-Jun-31
Site Regulatory	19-Oct-15 A	01-Jun-31
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	11-Jan-21 A	10-Apr-25
IPCC	03-Jun-24	01-Jun-26
PCC	01-Jun-26	01-Jun-31
AP-2	19-Oct-15 A	16-Sep-30
Site Regulatory	19-Oct-15 A	16-Sep-30
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	04-Jan-21 A	09-Feb-24
IPCC	17-Sep-23	16-Sep-25
PCC	16-Sep-25	16-Sep-30
AP-3	19-Oct-15 A	09-Oct-54
Site Regulatory	19-Oct-15 A	09-Oct-54
CCR Draft Permit	12-Jul-21 A	12-Jul-21 A
Front End Planning	01-Jan-16 A	25-May-16 A
Construction	26-May-16 A	20-Jan-25
IPCC	13-Nov-18 A	08-Oct-24
PCC	09-Oct-24	08-Oct-54
AP-4	19-Oct-15 A	21-Mar-39
Site Regulatory	19-Oct-15 A	21-Mar-39
CCR Final Permit Effective	27-Jan-21 A	27-Jan-21 A
Front End Planning	19-Oct-15 A	28-Sep-26
Construction	11-Jan-21 A	23-Mar-32
IPCC	22-Mar-32	21-Mar-34
PCC	22-Mar-34	21-Mar-39
Huffaker Rd LF	01-Jan-08 A	30-Sep-64
Site Regulatory	01-Jan-08 A	30-Sep-64
Huffaker Rd A/B	01-Jan-08 A	30-Sep-64
Active Landfill	01-Jan-08 A	03-Jan-26
Cell Closure/Capping	03-Apr-24	24-Nov-26
IPCC	02-Jan-26	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell E	01-Jan-08 A	30-Sep-64
Active Landfill	01-Jan-08 A	21-Jan-32
Cell/Closure Capping	21-Jan-32	28-Sep-32
IPCC	28-Sep-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell F	01-Jan-16 A	30-Sep-64
Front End Planning	01-Jan-16 A	03-Apr-25
Construct/Active/Close&Cap	30-Apr-25	01-Sep-32
IPCC	01-Sep-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64

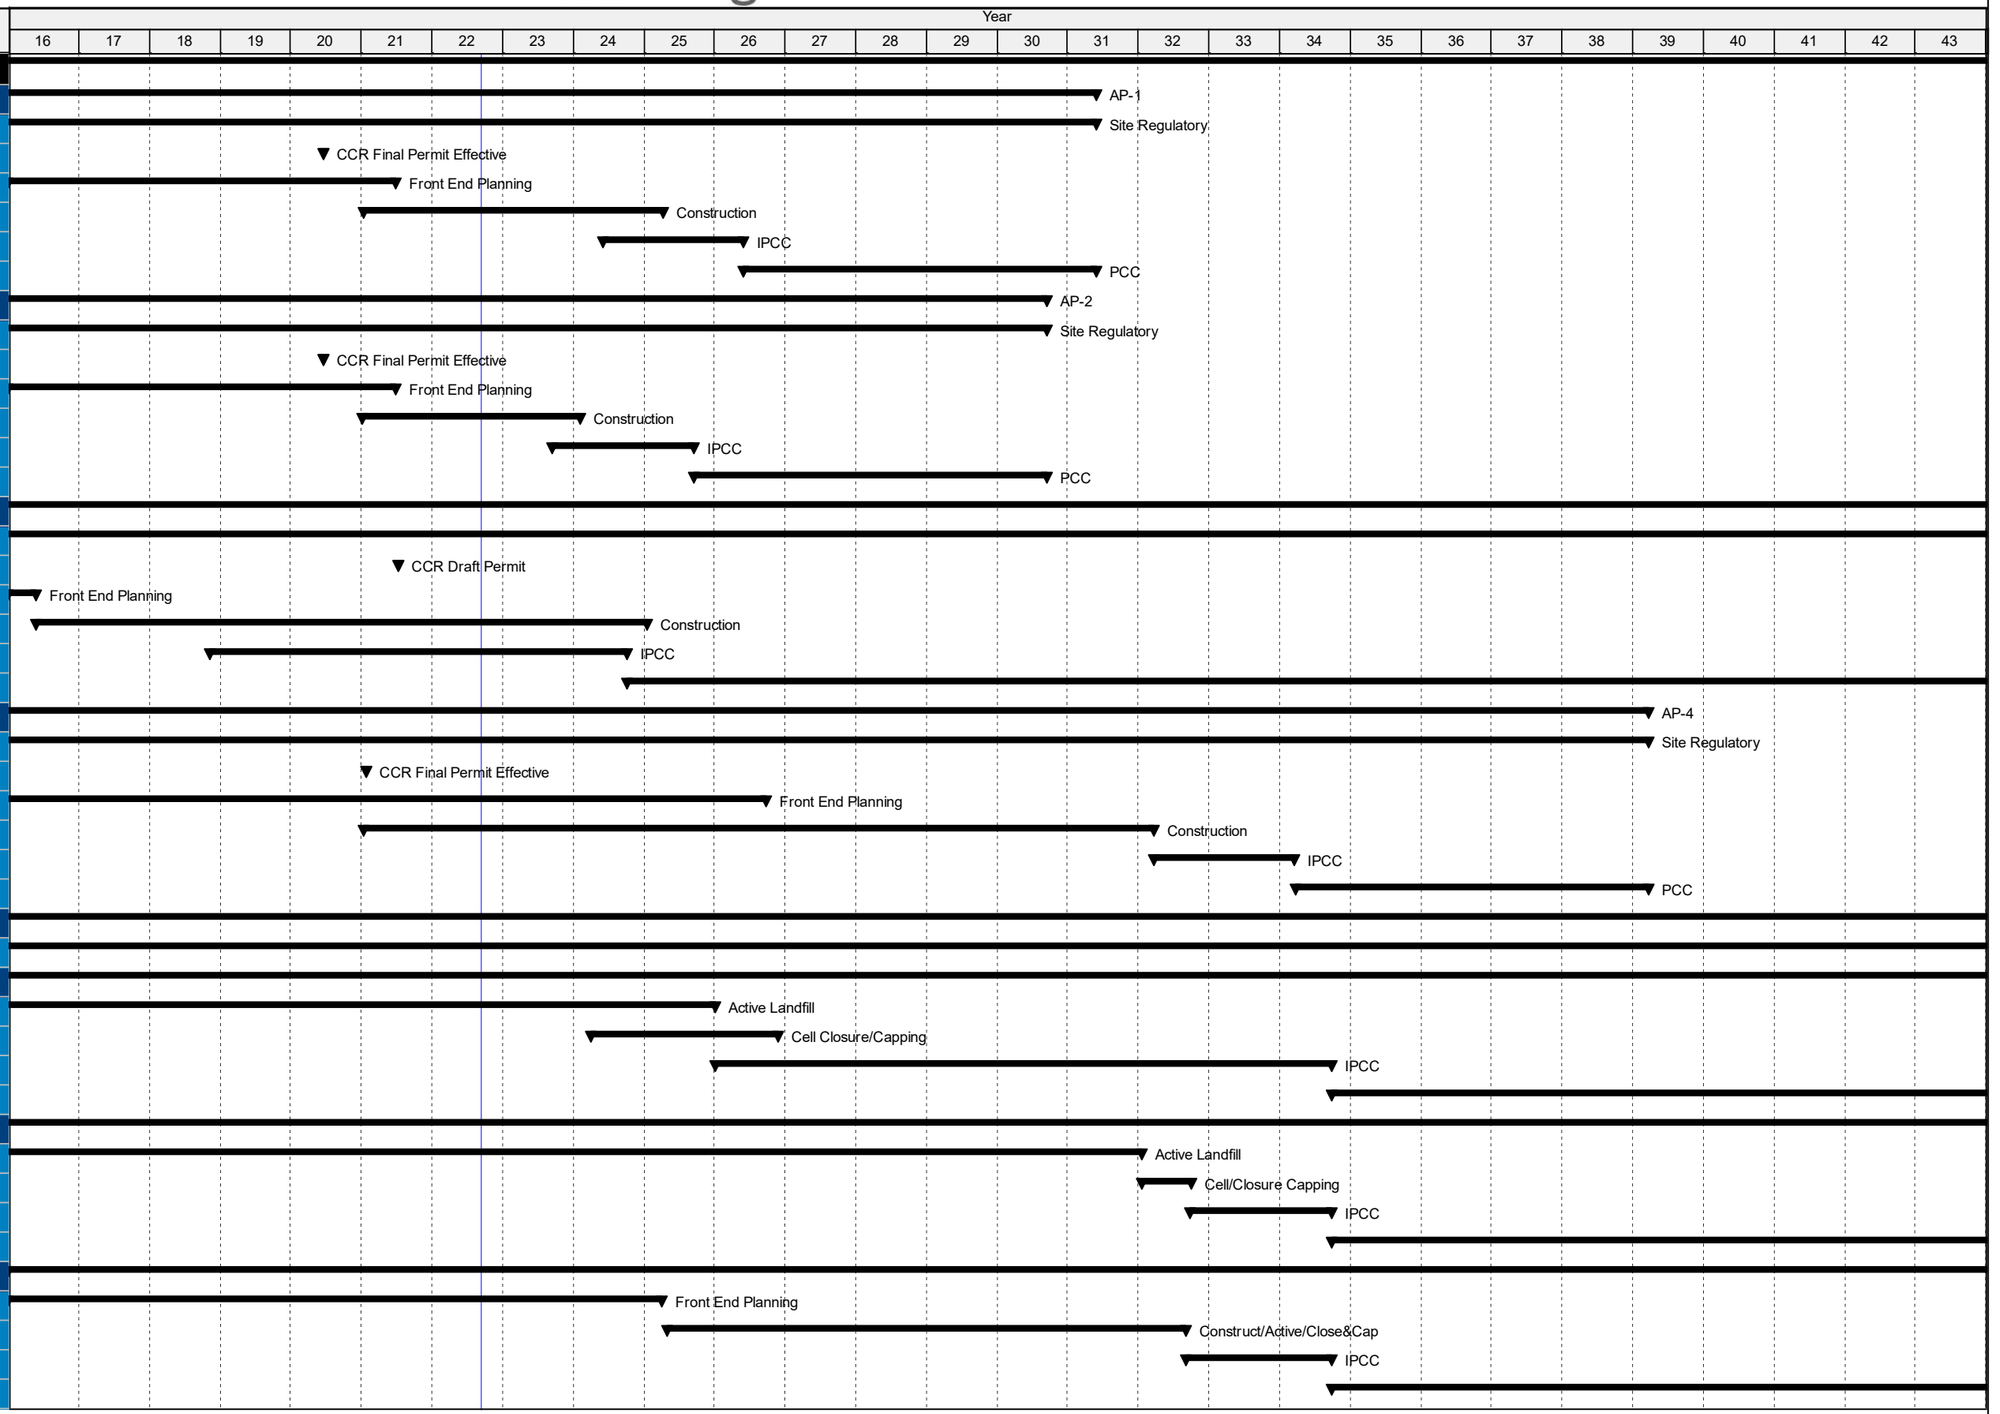

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.

Georgia Power


Activity ID	Start	Finish
Kraft CCR	19-Oct-15 A	06-Jun-53
Grumman Rd.	19-Oct-15 A	06-Jun-53
Site Regulatory	19-Oct-15 A	06-Jun-53
Front End Planning	05-Nov-15 A	04-Jan-19 A
Construction	27-Feb-17 A	30-Oct-20 A
IPCC	03-Jan-20 A	07-Jun-23
PCC	07-Jun-23	06-Jun-53

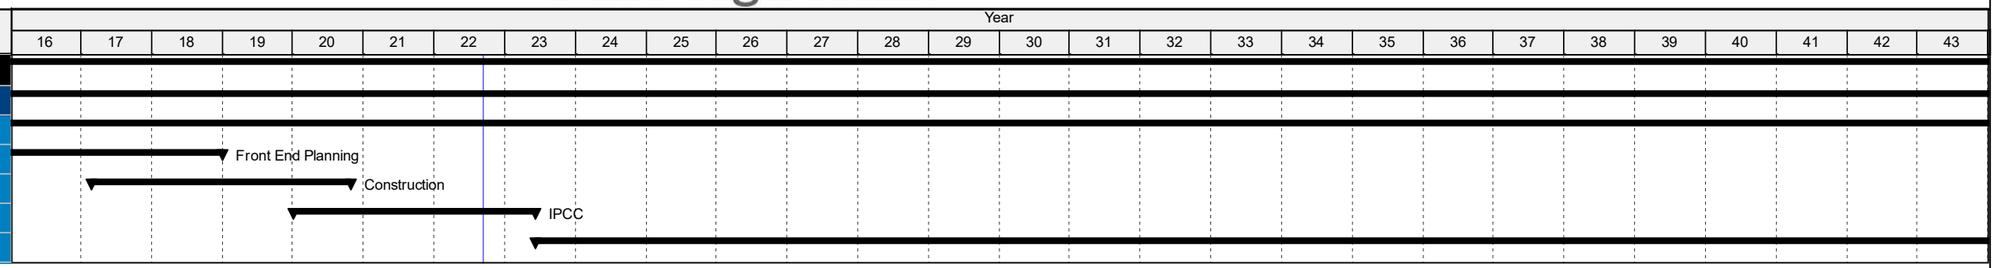

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.


Georgia Power

Activity ID	Start	Finish
McDonough CCR	19-Oct-15 A	01-Dec-56
AP-1	19-Oct-15 A	01-Dec-56
Site Regulatory	19-Oct-15 A	01-Dec-56
Front End Planning	01-Jan-16 A	12-Nov-21 A
Construction	18-Jan-16 A	29-Nov-24
IPCC	29-Nov-24	29-Nov-26
PCC	30-Nov-26	30-Nov-56
AP-2/AP-3/AP-4	19-Oct-15 A	30-Nov-54
Site Regulatory	19-Oct-15 A	30-Nov-54
Front End Planning	01-Jan-16 A	12-Feb-16 A
Construction	19-Jan-16 A	27-Dec-22
IPCC	30-Nov-22	28-Nov-24
PCC AP-2	29-Nov-24	30-Nov-29
PCC AP-3/AP-4	29-Nov-24	29-Nov-54

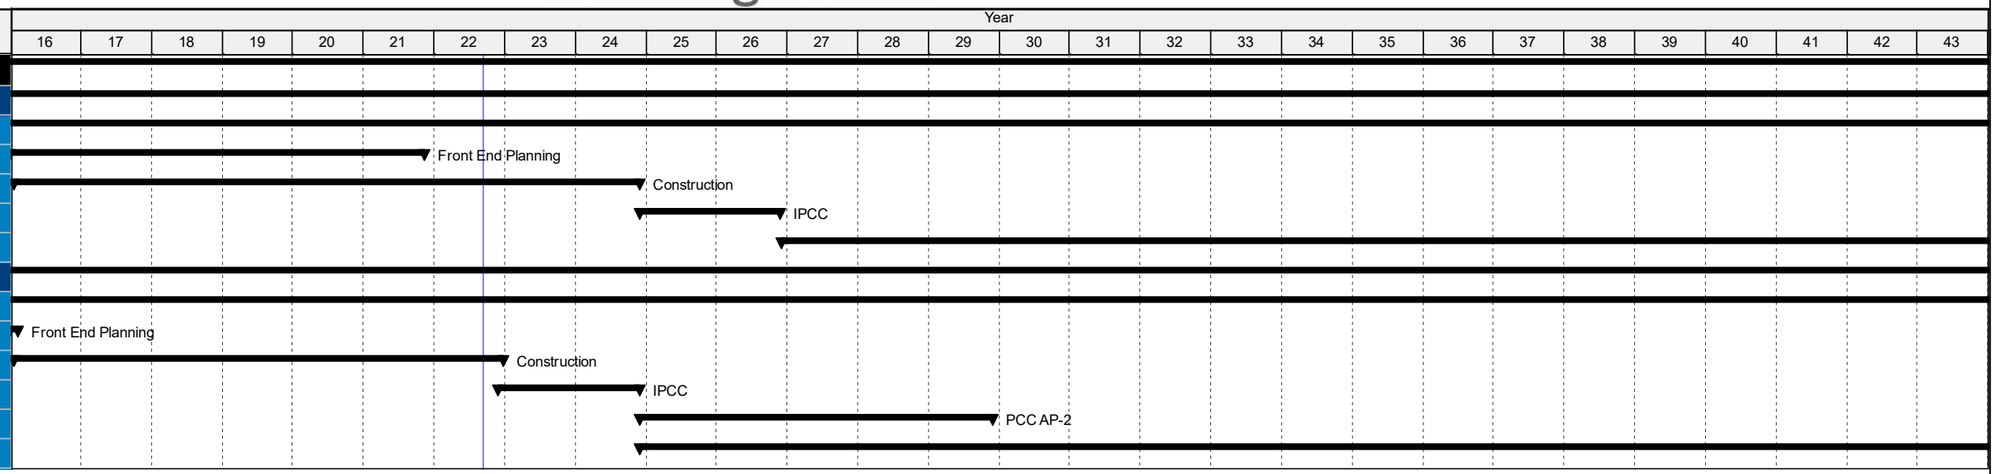

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.


Activity ID	Start	Finish
McIntosh CCR	12-Mar-08 A	23-Oct-54
AP-1	19-Oct-15 A	06-Oct-26
Site Regulatory	19-Oct-15 A	06-Oct-26
CCR Final Permit Effective	06-Feb-20 A	06-Feb-20 A
Front End Planning	01-Jan-16 A	06-Feb-20 A
Construction	01-Oct-19 A	06-Jul-22 A
IPCC	08-Sep-21 A	05-Oct-21 A
PCC	06-Oct-21 A	06-Oct-26
LF3	12-Mar-08 A	12-Mar-38
Site Regulatory	12-Mar-08 A	12-Mar-38
CCR Draft Permit	31-Jan-23	31-Jan-23
PCC	12-Mar-08 A	12-Mar-38
LF4	19-Oct-15 A	23-Oct-54
Site Regulatory	19-Oct-15 A	23-Oct-54
CCR Draft Permit	24-Feb-23	24-Feb-23
LF4 Cell 1	27-Nov-18 A	23-Oct-54
IPCC	27-Nov-18 A	22-Oct-24
PCC	22-Oct-24	23-Oct-54
LF4 Cell 2A	04-May-20 A	23-Oct-54
Construct/Active/Close&Cap	04-May-20 A	20-Oct-22
IPCC	22-Oct-22	22-Oct-24
PCC	22-Oct-24	23-Oct-54

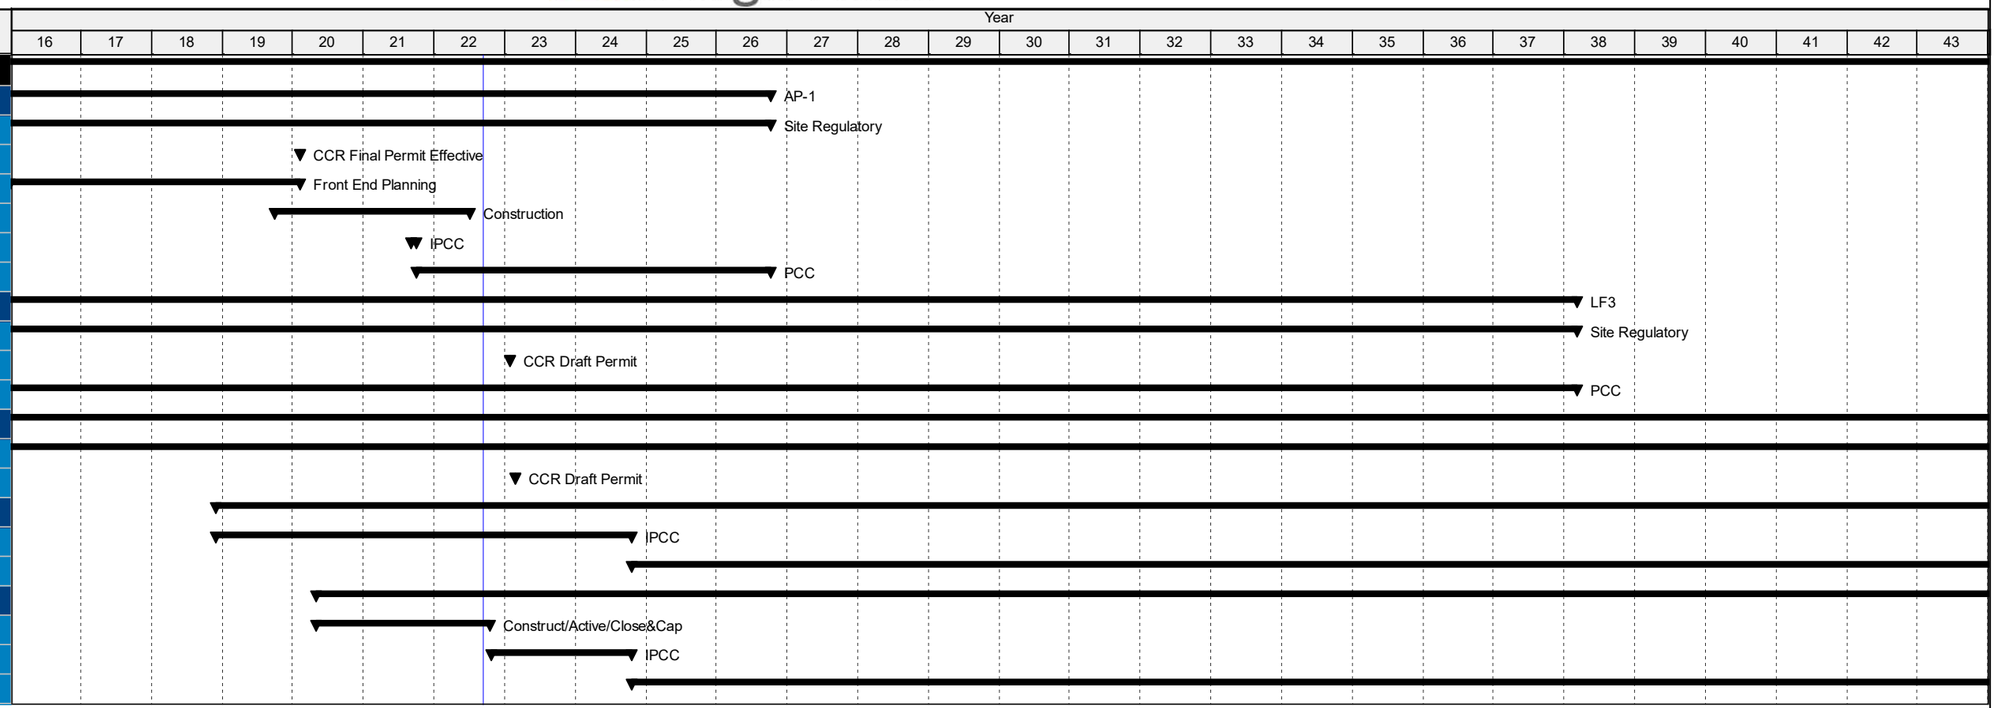

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.
The actual finish date for the CCR Draft Permit for McIntosh CCR LF3 is 31JAN23. The actual finish date for the CCR Draft Permit for McIntosh CCR LF4 is 03MAR23.

Georgia Power


Activity ID	Start	Finish
McManus CCR	19-Oct-15 A	21-Jul-36
McManus AP-1	19-Oct-15 A	21-Jul-36
Site Regulatory	19-Oct-15 A	21-Jul-36
CCR Final Permit Effective	18-Jun-21 A	18-Jun-21 A
Front End Planning	01-Jan-16 A	08-Dec-16 A
Construction	22-Jan-16 A	28-Jul-20 A
IPCC	25-Nov-19 A	20-Jul-21 A
PCC	20-Jul-21 A	21-Jul-36

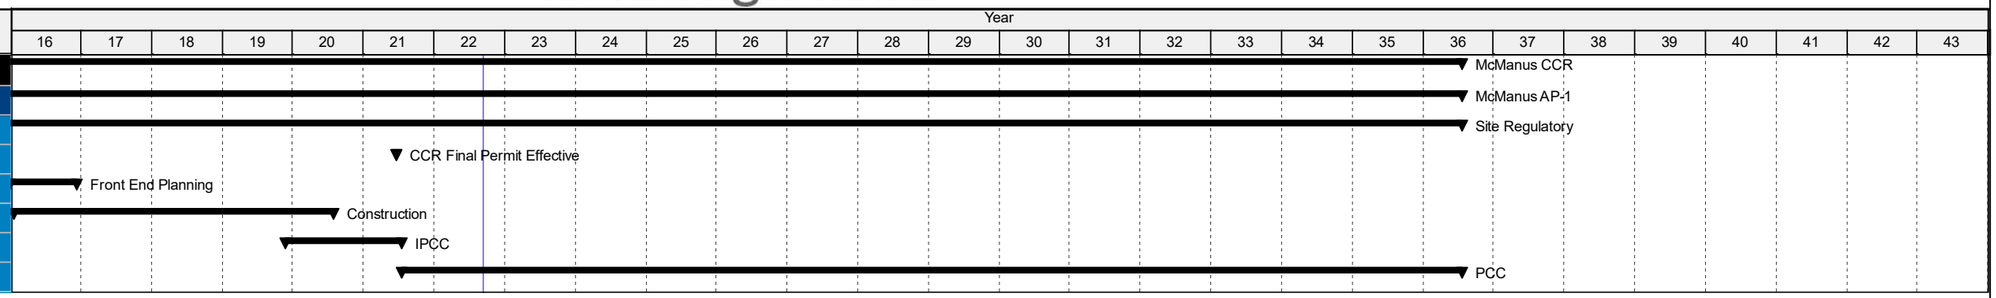

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.

Georgia Power


Activity ID	Start	Finish
Mitchell CCR	19-Oct-15 A	29-Sep-37
Mitchell AP-1/AP-2/AP-A	19-Oct-15 A	29-Sep-37
Site Regulatory	19-Oct-15 A	29-Sep-37
CCR Final Permit Effective	28-Jun-22 A	28-Jun-22 A
Front End Planning	01-Jan-16 A	19-Feb-21 A
Construction	17-Sep-19 A	27-Sep-30
IPCC	30-Sep-30	30-Sep-32
PCC	30-Sep-32	29-Sep-37

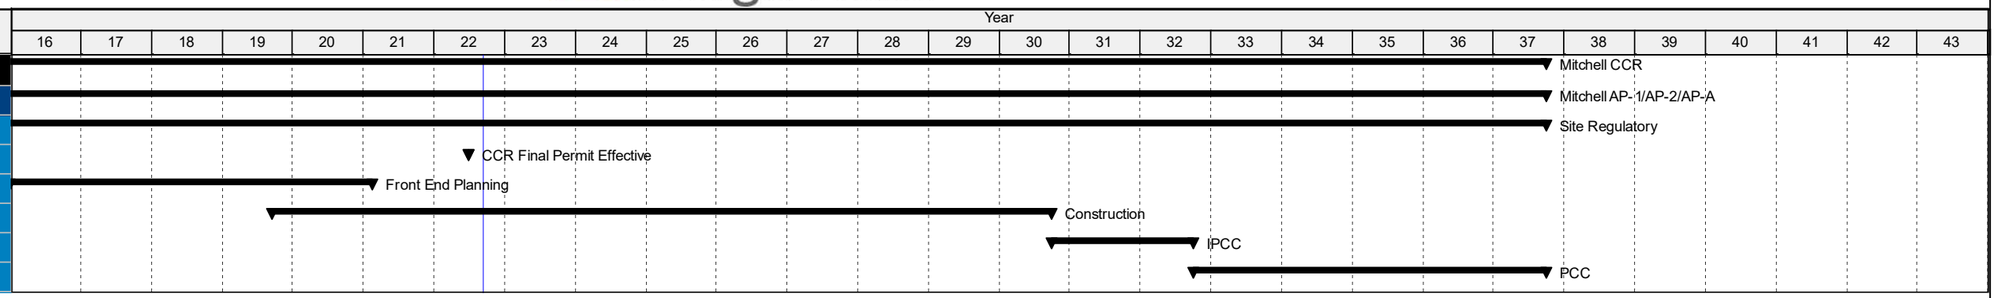

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.

Georgia Power


Activity ID	Start	Finish
Scherer CCR	01-Jan-10 A	01-Jan-79
Scherer AP-1	19-Oct-15 A	27-Oct-64
Site Regulatory	19-Oct-15 A	27-Oct-64
Front End Planning	01-Jan-16 A	22-Jan-27
Construction	06-Jul-21 A	01-Nov-32
IPCC	26-Oct-32	26-Oct-34
PCC	26-Oct-34	26-Oct-64
Scherer LF	01-Jan-10	01-Jan-79
Site Regulatory	01-Jan-10	01-Jan-79
LF Cell 1	01-Jan-10 A	01-Jan-79
Active Landfill	01-Jan-10 A	02-Jan-45
Cell Closure/Capping	02-Jan-45	31-Dec-46
IPCC	01-Jan-47	31-Dec-48
PCC	01-Jan-49	01-Jan-79
PAC/ASH CELL	01-Jan-11 A	01-Jan-79
Active Landfill	01-Jan-11 A	01-Jan-27
Cell Closure/Capping	01-Jan-27	31-Dec-28
IPCC	01-Jan-29	31-Dec-48
PCC	01-Jan-49	01-Jan-79

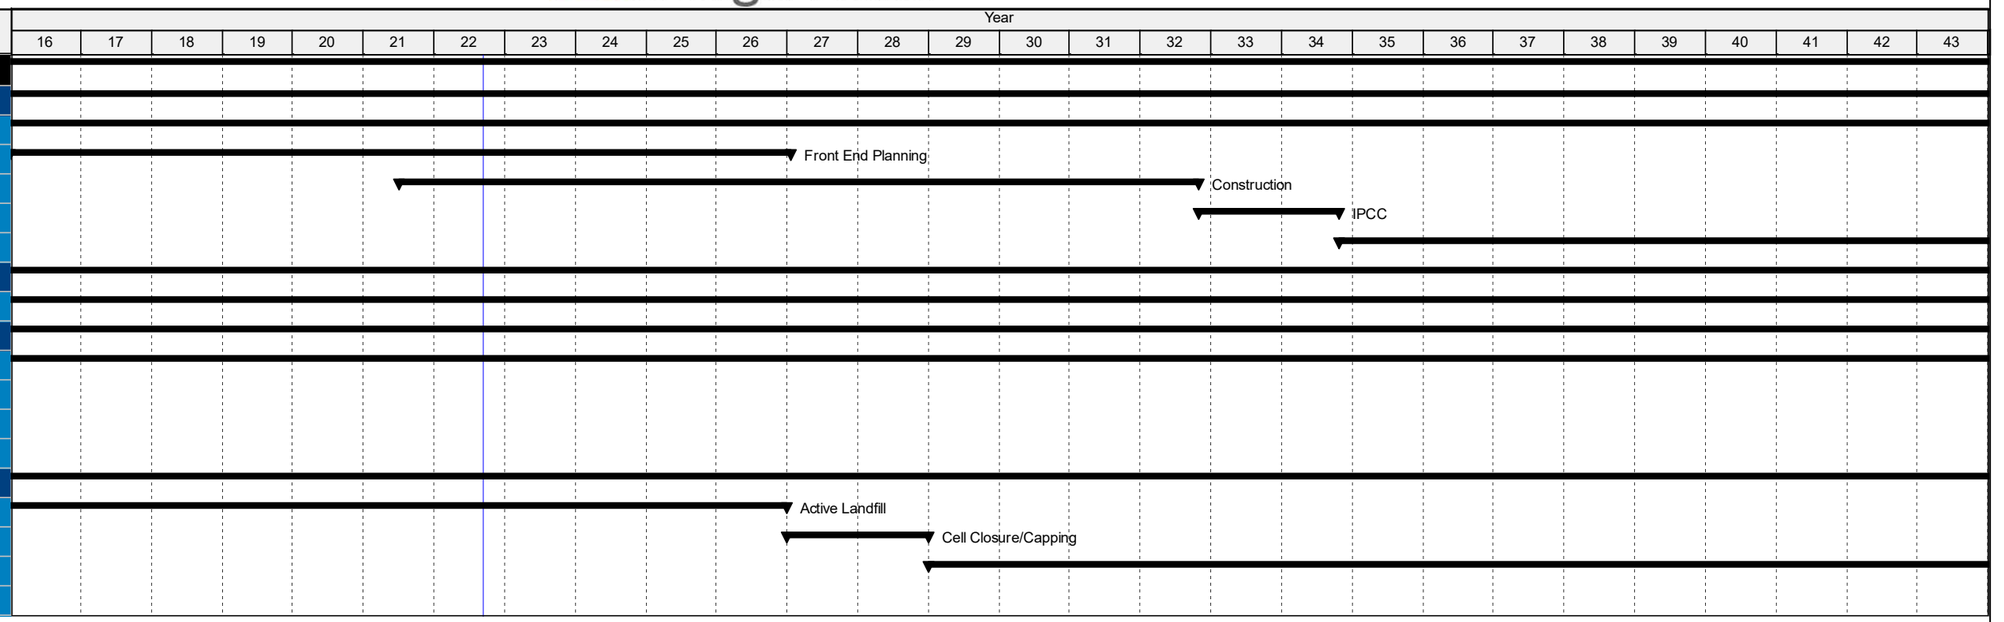

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.

Georgia Power


Activity ID	Start	Finish
Wansley CCR	01-Jan-12 A	08-May-65
Wansley AP-1	19-Oct-15 A	07-Nov-39
Site Regulatory	19-Oct-15 A	07-Nov-39
Front End Planning	01-Jan-16 A	08-Apr-25
Construction	19-Apr-21 A	02-Nov-32
IPCC	03-Nov-32	03-Nov-34
PCC	06-Nov-34	04-Nov-39
Wansley Landfill	01-Jan-12 A	08-May-65
Site Regulatory	01-Jan-12 A	08-May-65
Landfill Cells 1&2	01-Jan-12 A	08-May-65
Active for Closure	01-Jan-12 A	15-May-30
Cell Closure/Capping	16-May-30	07-May-33
IPCC	08-May-33	07-May-35
PCC	08-May-35	08-May-65
Landfill Cell 3	28-Jun-19 A	08-May-65
Active for Closure	28-Jun-19 A	15-May-30
Cell Closure/Capping	16-May-30	07-May-33
IPCC	08-May-33	07-May-35
PCC	08-May-35	08-May-65
Landfill Cell 4	22-Jul-22 A	08-May-65
Front End Planning	22-Jul-22 A	09-Sep-25
Construct/Active for Closure	02-Nov-23	15-May-30
Cell Closure/Capping	16-May-30	06-May-33
IPCC	08-May-33	07-May-35
PCC	08-May-35	08-May-65

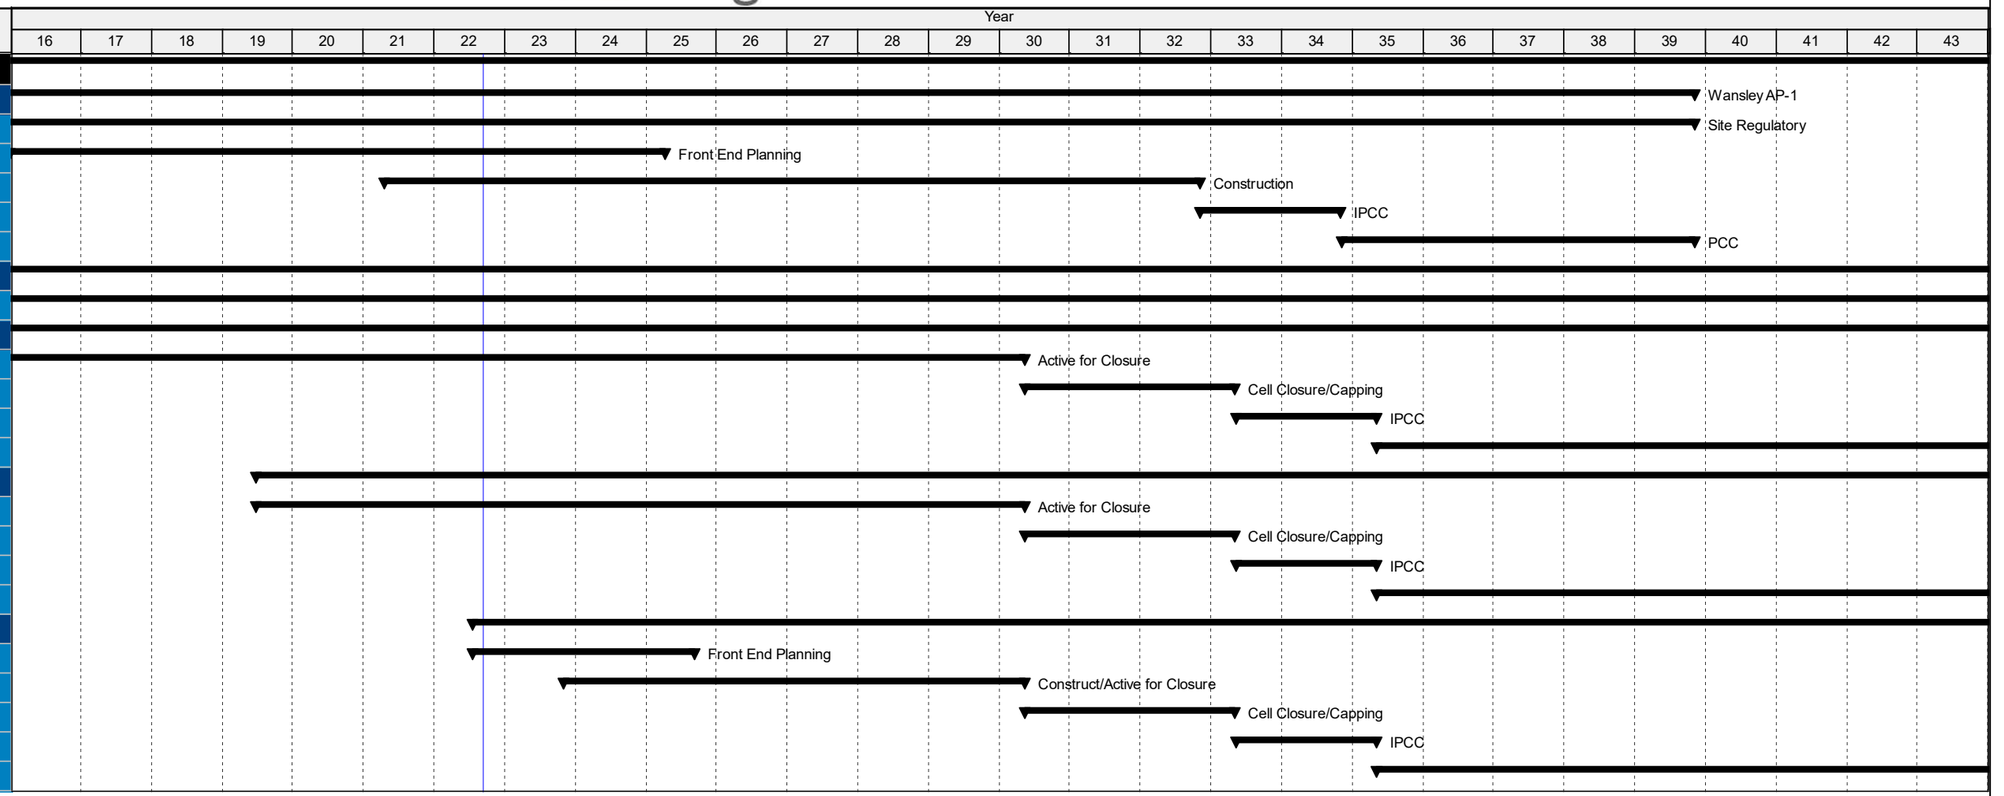

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.

Georgia Power

Activity ID	Start	Finish
Yates CCR	04-May-15 A	02-Jul-55
Yates AP-1	04-May-15 A	01-Feb-27
Site Regulatory	19-Oct-15 A	01-Feb-27
CCR Final Permit Effective	06-Jan-22 A	06-Jan-22 A
Front End Planning	04-May-15 A	21-Jul-16 A
Construction	04-May-15 A	31-Dec-21 A
IPCC	27-Nov-19 A	31-Jan-22 A
PCC	31-Jan-22 A	01-Feb-27
Yates AP-2	19-Oct-15 A	30-Nov-29
Site Regulatory	19-Oct-15 A	30-Nov-29
Front End Planning	01-Jan-16 A	20-Nov-19 A
Construction	05-Sep-19 A	09-May-23
IPCC	01-Dec-22	29-Nov-24
PCC	02-Dec-24	29-Nov-29
Yates AP-3/AP-B/AP-B'/AP-A	19-Oct-15 A	02-Jul-55
Site Regulatory	19-Oct-15 A	02-Jul-55
Front End Planning	01-Jan-16 A	30-Apr-18 A
Construction	19-Aug-16 A	01-Jul-23
IPCC	03-Jul-23	02-Jul-25
PCC	02-Jul-25	02-Jul-55
Yates Gypsum Landfill	22-Jul-15 A	02-Feb-27
Site Regulatory	22-Jul-15 A	02-Feb-27
CCR Final Permit Effective	05-Jan-22 A	05-Jan-22 A
IPCC	19-Jan-17 A	02-Feb-22 A
PCC	02-Feb-22 A	02-Feb-27
Yates R-6/AP-C	29-May-15 A	27-Mar-55
Site Regulatory	29-May-15 A	26-Mar-55
Front End Planning	29-May-15 A	21-Jul-16 A
Construction	29-May-15 A	26-Mar-23
IPCC	27-Mar-23	26-Mar-25
PCC	26-Mar-25	27-Mar-55

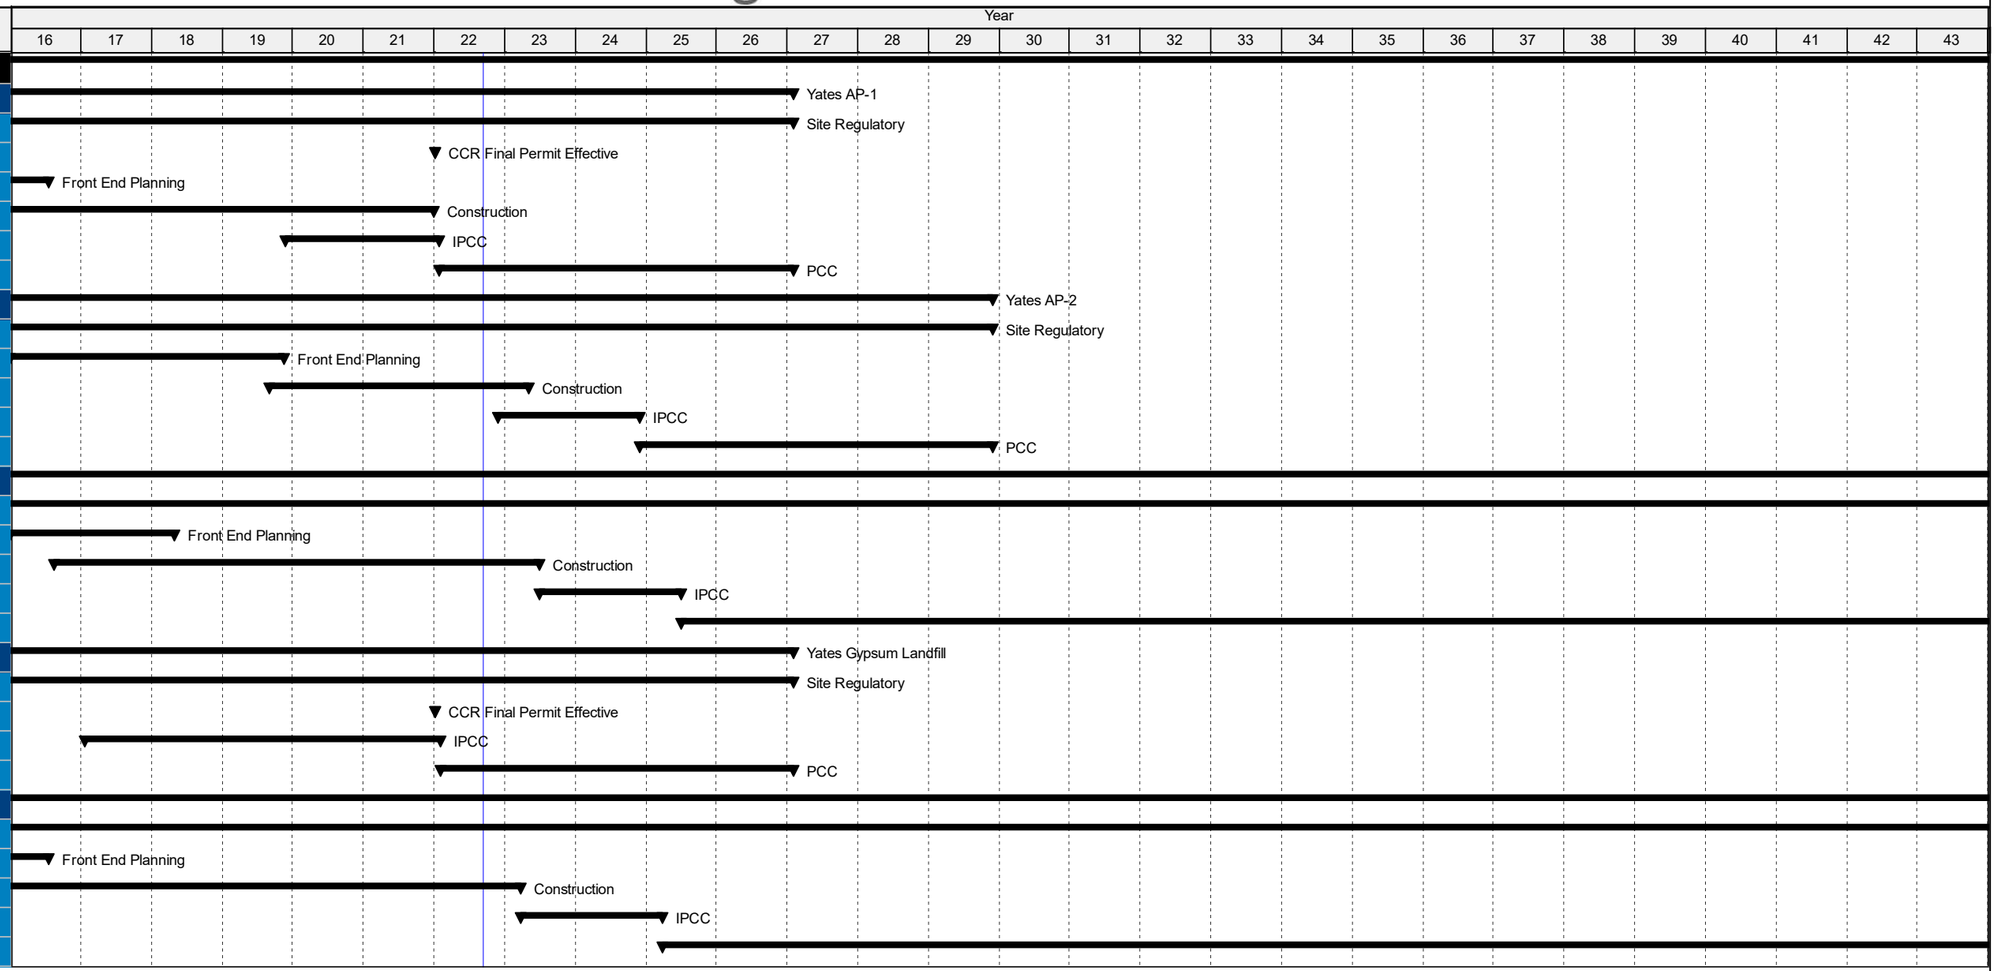

Note: This schedule forecast reflects the set of dates used as the cost forecast basis for the 1Q23 semi-annual update and as such current forecast activity dates may differ from what is reflected for future forecast activities.
