

Activity ID	Start	Finish
Arkwright CCR	19-Oct-15 A	05-Feb-63
AP-1	19-Oct-15 A	29-Jul-37
Site Regulatory	19-Oct-15 A	29-Jul-37
Front End Planning	01-Jan-16 A	27-Jun-25
Construction	21-Aug-23	23-Apr-31
IPCC	28-Jul-30	28-Jul-32
PCC	28-Jul-32	29-Jul-37
AP-2 DAS	19-Oct-15 A	19-Nov-35
Site Regulatory	19-Oct-15 A	19-Nov-35
Front End Planning	01-Jan-16 A	14-Jul-25
Construction	21-Aug-23	23-Apr-31
IPCC	14-Nov-28	16-Nov-30
PCC	16-Nov-30	17-Nov-35
CCRLF/AP-3/Monofill	01-Jan-16 A	05-Feb-63
Site Regulatory	20-Nov-18 A	05-Feb-63
Front End Planning	01-Jan-16 A	14-Jul-25
Construct/Active/Close&Cap	11-Aug-25	23-Apr-31
IPCC	03-Feb-31	04-Feb-33
PCC	04-Feb-33	05-Feb-63

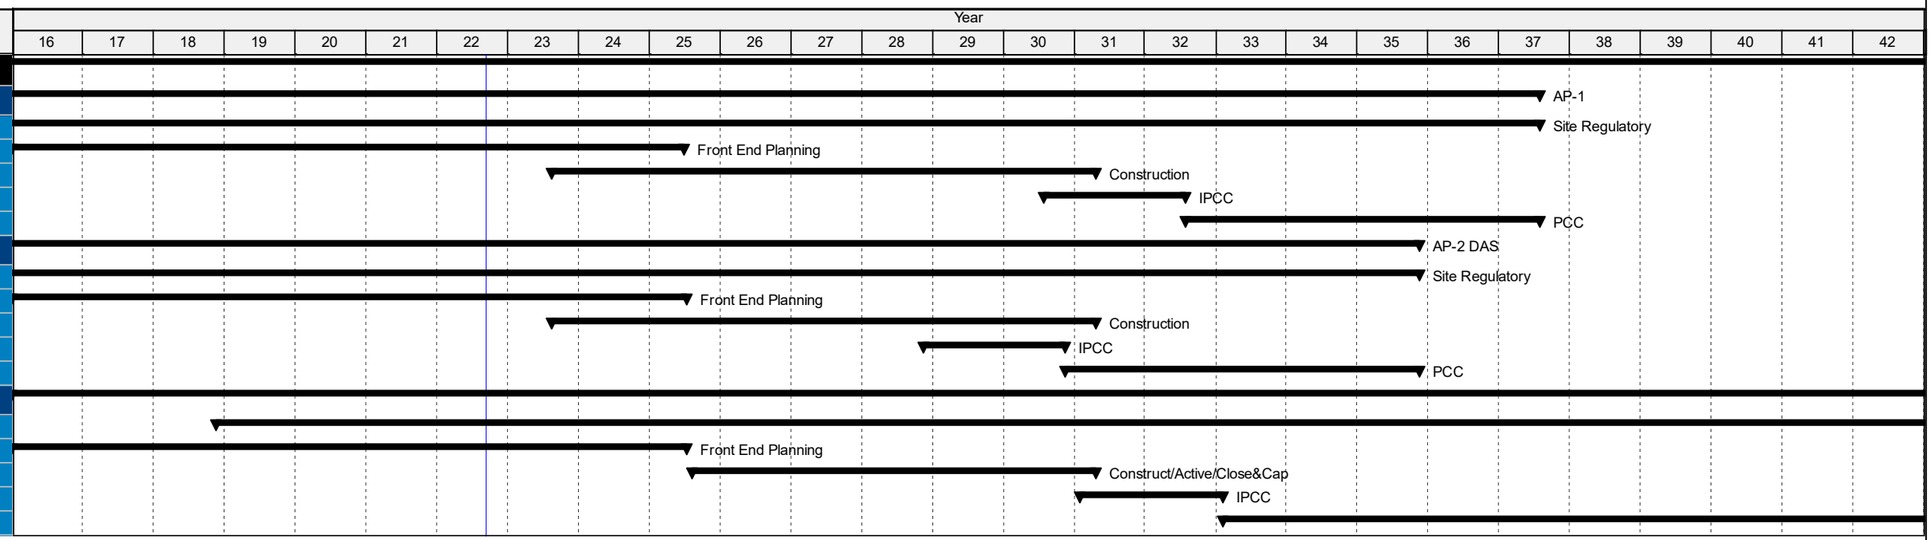


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Bowen CCR	12-May-08 A	01-Jan-72
AP-1	19-Oct-15 A	07-Jul-66
Site Regulatory	19-Oct-15 A	07-Jul-66
CCR Final Permit Effective	17-Feb-22 A	17-Feb-22 A
Front End Planning	01-Jan-16 A	08-Dec-20 A
Construction	14-Dec-17 A	15-Dec-34
IPCC	06-Jul-34	04-Jul-36
PCC	04-Jul-36	06-Jul-66
Bowen Landfill	12-May-08 A	01-Jan-72
Site Regulatory	12-May-08 A	01-Jan-72
CCR Final Permit Effective	08-Dec-22	08-Dec-22
LF Cells 1&2	12-May-08 A	01-Jan-72
Active Landfill	12-May-08 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 3&4	01-Jan-14 A	01-Jan-72
Active Landfill	01-Jan-14 A	31-Dec-38
Cell Closure/Capping	01-Jan-39	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 5&6	17-Oct-22	01-Jan-72
Construct/Active for Closure	17-Oct-22	31-Dec-38
Cell Closure/Capping	01-Jan-39	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 9&10	18-Sep-20 A	01-Jan-72
Active Landfill	18-Sep-20 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72

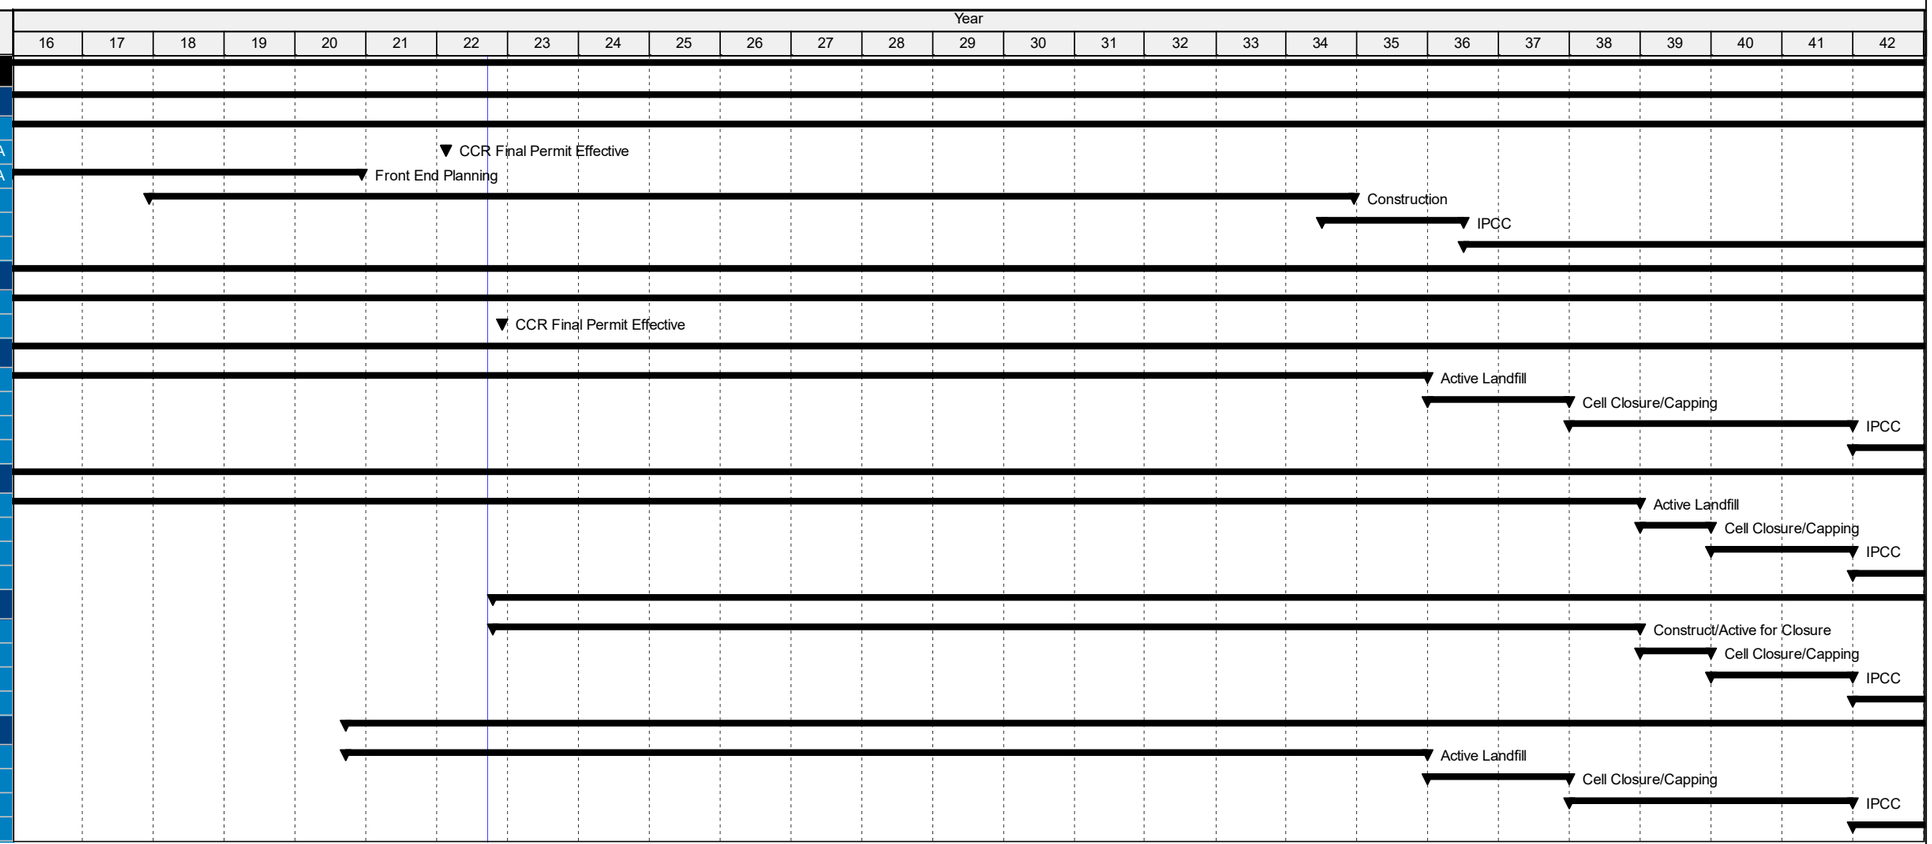


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Branch CCR	19-Oct-15 A	16-Aug-69
AP-B/AP-C/AP-D	19-Oct-15 A	11-Jun-43
Site Regulatory	19-Oct-15 A	11-Jun-43
Front End Planning	01-Jan-16 A	15-May-24
Construction	01-Mar-19 A	20-Oct-36
IPCC	09-Jun-36	10-Jun-38
PCC	11-Jun-38	11-Jun-43
AP-E	19-Oct-15 A	31-Dec-41
Site Regulatory	19-Oct-15 A	31-Dec-41
Front End Planning	01-Jan-16 A	15-May-24
Construction	01-Mar-19 A	27-Oct-36
IPCC	27-Dec-34	30-Dec-36
PCC	31-Dec-36	31-Dec-41
Branch LF	01-Jan-16 A	16-Aug-69
Site Regulatory	28-Feb-17 A	16-Aug-69
CCR Final Permit Effective	25-Jan-23	25-Jan-23
Front End Planning	01-Jan-16 A	22-Jul-25
Construct/Active/Close&Cap	27-Feb-23	14-Aug-37
IPCC	17-Aug-37	16-Aug-39
PCC	17-Aug-39	16-Aug-69

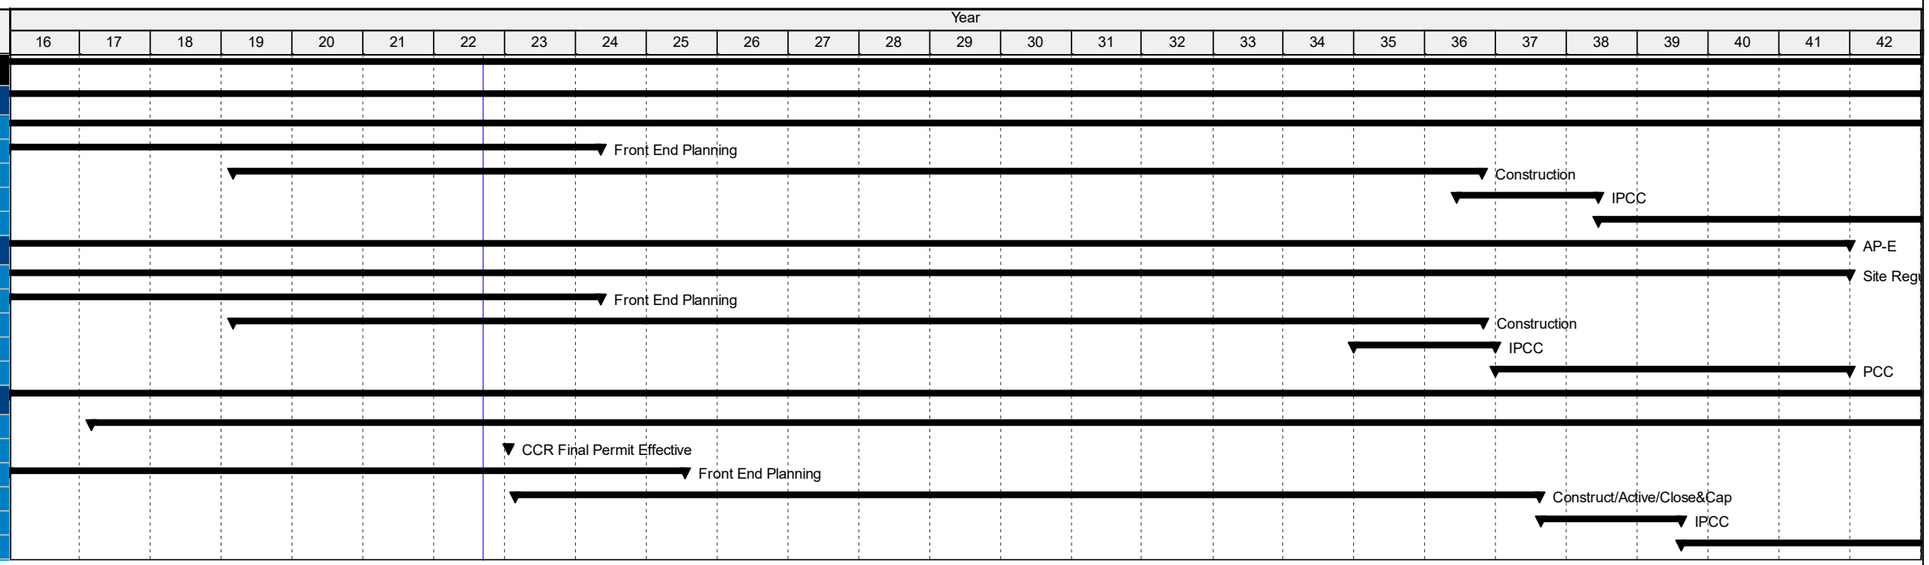


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Hammond CCR	01-Jan-08 A	30-Sep-64
AP-1	19-Oct-15 A	01-Jun-31
Site Regulatory	19-Oct-15 A	01-Jun-31
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	11-Jan-21 A	10-Apr-25
IPCC	03-Jun-24	01-Jun-26
PCC	01-Jun-26	01-Jun-31
AP-2	19-Oct-15 A	16-Sep-30
Site Regulatory	19-Oct-15 A	16-Sep-30
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	04-Jan-21 A	09-Feb-24
IPCC	17-Sep-23	16-Sep-25
PCC	16-Sep-25	16-Sep-30
AP-3	19-Oct-15 A	09-Oct-54
Site Regulatory	19-Oct-15 A	09-Oct-54
CCR Draft Permit	12-Jul-21 A	12-Jul-21 A
Front End Planning	01-Jan-16 A	25-May-16 A
Construction	26-May-16 A	20-Jan-25
IPCC	13-Nov-18 A	08-Oct-24
PCC	09-Oct-24	08-Oct-54
AP-4	19-Oct-15 A	21-Mar-39
Site Regulatory	19-Oct-15 A	21-Mar-39
CCR Final Permit Effective	27-Jan-21 A	27-Jan-21 A
Front End Planning	19-Oct-15 A	28-Sep-26
Construction	11-Jan-21 A	23-Mar-32
IPCC	22-Mar-32	21-Mar-34
PCC	22-Mar-34	21-Mar-39
Huffaker Rd LF	01-Jan-08 A	30-Sep-64
Site Regulatory	01-Jan-08 A	30-Sep-64
Huffaker Rd A/B	01-Jan-08 A	30-Sep-64
Active Landfill	01-Jan-08 A	03-Jan-26
Cell Closure/Capping	03-Apr-24	24-Nov-26
IPCC	02-Jan-26	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell E	01-Jan-08 A	30-Sep-64
Active Landfill	01-Jan-08 A	21-Jan-32
Cell/Closure Capping	21-Jan-32	28-Sep-32
IPCC	28-Sep-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell F	01-Jan-16 A	30-Sep-64
Front End Planning	01-Jan-16 A	03-Apr-25
Construct/Active/Close&Cap	30-Apr-25	01-Sep-32
IPCC	01-Sep-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64

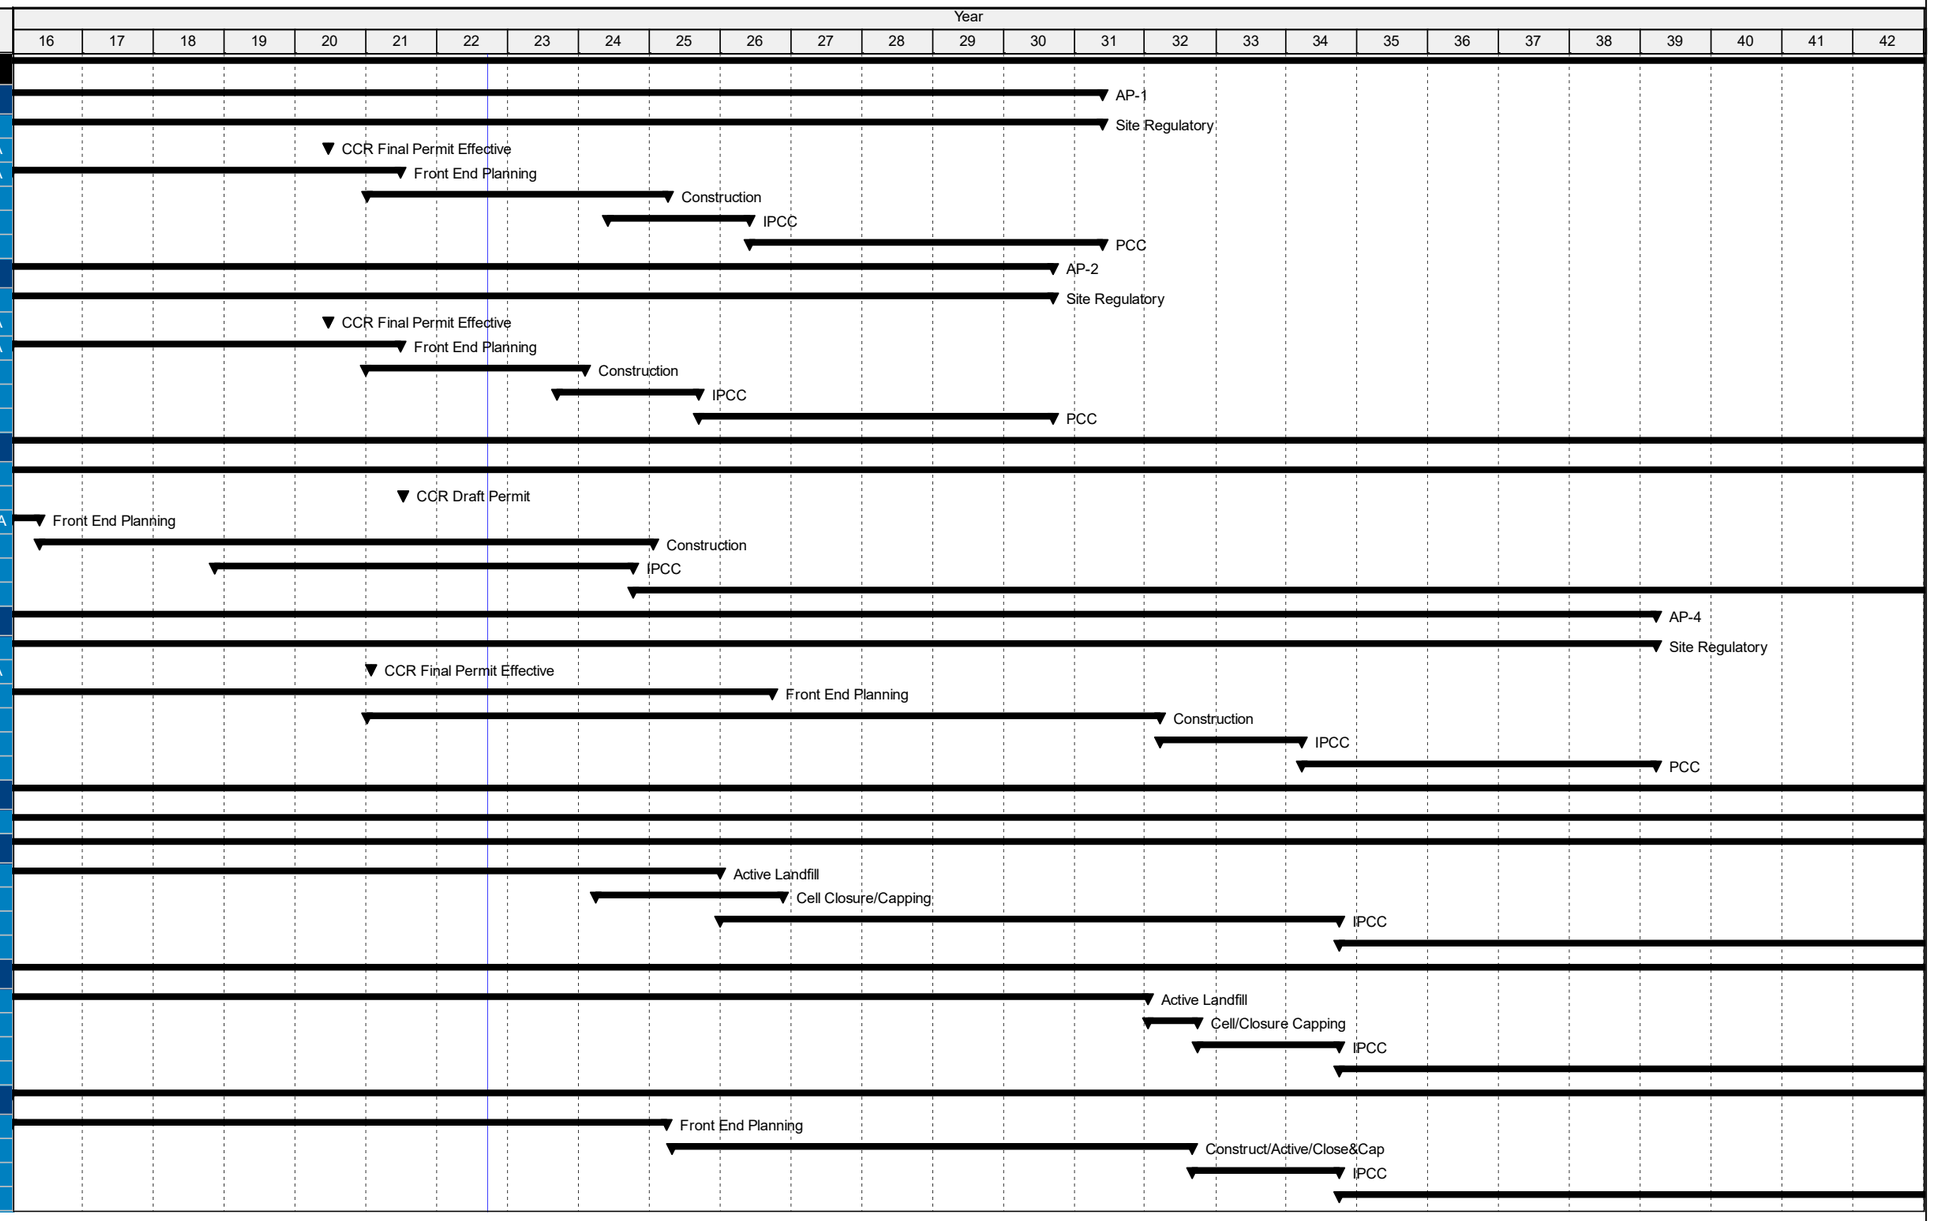


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Kraft CCR	19-Oct-15 A	06-Jun-53
Grumman Rd.	19-Oct-15 A	06-Jun-53
Site Regulatory	19-Oct-15 A	06-Jun-53
Front End Planning	05-Nov-15 A	04-Jan-19 A
Construction	27-Feb-17 A	30-Oct-20 A
IPCC	03-Jan-20 A	07-Jun-23
PCC	07-Jun-23	06-Jun-53




Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
McDonough CCR	19-Oct-15 A	27-Aug-57
AP-1	19-Oct-15 A	27-Aug-57
Site Regulatory	19-Oct-15 A	27-Aug-57
Front End Planning	01-Jan-16 A	26-Jul-24
Construction	18-Jan-16 A	01-Sep-25
IPCC	26-Aug-25	26-Aug-27
PCC	26-Aug-27	26-Aug-57
AP-2/AP-3/AP-4	19-Oct-15 A	06-Sep-55
Site Regulatory	19-Oct-15 A	06-Sep-55
Front End Planning	01-Jan-16 A	12-Feb-16 A
Construction	19-Jan-16 A	18-Sep-23
IPCC	07-Sep-23	05-Sep-25
PCC AP-2	06-Sep-25	07-Sep-30
PCC AP-3/AP-4	06-Sep-25	06-Sep-55

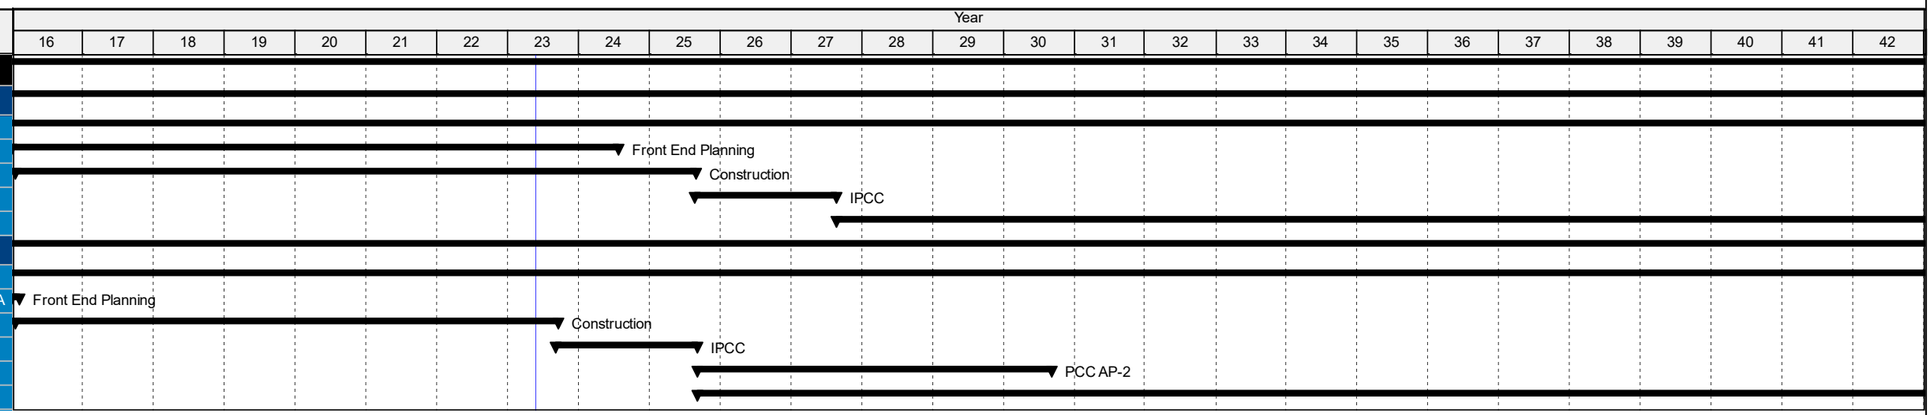


Note: The schedule forecast for this site is based on a comprehensive review completed in 3Q23 and reflects updated project schedule assumptions. Based on the timing of various reporting requirements to administer updates, actual activity dates may differ from forecasted activities at the time this version was created. The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
McIntosh CCR	12-Mar-08 A	23-Oct-54
AP-1	19-Oct-15 A	06-Oct-26
Site Regulatory	19-Oct-15 A	06-Oct-26
CCR Final Permit Effective	06-Feb-20 A	06-Feb-20 A
Front End Planning	01-Jan-16 A	06-Feb-20 A
Construction	01-Oct-19 A	06-Jul-22 A
IPCC	08-Sep-21 A	05-Oct-21 A
PCC	06-Oct-21 A	06-Oct-26
LF3	12-Mar-08 A	12-Mar-38
Site Regulatory	12-Mar-08 A	12-Mar-38
CCR Draft Permit	31-Jan-23	31-Jan-23
PCC	12-Mar-08 A	12-Mar-38
LF4	19-Oct-15 A	23-Oct-54
Site Regulatory	19-Oct-15 A	23-Oct-54
CCR Draft Permit	24-Feb-23	24-Feb-23
LF4 Cell 1	27-Nov-18 A	23-Oct-54
IPCC	27-Nov-18 A	22-Oct-24
PCC	22-Oct-24	23-Oct-54
LF4 Cell 2A	04-May-20 A	23-Oct-54
Construct/Active/Close&Cap	04-May-20 A	20-Oct-22
IPCC	22-Oct-22	22-Oct-24
PCC	22-Oct-24	23-Oct-54

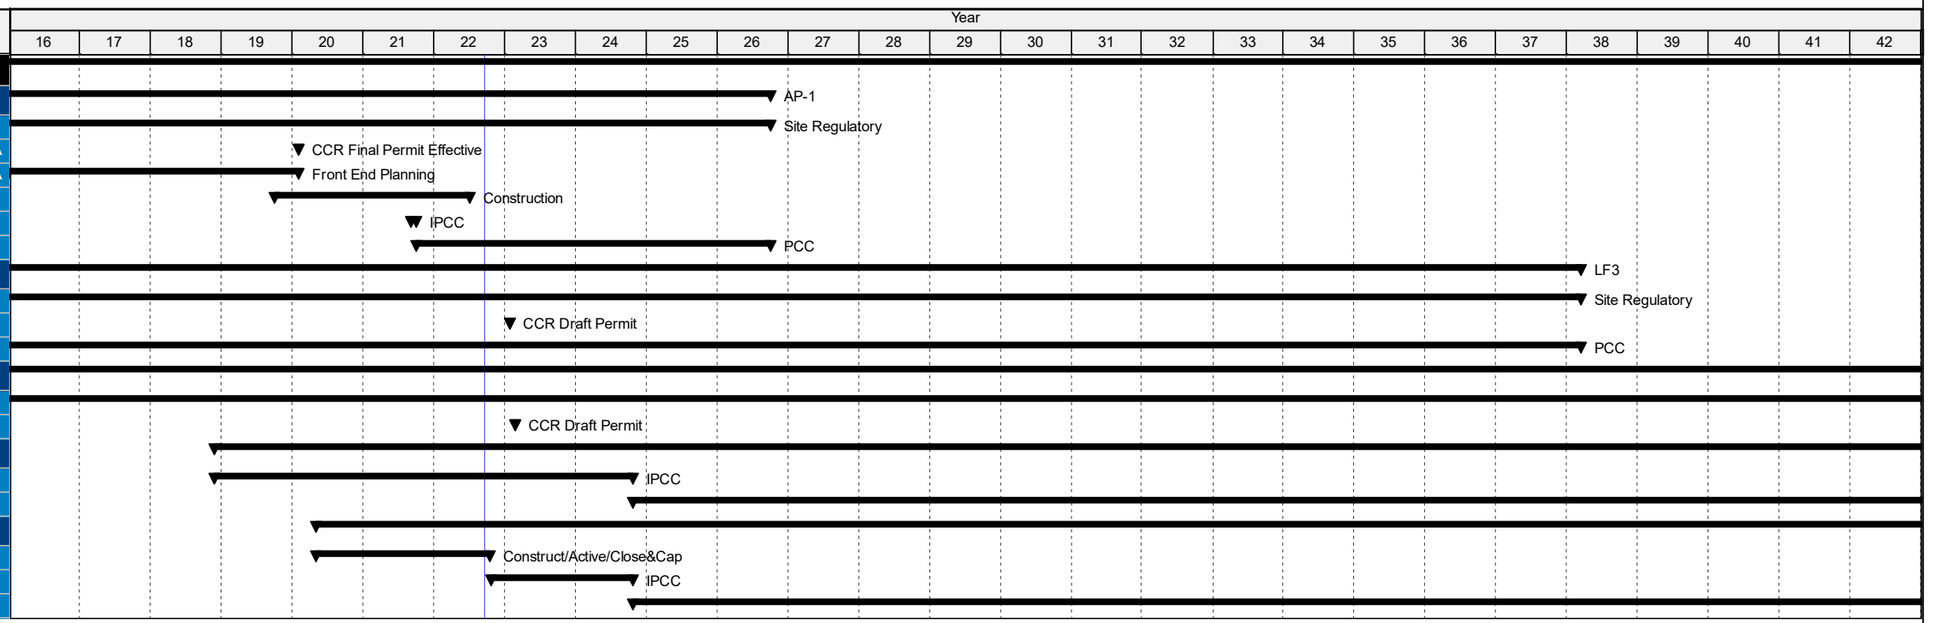


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
McManus CCR	19-Oct-15 A	21-Jul-36
McManus AP-1	19-Oct-15 A	21-Jul-36
Site Regulatory	19-Oct-15 A	21-Jul-36
CCR Final Permit Effective	18-Jun-21 A	18-Jun-21 A
Front End Planning	01-Jan-16 A	08-Dec-16 A
Construction	22-Jan-16 A	28-Jul-20 A
IPCC	25-Nov-19 A	20-Jul-21 A
PCC	20-Jul-21 A	21-Jul-36

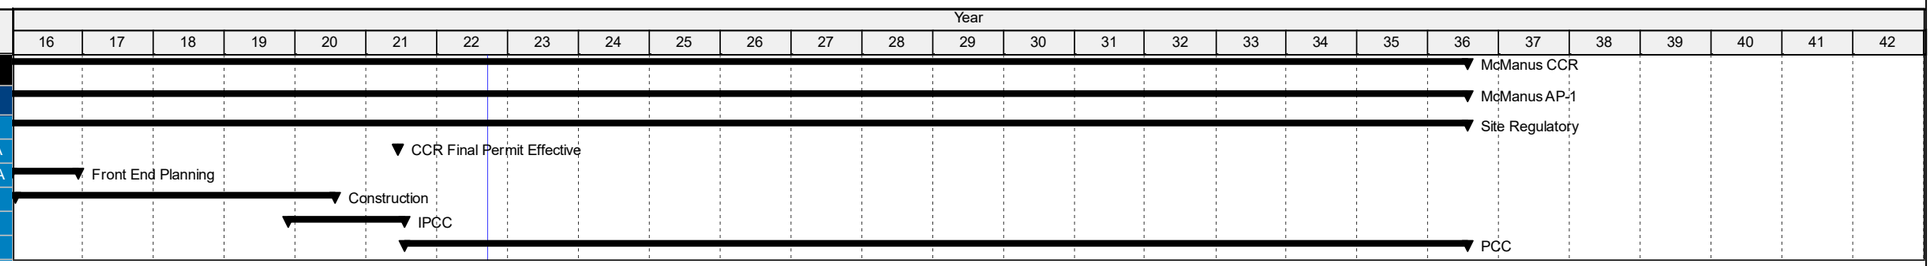


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Mitchell CCR	19-Oct-15 A	29-Sep-37
Mitchell AP-1/AP-2/AP-A	19-Oct-15 A	29-Sep-37
Site Regulatory	19-Oct-15 A	29-Sep-37
CCR Final Permit Effective	28-Jun-22 A	28-Jun-22 A
Front End Planning	01-Jan-16 A	19-Feb-21 A
Construction	17-Sep-19 A	27-Sep-30
IPCC	30-Sep-30	30-Sep-32
PCC	30-Sep-32	29-Sep-37

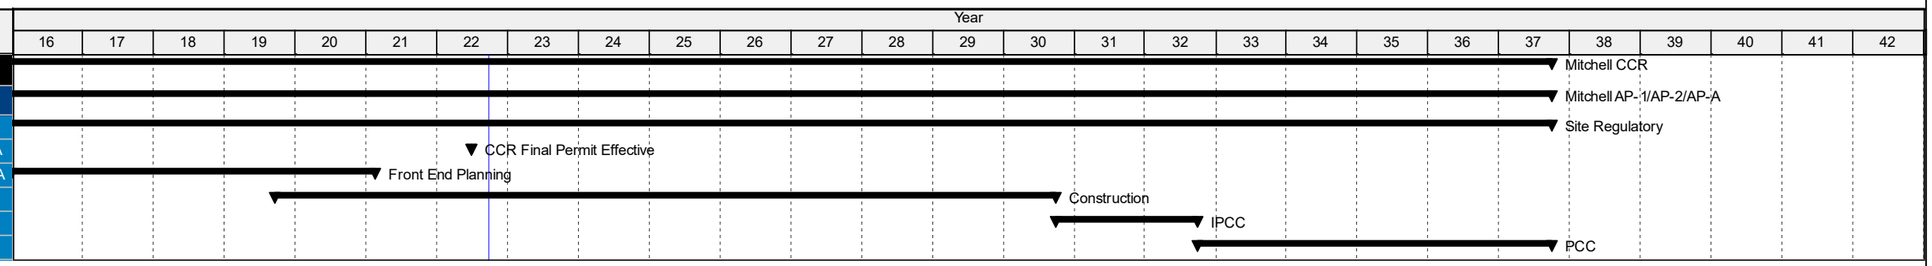


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Scherer CCR	01-Jan-10 A	01-Jan-79
Scherer AP-1	19-Oct-15 A	27-Oct-64
Site Regulatory	19-Oct-15 A	27-Oct-64
Front End Planning	01-Jan-16 A	22-Jan-27
Construction	06-Jul-21 A	01-Nov-32
IPCC	26-Oct-32	26-Oct-34
PCC	26-Oct-34	26-Oct-64
Scherer LF	01-Jan-10	01-Jan-79
Site Regulatory	01-Jan-10	01-Jan-79
LF Cell 1	01-Jan-10 A	01-Jan-79
Active Landfill	01-Jan-10 A	02-Jan-45
Cell Closure/Capping	02-Jan-45	31-Dec-46
IPCC	01-Jan-47	31-Dec-48
PCC	01-Jan-49	01-Jan-79
PAC/ASH CELL	01-Jan-11 A	01-Jan-79
Active Landfill	01-Jan-11 A	01-Jan-27
Cell Closure/Capping	01-Jan-27	31-Dec-28
IPCC	01-Jan-29	31-Dec-48
PCC	01-Jan-49	01-Jan-79

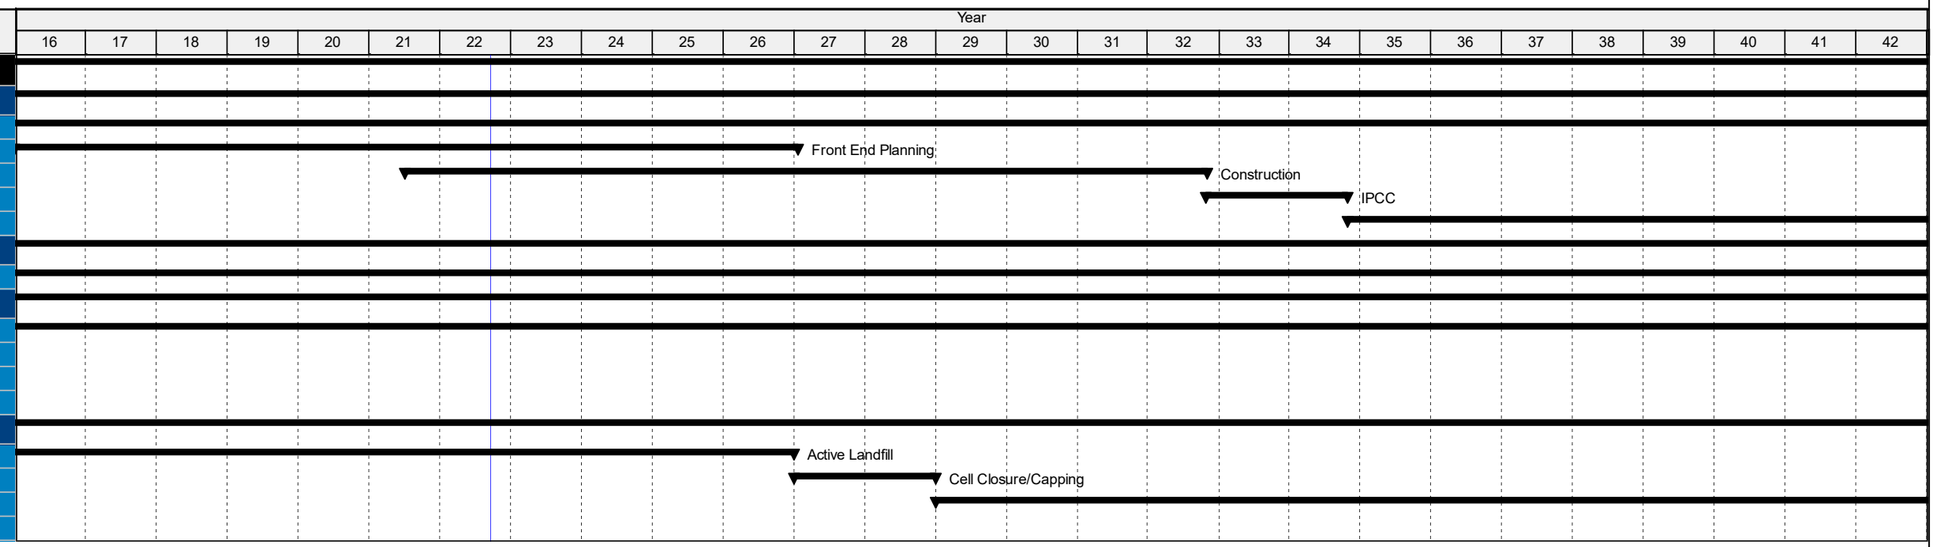


Note: Based on a comprehensive review performed during 3Q23, the current schedule forecast for this site has been determined to be substantially consistent with the prior update reflected in the March 2023 Semi-Annual status report and is therefore reflected consistently with that report. In some cases, actual activity dates may differ from forecasted activities The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Wansley CCR	01-Jan-12 A	14-Feb-66
Wansley AP-1	19-Oct-15 A	23-Mar-41
Site Regulatory	19-Oct-15 A	23-Mar-41
Front End Planning	01-Jan-16 A	27-Mar-24
Construction	19-Apr-21 A	06-Apr-34
IPCC	01-Apr-34	28-Mar-36
PCC	29-Mar-36	22-Mar-41
Wansley Landfill	31-Oct-22 A	14-Feb-66
Site Regulatory	31-Oct-22 A	14-Feb-66
Landfill Cells 1&2	01-Jan-12 A	14-Feb-66
Active for Closure	01-Jan-12 A	06-Mar-31
Cell Closure/Capping	16-May-30	26-Mar-34
IPCC	27-Mar-34	23-Mar-36
PCC	24-Mar-36	14-Feb-66
Landfill Cell 3	28-Jun-19 A	14-Feb-66
Active for Closure	28-Jun-19 A	24-Mar-34
Cell Closure/Capping	28-Jun-19 A	24-Mar-34
IPCC	27-Mar-34	23-Mar-36
PCC	24-Mar-36	14-Feb-66
Landfill Cell 4	08-Apr-24	14-Feb-66
Front End Planning	24-Jun-24	24-Jun-24
Construct/Active for Closure	08-Apr-24	28-Apr-27
Cell Closure/Capping	22-Jan-30	26-Mar-34
IPCC	27-Mar-34	23-Mar-36
PCC	24-Mar-36	14-Feb-66

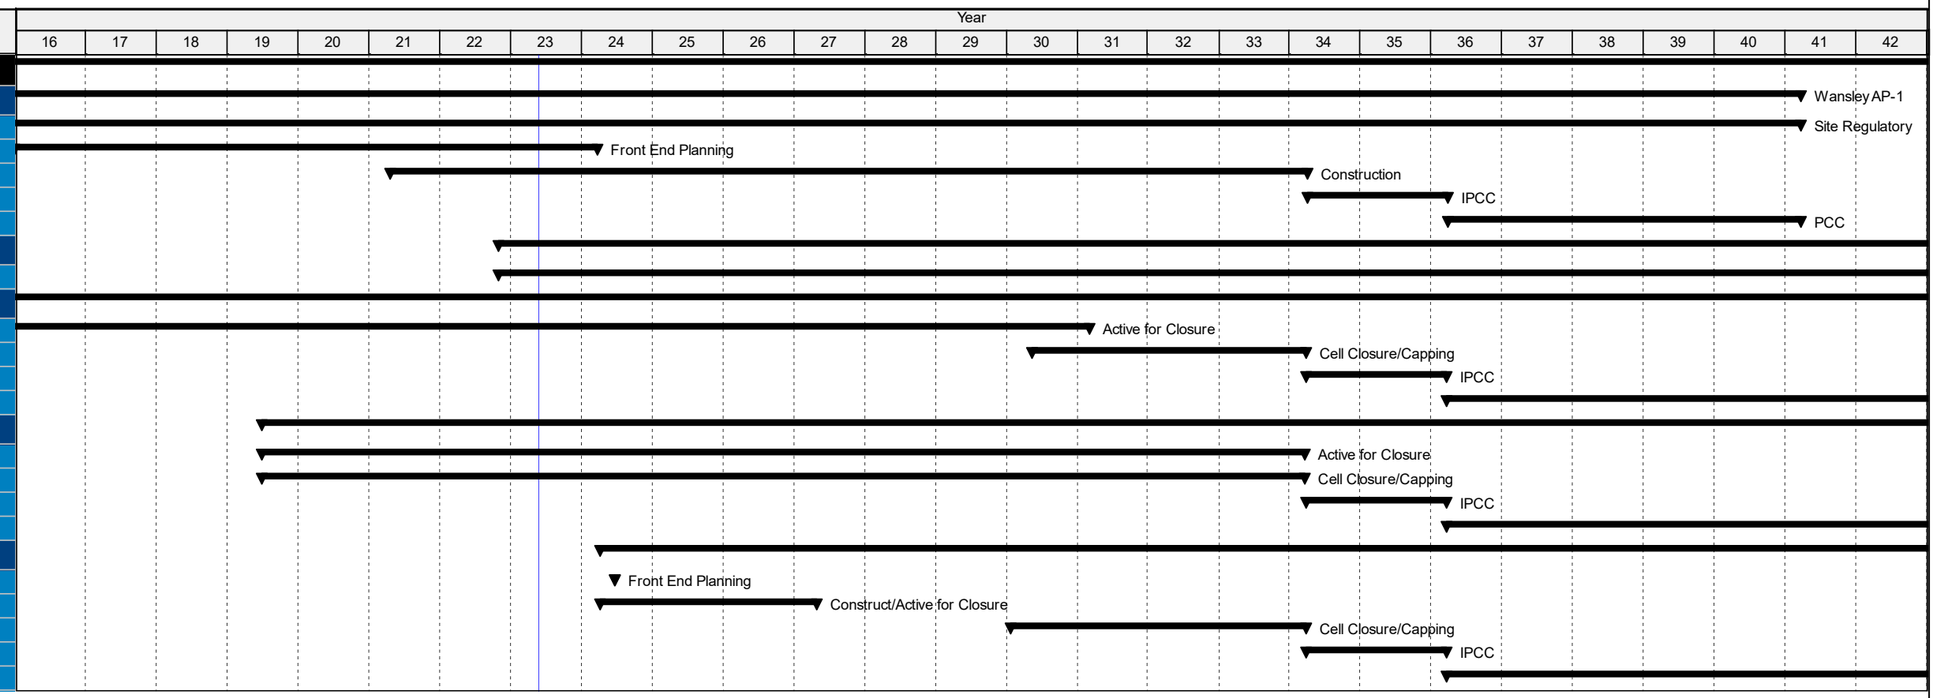

Note: The schedule forecast for this site is based on a comprehensive review completed in 3Q23 and reflects updated project schedule assumptions. Based on the timing of various reporting requirements to administer updates, actual activity dates may differ from forecasted activities at the time this version was created. The Company will continue to monitor all project assumptions and provide updates in the future.

Activity ID	Start	Finish
Yates CCR	04-May-15 A	21-Jun-56
Yates AP-1	04-May-15 A	01-Feb-27
Site Regulatory	19-Oct-15 A	01-Feb-27
CCR Final Permit Effective	06-Jan-22 A	06-Jan-22 A
Front End Planning	04-May-15 A	21-Jul-16 A
Construction	04-May-15 A	08-May-24
IPCC	27-Nov-19 A	31-Jan-22 A
PCC	31-Jan-22 A	01-Feb-27
Yates AP-2	19-Oct-15 A	31-May-30
Site Regulatory	19-Oct-15 A	31-May-30
Front End Planning	01-Jan-16 A	20-Nov-19 A
Construction	05-Sep-19 A	08-May-24
IPCC	01-Jun-23 A	30-May-25
PCC	31-May-25	30-May-30
Yates AMA (AP-3/AP-B/AP-B'/AP-A)	19-Oct-15 A	21-Jun-56
Site Regulatory	19-Oct-15 A	21-Jun-56
Front End Planning	01-Jan-16 A	30-Apr-18 A
Construction	19-Aug-16 A	18-Jun-24
IPCC	20-Jun-24	19-Jun-26
PCC	20-Jun-26	20-Jun-56
Yates Gypsum Landfill	22-Jul-15 A	15-Aug-24
Site Regulatory	22-Jul-15 A	15-Aug-24
CCR Final Permit Effective	05-Jan-22 A	05-Jan-22 A
IPCC	19-Jan-17 A	14-Feb-22 A
PCC	14-Feb-22 A	15-Aug-24
Yates R-6/AP-C	29-May-15 A	28-Nov-55
Site Regulatory	29-May-15 A	28-Nov-55
Front End Planning	29-May-15 A	21-Jul-16 A
Construction	29-May-15 A	08-May-24
IPCC	28-Nov-23	27-Nov-25
PCC	27-Nov-25	28-Nov-55

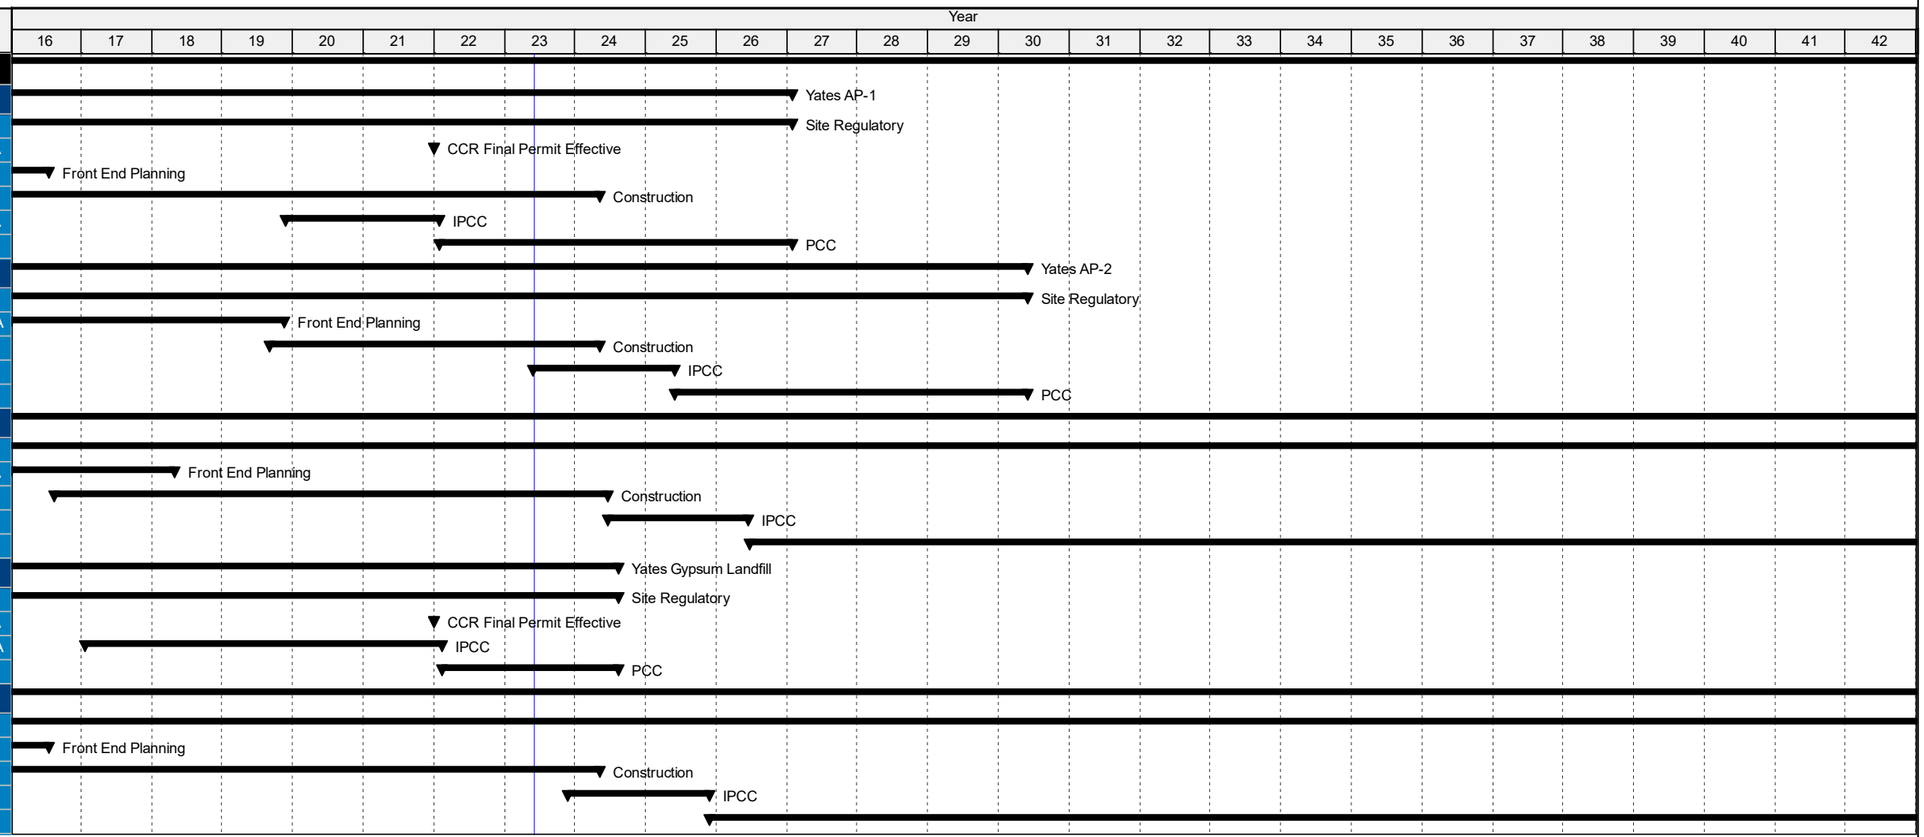

Note: The schedule forecast for this site is based on a comprehensive review completed in 3Q23 and reflects updated project schedule assumptions. Based on the timing of various reporting requirements to administer updates, actual activity dates may differ from forecasted activities at the time this version was created. The Company will continue to monitor all project assumptions and provide updates in the future.
