

Activity ID	Start	Finish
Arkwright CCR	19-Oct-15 A	05-May-64
AP-1	19-Oct-15 A	19-Oct-38
Site Regulatory	19-Oct-15 A	19-Oct-38
Front End Planning	01-Jan-16 A	16-Nov-26
Construction	01-Jun-23 A	06-Aug-32
IPCC	20-Oct-31	19-Oct-33
PCC	19-Oct-33	19-Oct-38
AP-2 DAS	19-Oct-15 A	16-Nov-35
Site Regulatory	19-Oct-15 A	16-Nov-35
Front End Planning	01-Jan-16 A	13-Nov-26
Construction	31-Mar-25	06-Aug-32
IPCC	15-Nov-28	18-Nov-30
PCC	18-Nov-30	16-Nov-35
CCRLF/AP-3/Monofill	01-Jan-16 A	05-May-64
Site Regulatory	20-Nov-18 A	05-May-64
Front End Planning	01-Jan-16 A	13-Nov-26
Construction/Active/Close&Cap	20-Jul-26	06-Aug-32
IPCC	03-May-32	04-May-34
PCC	05-May-34	04-May-64

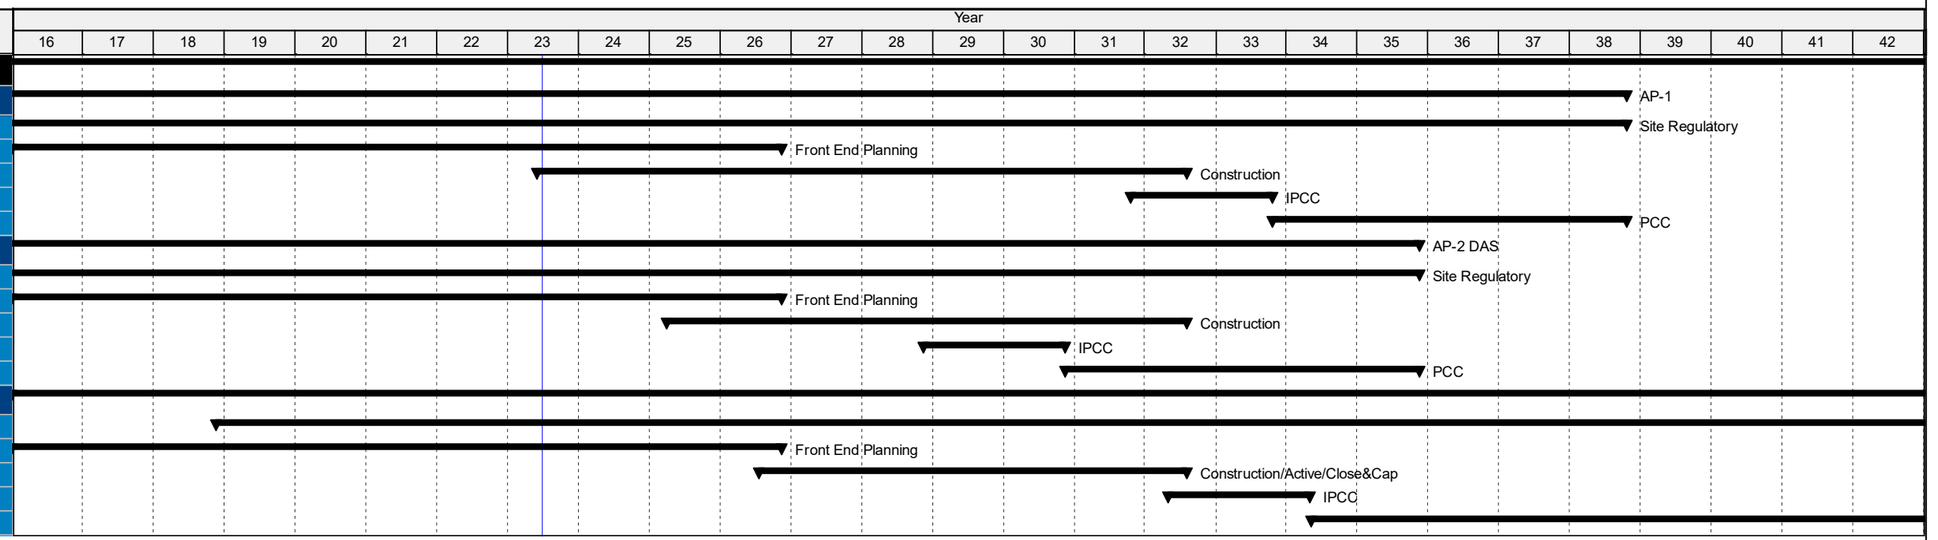

Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.


Activity ID	Start	Finish
Bowen CCR	12-May-08 A	01-Jan-72
AP-1	19-Oct-15 A	07-Jul-66
Site Regulatory	19-Oct-15 A	07-Jul-66
CCR Final Permit Effective	17-Feb-22 A	17-Feb-22 A
Front End Planning	01-Jan-16 A	08-Dec-20 A
Construction	14-Dec-17 A	21-Dec-34
IPCC	06-Jul-34	06-Jul-36
PCC	06-Jul-36	07-Jul-66
Bowen Landfill	12-May-08 A	01-Jan-72
Site Regulatory	12-May-08 A	01-Jan-72
CCR Final Permit Effective	08-Dec-22 A	08-Dec-22 A
LF Cells 1 & 2	02-Jan-20 A	01-Jan-72
Active Landfill	02-Jan-20 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 3 & 4	02-Jan-20 A	01-Jan-72
Active Landfill	02-Jan-20 A	31-Mar-23 A
Cell Closure/Capping	31-Mar-23 A	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 5 & 6	29-Apr-22 A	01-Jan-72
Construction/Active for Closure	29-Apr-22 A	28-Oct-39
Cell Closure/Capping	24-Dec-38	28-Oct-39
IPCC	01-Jan-40	31-Dec-41
PCC	31-Dec-41	01-Jan-72
LF Cells 9 & 10	01-Jan-23 A	01-Jan-72
Active Landfill	01-Jan-23 A	31-Dec-35
Cell Closure/Capping	01-Jan-36	31-Dec-37
IPCC	01-Jan-38	31-Dec-41
PCC	01-Jan-42	01-Jan-72

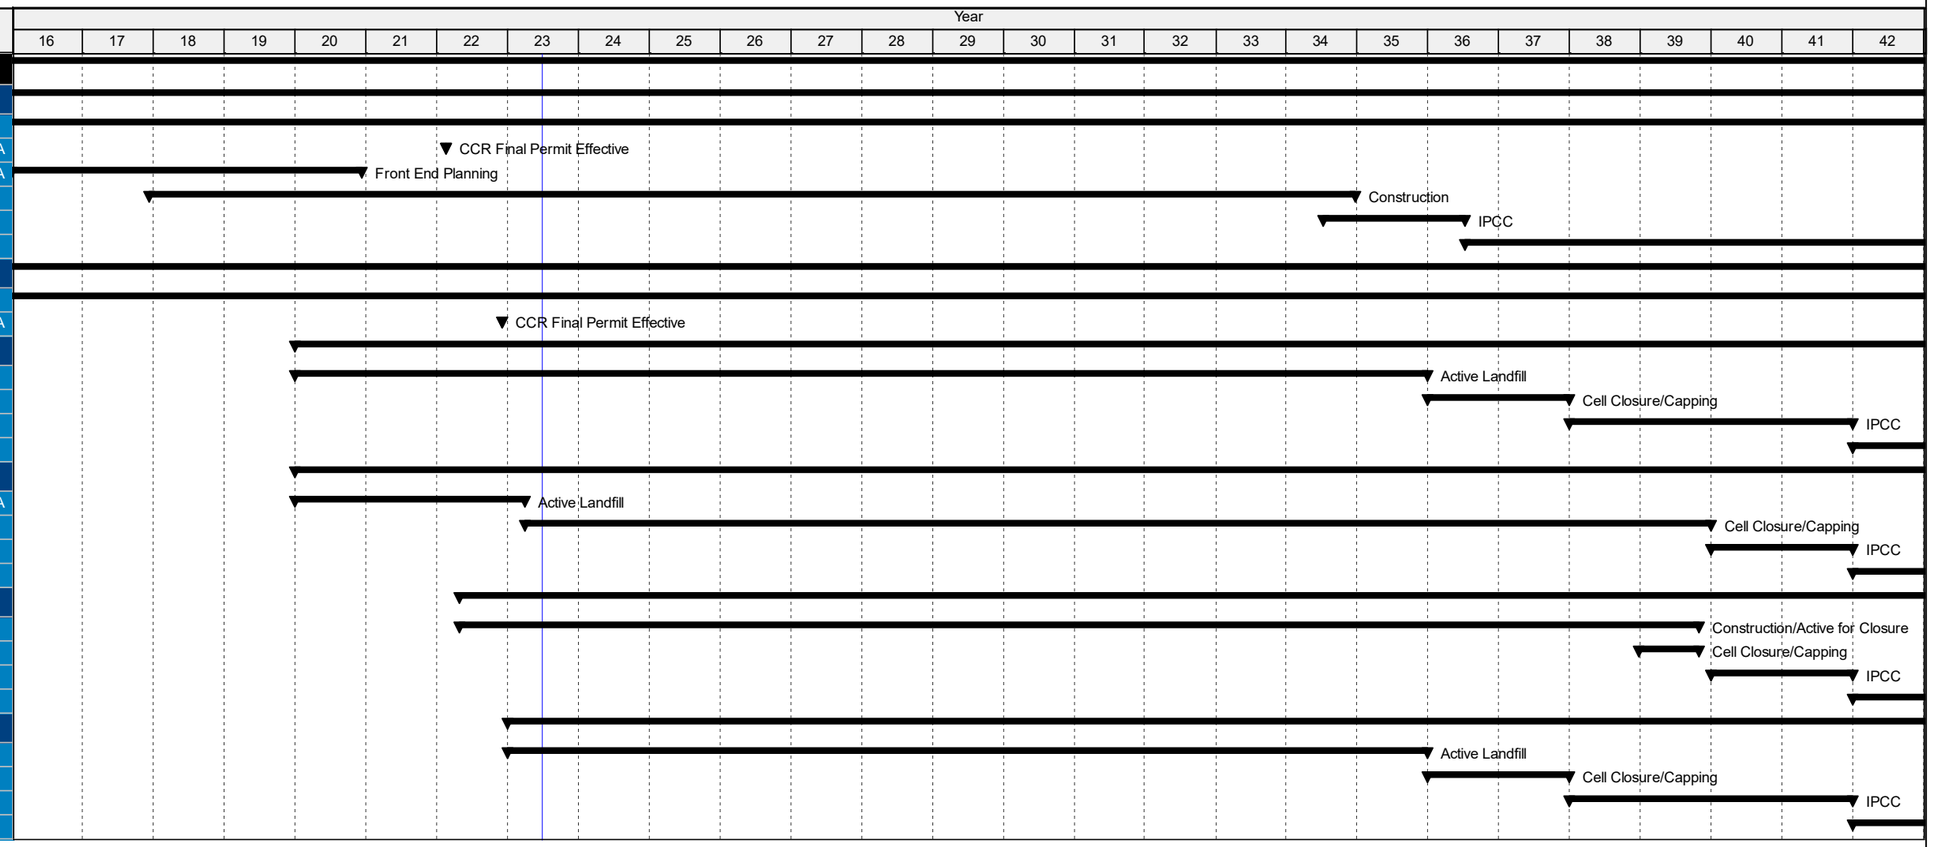

Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Ash Pond Closure Portfolio - 1Q24
Gantt Chart by Plant


Activity ID	Start	Finish
Branch CCR	19-Oct-15 A	29-May-73
AP-B/AP-C/AP-D	19-Oct-15 A	07-Jul-43
Site Regulatory	19-Oct-15 A	07-Jul-43
Front End Planning	01-Jan-16 A	11-Feb-25
Construction	01-Mar-19 A	18-Jun-41
IPCC	03-Jul-36	02-Jul-38
PCC	06-Jul-38	06-Jul-43
AP-E	19-Oct-15 A	20-Jan-42
Site Regulatory	19-Oct-15 A	20-Jan-42
Front End Planning	01-Jan-16 A	11-Feb-25
Construction	01-Mar-19 A	18-Jun-41
IPCC	15-Jan-35	18-Jan-37
PCC	20-Jan-37	19-Jan-42
Branch LF	01-Jan-16 A	29-May-73
Site Regulatory	28-Feb-17 A	29-May-73
CCR Final Permit Effective	25-Jan-23 A	25-Jan-23 A
Front End Planning	01-Jan-16 A	11-Jul-23
Construction/Active/Close&Cap	10-Apr-23 A	18-Jun-41
Beneficial Use	12-Jun-23 A	18-Jun-41
IPCC	29-May-41	29-May-43
PCC	29-May-43	29-May-73

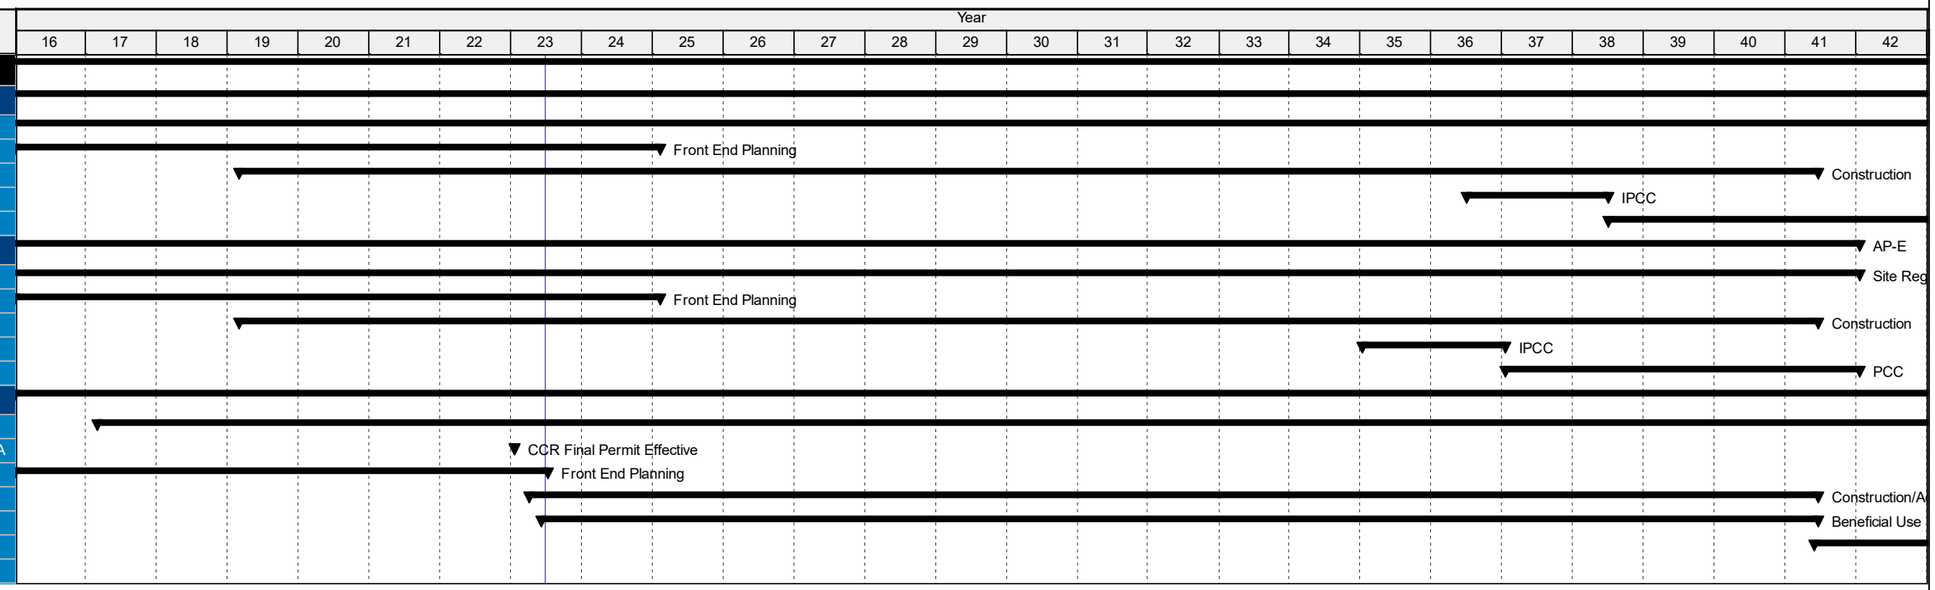

Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.


Ash Pond Closure Portfolio - 1Q24
Gantt Chart by Plant

Activity ID	Start	Finish
Hammond CCR	01-Jan-08 A	30-Sep-64
AP-1	19-Oct-15 A	14-Oct-31
Site Regulatory	19-Oct-15 A	16-Oct-26
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	11-Jan-21 A	08-May-25
IPCC	19-Oct-24	15-Oct-26
PCC	15-Oct-26	14-Oct-31
AP-2	19-Oct-15 A	23-Dec-30
Site Regulatory	19-Oct-15 A	23-Dec-30
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	04-Jan-21 A	13-May-24
IPCC	23-Dec-23	22-Dec-25
PCC	22-Dec-25	22-Dec-30
AP-3	19-Oct-15 A	29-Mar-55
Site Regulatory	19-Oct-15 A	29-Mar-55
CCR Draft Permit	12-Jul-21 A	12-Jul-21 A
Front End Planning	01-Jan-16 A	25-May-16 A
Construction	26-May-16 A	09-Jul-25
IPCC	13-Nov-18 A	28-Mar-25
PCC	28-Mar-25	26-Mar-55
AP-4	19-Oct-15 A	21-Mar-39
Site Regulatory	19-Oct-15 A	21-Mar-39
CCR Final Permit Effective	27-Jan-21 A	27-Jan-21 A
Front End Planning	01-Jan-16 A	28-Sep-26
Construction	11-Jan-21 A	23-Mar-32
IPCC	21-Mar-32	21-Mar-34
PCC	21-Mar-34	21-Mar-39
Huffaker Rd LF	01-Jan-08 A	30-Sep-64
Site Regulatory	01-Jan-08 A	30-Sep-64
Huffaker Rd A/B	01-Jan-08 A	30-Sep-64
Active Landfill	01-Jan-08 A	26-Oct-25
Cell Closure/Capping	16-Aug-24	03-Jun-27
IPCC	27-Oct-25	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell E	21-Jan-32	30-Sep-64
Active Landfill	21-Jan-32	29-Jul-32
Cell/Closure Capping	29-Jul-32	27-Sep-32
IPCC	28-Sep-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64
Huffaker Rd Cell F	15-Oct-24	30-Sep-64
Front End Planning	15-Oct-24	13-Mar-25
Construction/Active/Close&Cap	09-Apr-25	22-Oct-32
IPCC	30-Aug-32	30-Sep-34
PCC	01-Oct-34	30-Sep-64

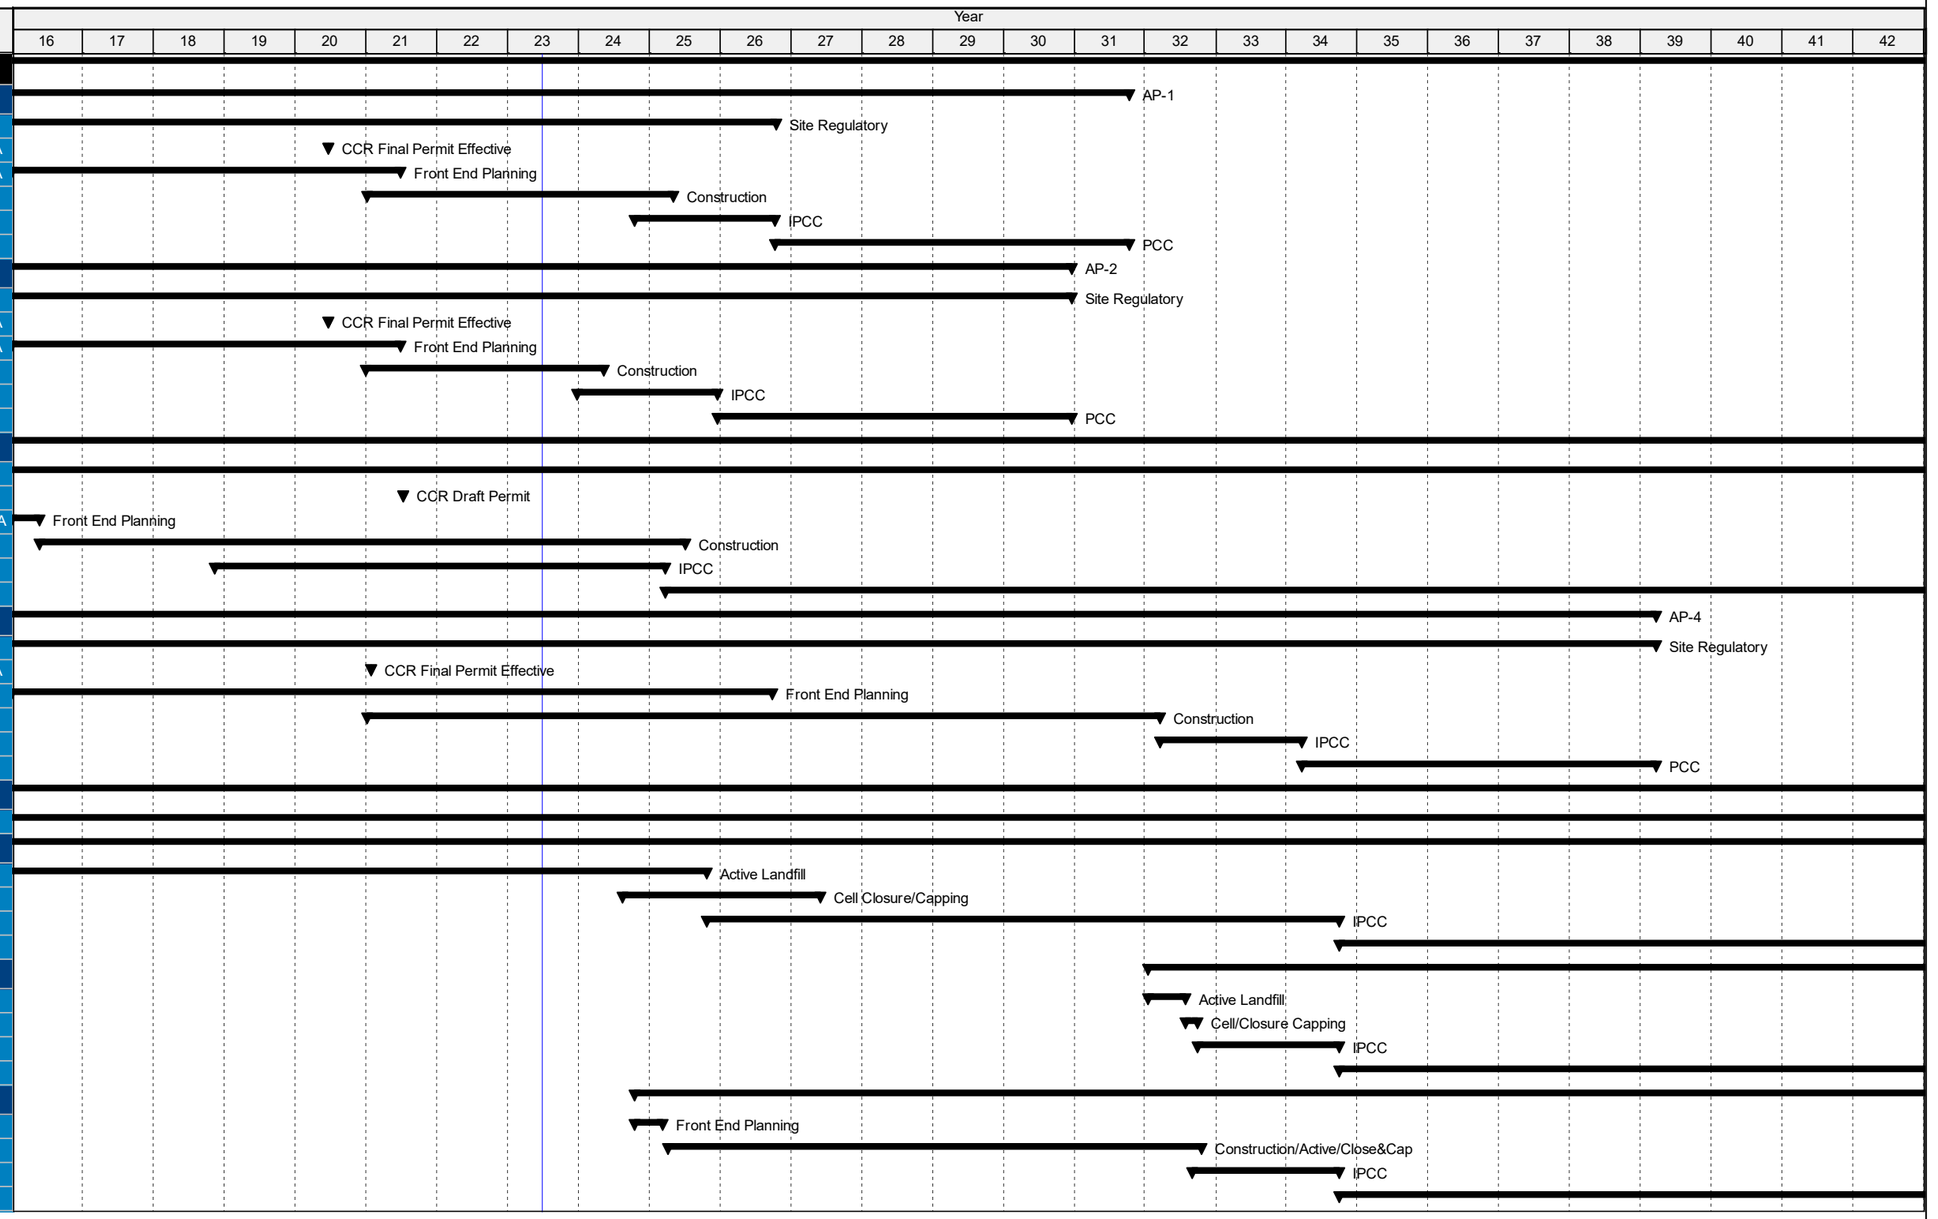


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Activity ID	Start	Finish
Kraft CCR	19-Oct-15 A	07-Jan-54
Grumman Rd.	19-Oct-15 A	07-Jan-54
Site Regulatory	19-Oct-15 A	07-Jan-54
Front End Planning	05-Nov-15 A	07-Jul-23
Construction	27-Feb-17 A	05-Jan-24
IPCC	03-Jan-20 A	07-Jan-24
PCC	08-Jan-24	07-Jan-54



Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Activity ID	Start	Finish
McDonough CCR	19-Oct-15 A	08-Nov-57
AP-1	19-Oct-15 A	08-Nov-57
Site Regulatory	19-Oct-15 A	08-Nov-57
Front End Planning	01-Jan-16 A	07-Oct-24
Construction	18-Jan-16 A	11-Nov-25
IPCC	07-Nov-25	07-Nov-27
PCC	08-Nov-27	08-Nov-57
AP-2/AP-3/AP-4	19-Oct-15 A	09-Oct-56
Site Regulatory	19-Oct-15 A	09-Oct-56
Front End Planning	01-Jan-16 A	12-Feb-16 A
Construction	19-Jan-16 A	11-Oct-24
IPCC	09-Oct-24	08-Oct-26
PCC AP-2	09-Oct-26	10-Oct-31
PCC AP-3/AP-4	09-Oct-26	08-Oct-56

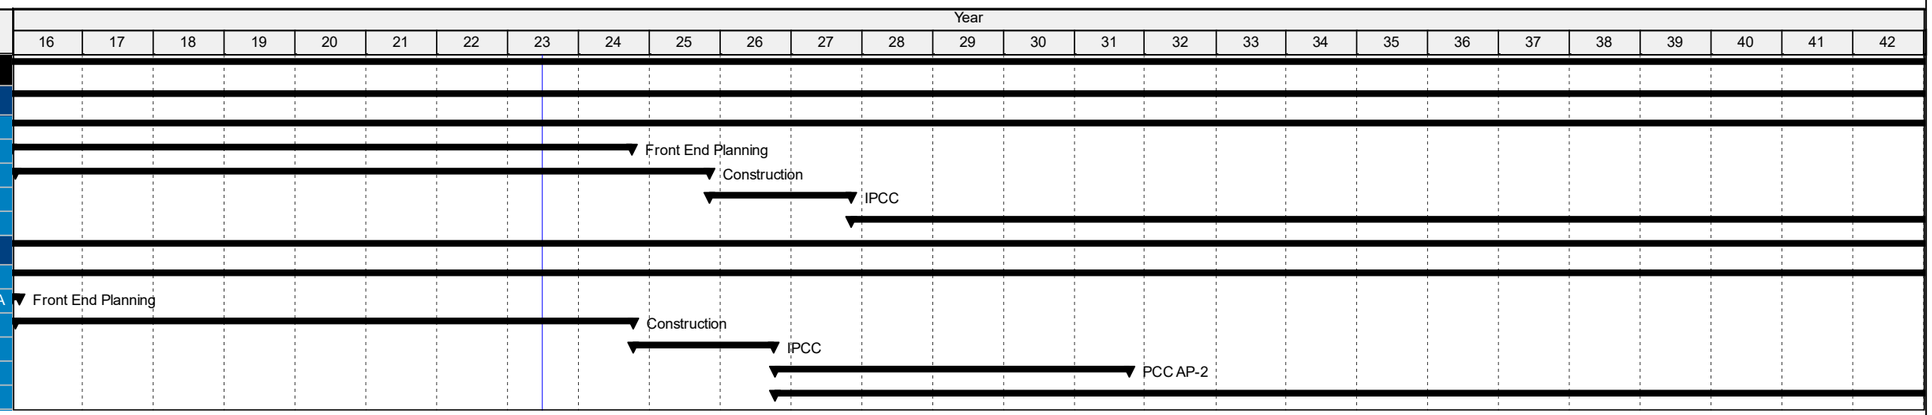


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.


Ash Pond Closure Portfolio - 1Q24
Gantt Chart by Plant

PUBLIC DISCLOSURE

Activity ID	Start	Finish
McIntosh CCR	12-Mar-08 A	23-Oct-54
AP-1	19-Oct-15 A	06-Oct-26
Site Regulatory	19-Oct-15 A	05-Oct-26
CCR Final Permit Effective	06-Feb-20 A	06-Feb-20 A
Front End Planning	01-Jan-16 A	06-Feb-20 A
Construction	01-Oct-19 A	06-Jul-22 A
IPCC	08-Sep-21 A	05-Oct-21 A
PCC	06-Oct-21 A	06-Oct-26
LF3	12-Mar-08 A	21-Mar-38
Site Regulatory	12-Mar-08 A	12-Mar-38
CCR Draft Permit	31-Jan-23 A	31-Jan-23 A
PCC	21-Mar-08 A	21-Mar-38
LF4	19-Oct-15 A	23-Oct-54
Site Regulatory	19-Oct-15 A	23-Oct-54
CCR Draft Permit	24-Feb-23 A	24-Feb-23 A
LF4 Cell 1	27-Nov-18 A	23-Oct-54
IPCC	27-Nov-18 A	22-Oct-24
PCC	22-Oct-24	23-Oct-54
LF4 Cell 2A	23-Feb-21 A	23-Oct-54
Construct/Active/Close&Cap	23-Feb-21 A	15-Mar-23 A
IPCC	20-Oct-22 A	22-Oct-24
PCC	22-Oct-24	23-Oct-54

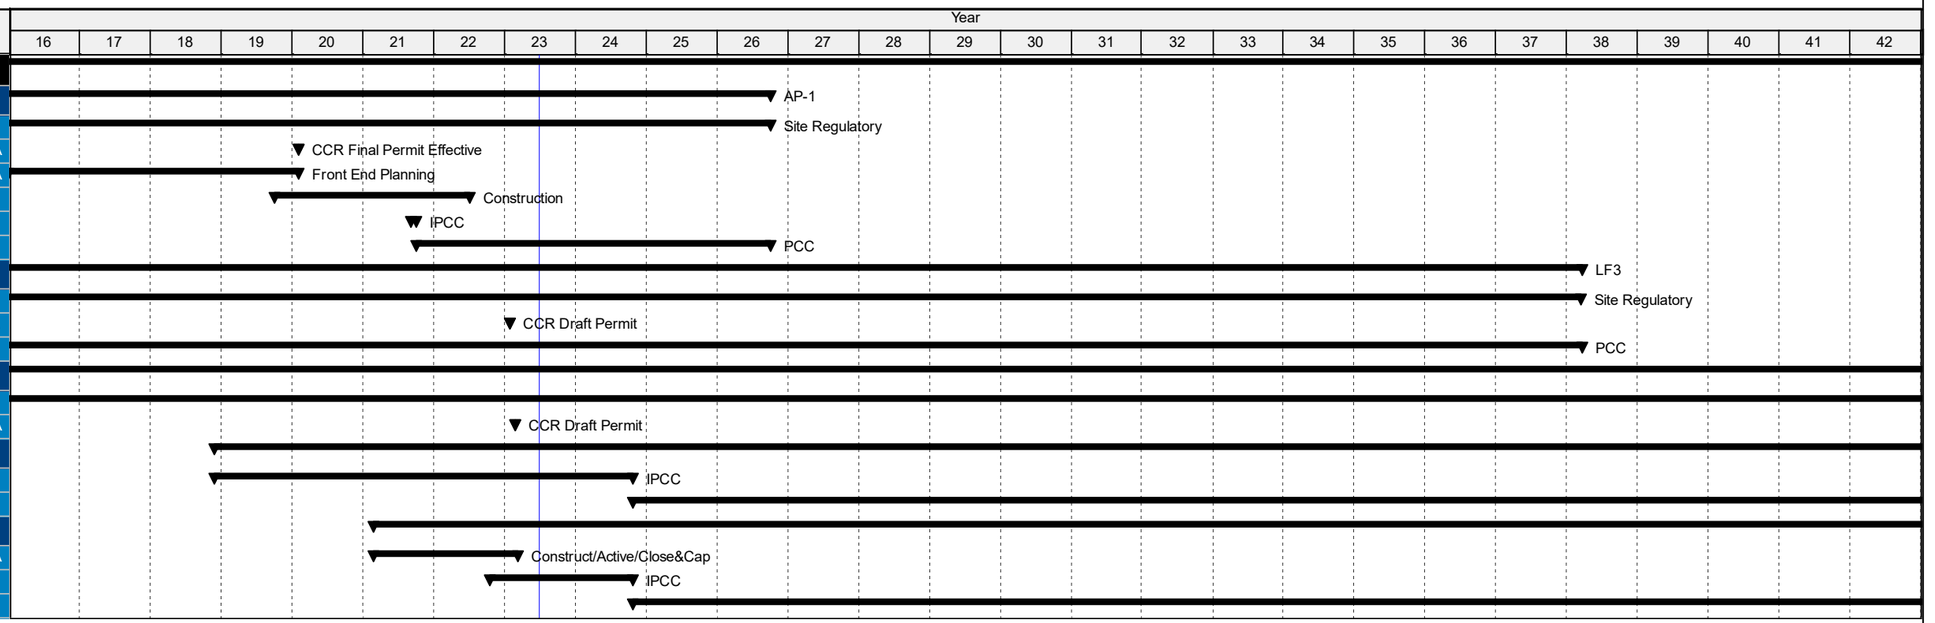


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

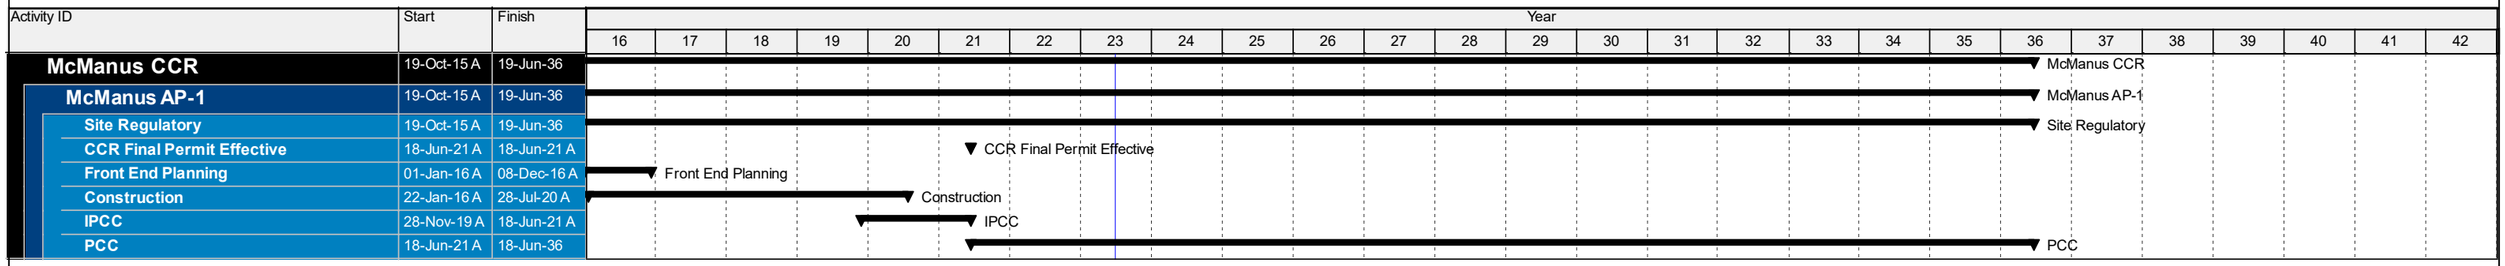


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Activity ID	Start	Finish
Mitchell CCR	19-Oct-15 A	01-Oct-37
Mitchell AP-1/AP-2/AP-A	19-Oct-15 A	01-Oct-37
Site Regulatory	19-Oct-15 A	01-Oct-37
CCR Final Permit Effective	28-Jun-22 A	28-Jun-22 A
Front End Planning	01-Jan-16 A	19-Feb-21 A
Construction	17-Sep-19 A	27-Sep-30
IPCC	30-Sep-30	30-Sep-32
PCC	30-Sep-32	29-Sep-37

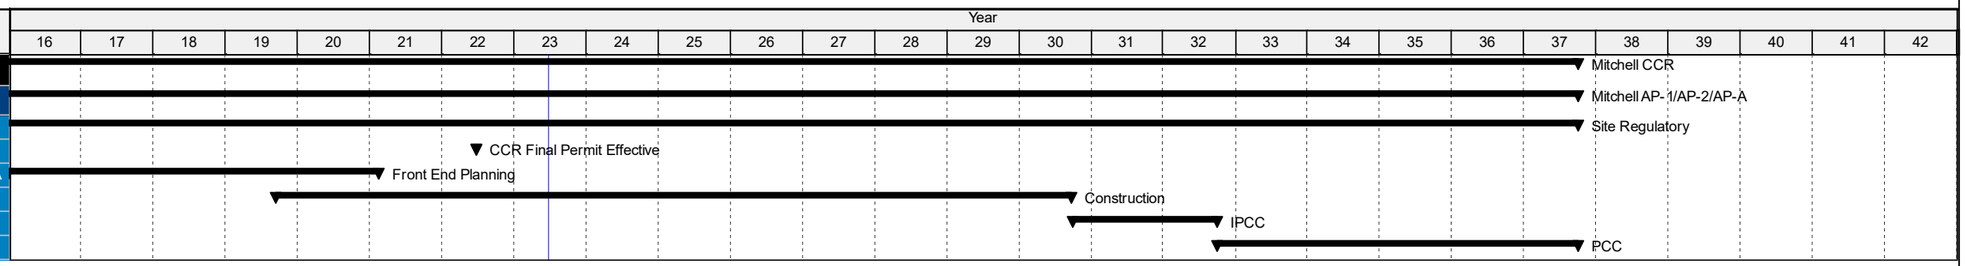


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

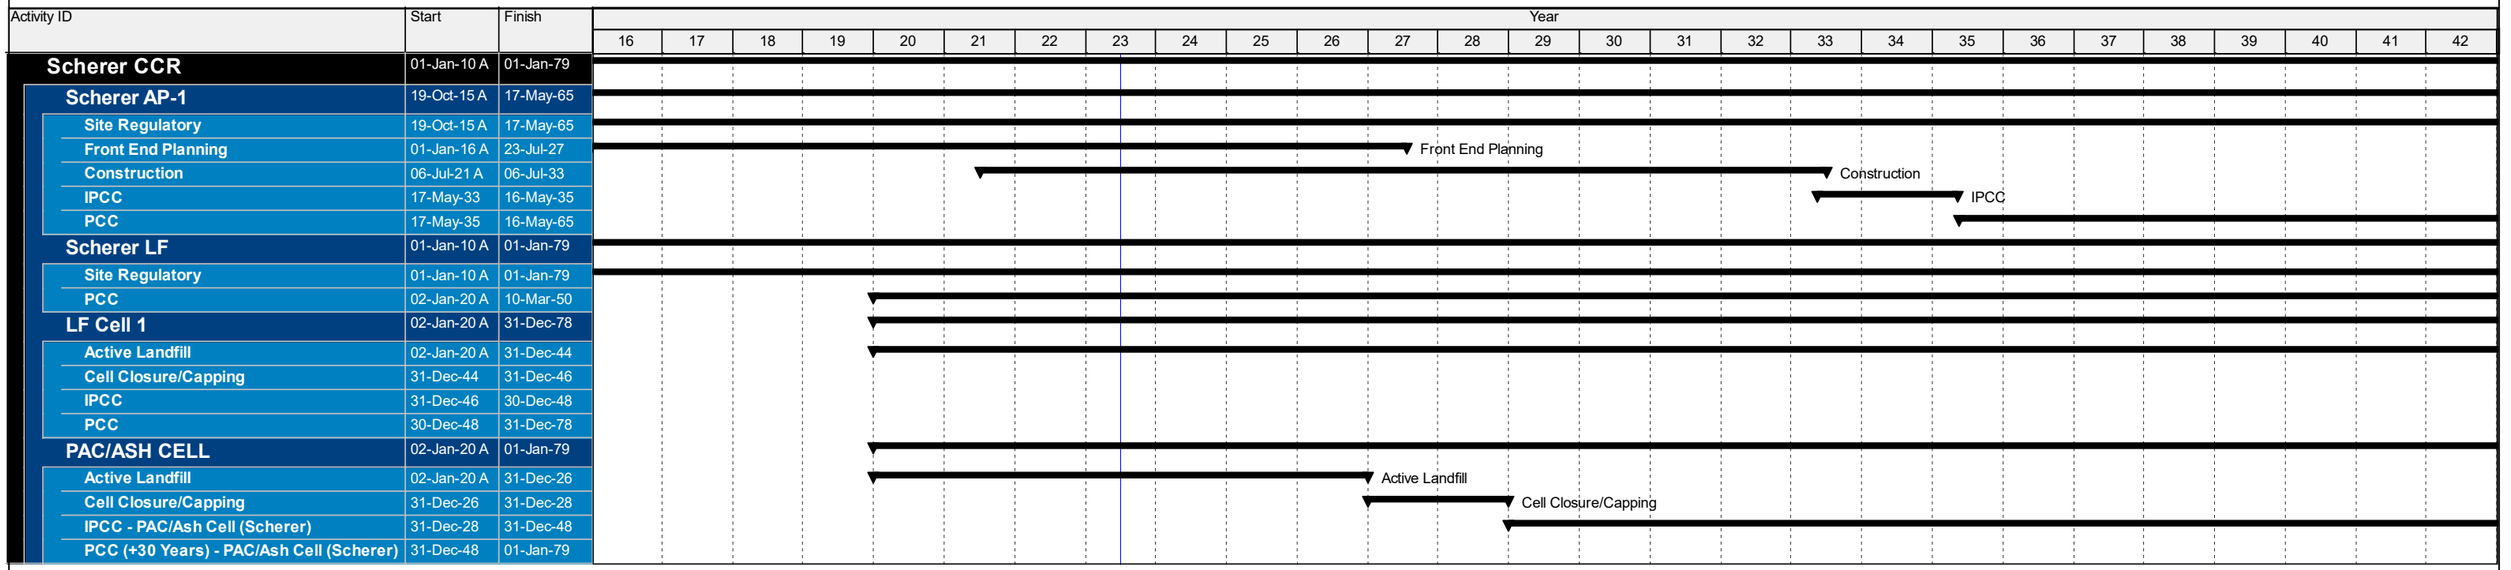

Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Ash Pond Closure Portfolio - 1Q24
Gantt Chart by Plant

Activity ID	Start	Finish
Wansley CCR	01-Jan-12 A	14-Feb-66
Wansley AP-1	19-Oct-15 A	23-Mar-41
Site Regulatory	19-Oct-15 A	23-Mar-41
Front End Planning	01-Jan-16 A	27-Mar-24
Construction	19-Apr-21 A	06-Apr-34
IPCC	01-Apr-34	28-Mar-36
PCC	29-Mar-36	22-Mar-41
Wansley Landfill	01-Jan-12 A	14-Feb-66
Site Regulatory	01-Jan-12 A	14-Feb-66
Front End Planning	22-Jul-22 A	03-Jun-24
Construct Cell/Active for Closure	10-Dec-24	08-Oct-25
Cell Closure/Capping	19-May-33	19-May-33
Landfill Cells 1/2/3	01-Jan-12 A	14-Feb-66
Active for Closure	01-Jan-12 A	22-Jan-30
Cell Closure/Capping	08-Apr-24	26-Mar-34
IPCC	26-Mar-34	23-Mar-36
PCC	23-Mar-36	14-Feb-66
Landfill Cell 4	08-Oct-25	14-Feb-66
Construct Cell/Active for Closure	08-Oct-25	28-Apr-27
Cell Closure/Capping	21-Jan-30	26-Mar-34
IPCC	26-Mar-34	23-Mar-36
PCC	23-Mar-36	14-Feb-66

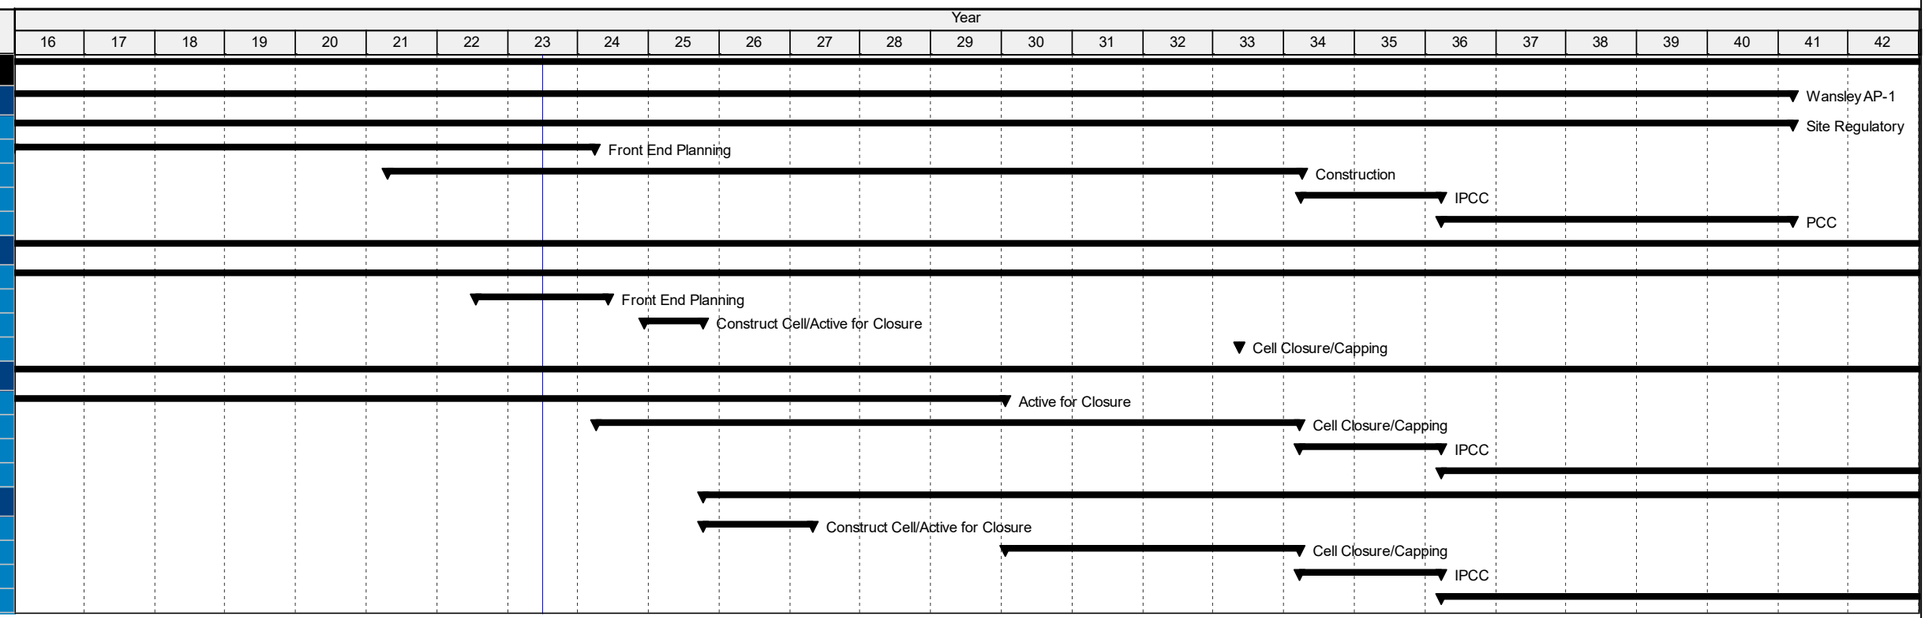


Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.

Ash Pond Closure Portfolio - 1Q24
Gantt Chart by Plant

PUBLIC DISCLOSURE

Activity ID	Start	Finish
Yates CCR	04-May-15 A	08-Jul-56
Yates AP-1	04-May-15 A	01-Feb-27
Site Regulatory	19-Oct-15 A	01-Feb-27
CCR Final Permit Effective	06-Jan-22 A	06-Jan-22 A
Front End Planning	04-May-15 A	21-Jul-16 A
Construction	04-May-15 A	08-May-24
IPCC	27-Nov-19 A	31-Jan-22 A
PCC	31-Jan-22 A	01-Feb-27
Yates AP-2	19-Oct-15 A	31-May-30
Site Regulatory	19-Oct-15 A	31-May-30
Front End Planning	01-Jan-16 A	20-Nov-19 A
Construction	05-Sep-19 A	10-May-24
IPCC	01-Jun-23 A	30-May-25
PCC	31-May-25	30-May-30
Yates AMA (AP-3/AP-B/AP-B'/AP-A)	19-Oct-15 A	08-Jul-56
Site Regulatory	19-Oct-15 A	08-Jul-56
Front End Planning	01-Jan-16 A	30-Apr-18 A
Construction	19-Aug-16 A	06-Jul-24
IPCC	08-Jul-24	08-Jul-26
PCC	08-Jul-26	08-Jul-56
Yates Gypsum Landfill	22-Jul-15 A	15-Aug-24
Site Regulatory	22-Jul-15 A	15-Aug-24
CCR Final Permit Effective	05-Jan-22 A	05-Jan-22 A
IPCC	19-Jan-17 A	14-Feb-22 A
PCC	14-Feb-22 A	15-Aug-24
Yates R-6/AP-C	29-May-15 A	28-Nov-55
Site Regulatory	29-May-15 A	28-Nov-55
Front End Planning	29-May-15 A	21-Jul-16 A
Construction	29-May-15 A	10-May-24
IPCC	28-Nov-23	26-Nov-25
PCC	26-Nov-25	27-Nov-55

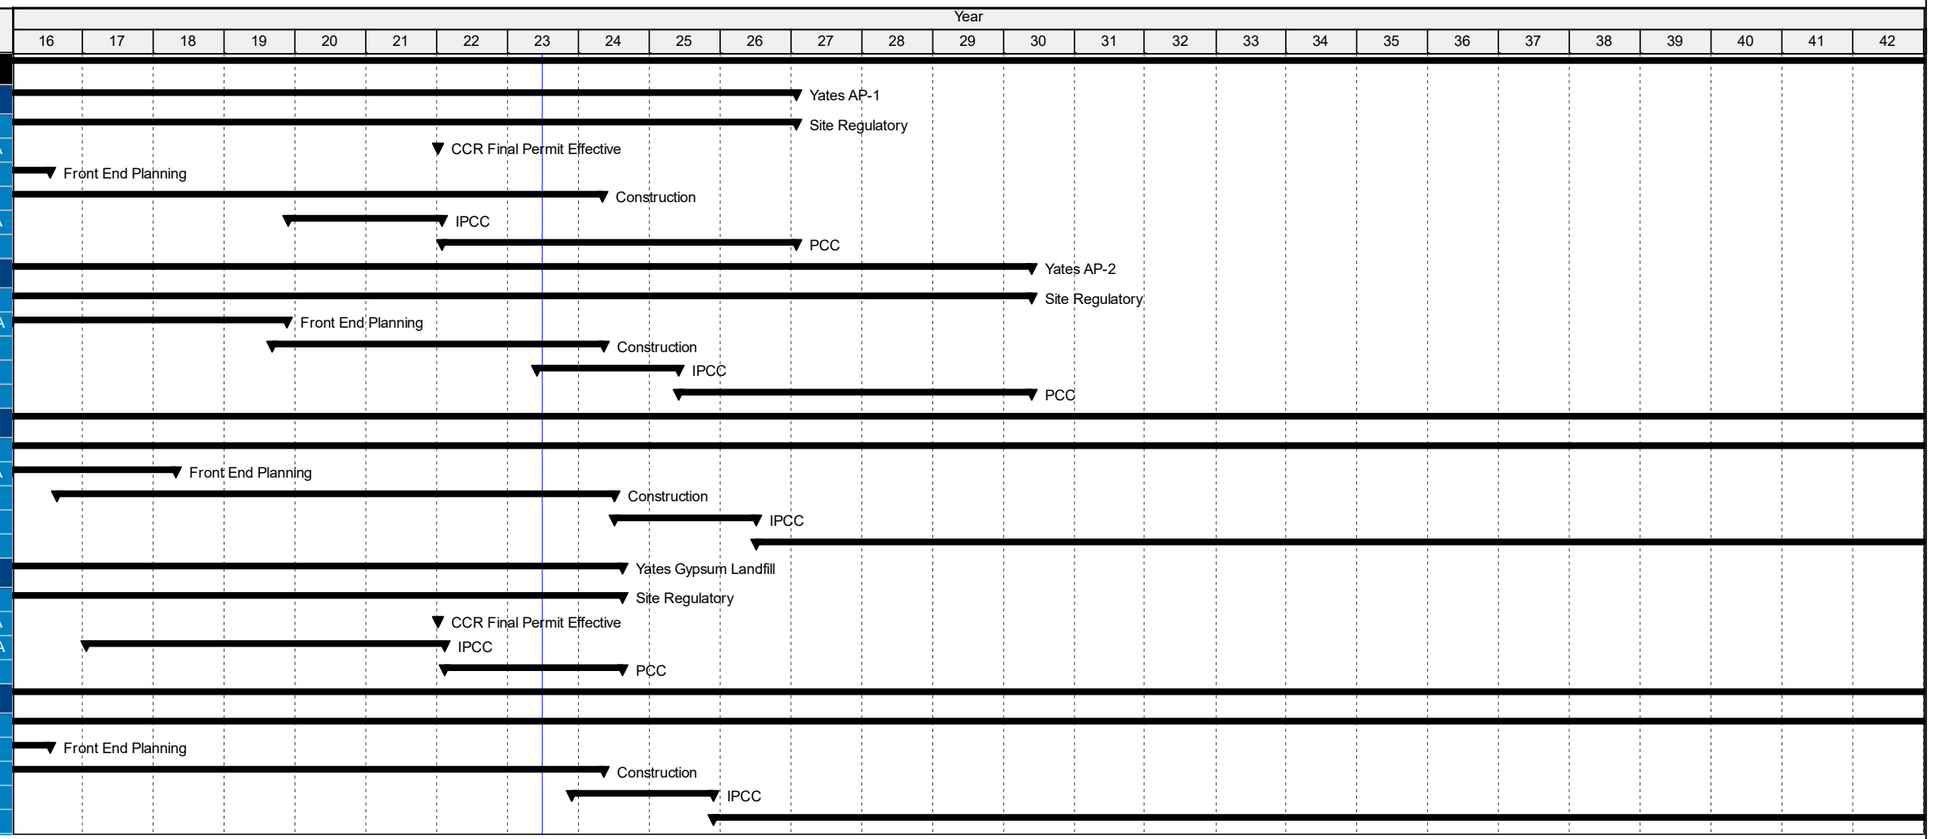

Note: This schedule forecast is consistent with the March 2024 GPC CCR ARO Semi-Annual Program Status Report; the Company is currently reviewing all years in its CCR ARO estimates and will update in the next CCR ARO semi-annual report.
