
DN 42959 STF-24-2(c) Attachment A


ID	Task Mode	Task Name	Duration	Start	Finish
1		**Phase 1: Pete Dickes to Hancock Bridge (51,000 LF)**	365 days?	Fri 11/1/24	Wed 12/31/25
2		Survey work - Phase 1	65 days	Fri 11/1/24	Wed 1/15/25
3		**Design RFP Process initiated for all phases**	45 days	Fri 11/1/24	Mon 12/23/24
4		Final review for Project Scope for Engineering firm	1 day	Mon 11/4/24	Mon 11/4/24
5		Liberty procurrement initiates RFP Process for design	0 days	Mon 11/4/24	Mon 11/4/24
6		Question/Answers Due	31 days	Mon 11/4/24	Mon 12/9/24
7		Engineering Design Bids Due	1 day	Mon 12/16/24	Mon 12/16/24
8		Engineering Design Award	1 day	Fri 12/20/24	Fri 12/20/24
9		**Engineering Design - Phase 1**	118 days	Mon 12/23/24	Thu 5/8/25
10		Engineering Design 30% - Phase 1	41 days	Mon 12/23/24	Fri 2/7/25
11		Engineering Design 60% - Phase 1	22 days	Mon 2/17/25	Thu 3/13/25
12		Engineering Design 90% - Phase 1	25 days	Tue 3/18/25	Tue 4/15/25
13		Eng Design Complete for Phase 1	11 days	Mon 4/21/25	Fri 5/2/25
14		**Construction RFP Process - Phase 1**	**45 days**	**Tue 3/18/25**	Thu 5/8/25
15		Construction RFP review and sent to vendors for Phase 1	4 days	Tue 3/18/25	Fri 3/21/25
16		Pre-Construction Meeting	0 days	Wed 4/2/25	Wed 4/2/25
17		Questions/Answers - Phase 1	14 days	Wed 4/2/25	Thu 4/17/25
18		Construction Bids Due for Phase 1	0 days	Mon 4/28/25	Mon 4/28/25
19		Award - Phase 1	1 day	Tue 4/29/25	Tue 4/29/25
20		Contract signed - Phase 1	7 days	Wed 4/30/25	Wed 5/7/25
21		**Construction Pipeline Installation (51,000 LF @ 300 LF per day)**	204 days	Thu 5/8/25	Wed 12/31/25
22		Survey work - Phase 2 & 3	117 days	Wed 1/15/25	Fri 5/30/25
23		**Engineering Design - Phase 2 & 3**	**169 days**	**Fri 5/2/25**	**Fri 11/14/25**
24		Engineering Design 30% - Phase 2 & 3	88 days	Fri 5/2/25	Tue 8/12/25
25		Engineering Design 60% - Phase 2 & 3	28 days	Tue 8/12/25	Fri 9/12/25
26		Engineering Design 90% - Phase 2 & 3	27 days	Fri 9/12/25	Mon 10/13/25
27		Eng Design Complete for Phase 2 & 3	29 days	Mon 10/13/25	Fri 11/14/25
28		**Phase 2: Hancock Bridge to Ward Rd (29,702 LF)**	**405 days**	**Tue 9/16/25**	Thu 12/31/26
29		**Construction RFP Process - Phase 2 (29,702 LF)**	**66 days**	**Tue 9/16/25**	Mon 12/1/25
30		Construction RFP review and sent to vendors for Phase 1	1 day	Tue 9/16/25	Tue 9/16/25
31		Pre-Construction Meeting	0 days	Tue 9/30/25	Tue 9/30/25

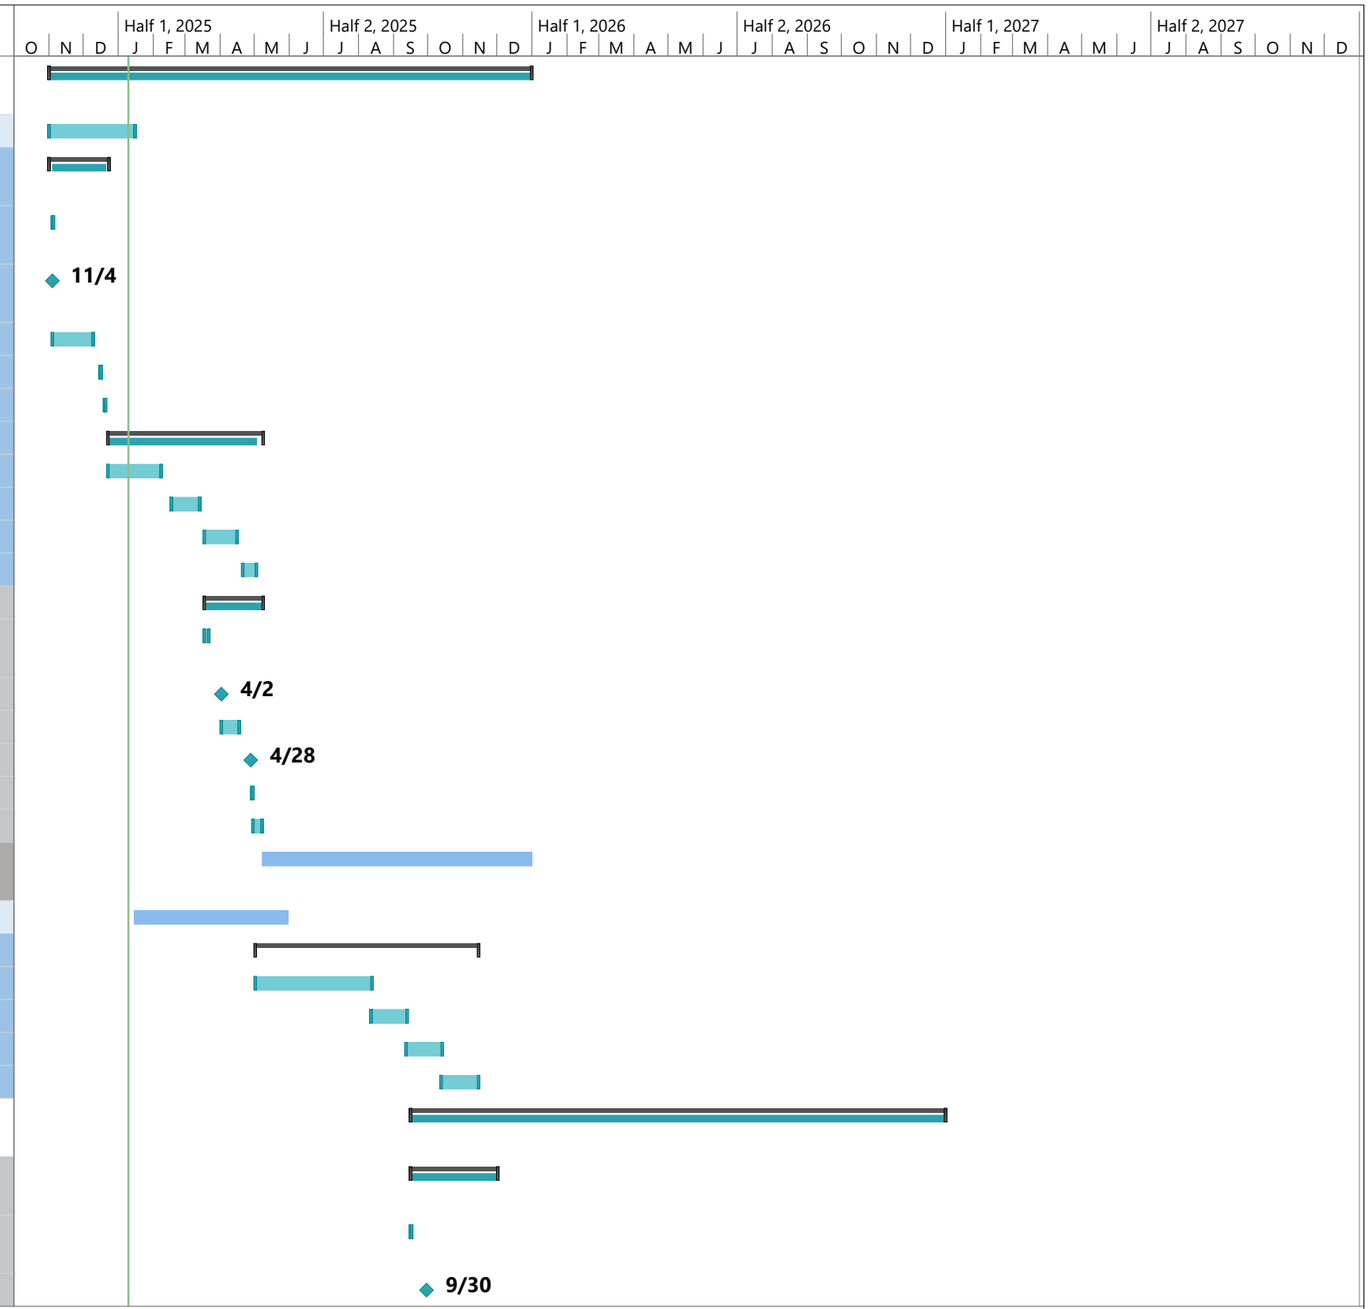

Project: AGTL Gantt Chart
Date: Fri 1/10/25

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone

ID	Task Mode	Task Name	Duration	Start	Finish
32		Questions/Answers - Phase 2	27 days	Tue 9/30/25	Thu 10/30/25
33		Construction Bids Due for Phase 1	14 days	Thu 10/30/25	Fri 11/14/25
34		Award - Phase 1	14 days	Thu 11/13/25	Fri 11/28/25
35		Contract signed - Phase 1	3 days	Fri 11/28/25	Mon 12/1/25
36		**Construction Pipeline Installation - Phase 2 (29,702 LF)**	313 days	Thu 1/1/26	Thu 12/31/26
37		**Phase 3: Ward Rd to Roy Parks Rd (35,298 LF)**	**405 days**	**Wed 9/16/26**	**Fri 12/31/27**
38		**Construction RFP Process - Phase 3 (35,298 LF)**	**77 days**	**Wed 9/16/26**	Mon 12/14/26
39		Construction RFP review and sent to vendors for Phase 3	**0 days**	**Wed 9/16/26**	Wed 9/16/26
40		Pre-Construction Meeting	1 day	Wed 9/30/26	Wed 9/30/26
41		Questions/Answers - Phase 3	0 days	Wed 9/30/26	Wed 9/30/26
42		Construction Bids Due for Phase 1	27 days	Fri 10/30/26	Mon 11/30/26
43		Award - Phase 1	14 days	Fri 11/13/26	Sat 11/28/26
44		Contract signed - Phase 1	14 days	Sat 11/28/26	Mon 12/14/26
45		**Construction Pipeline Installation - Phase 3 (29,702 LF)**	287 days	Fri 1/1/27	Wed 12/1/27

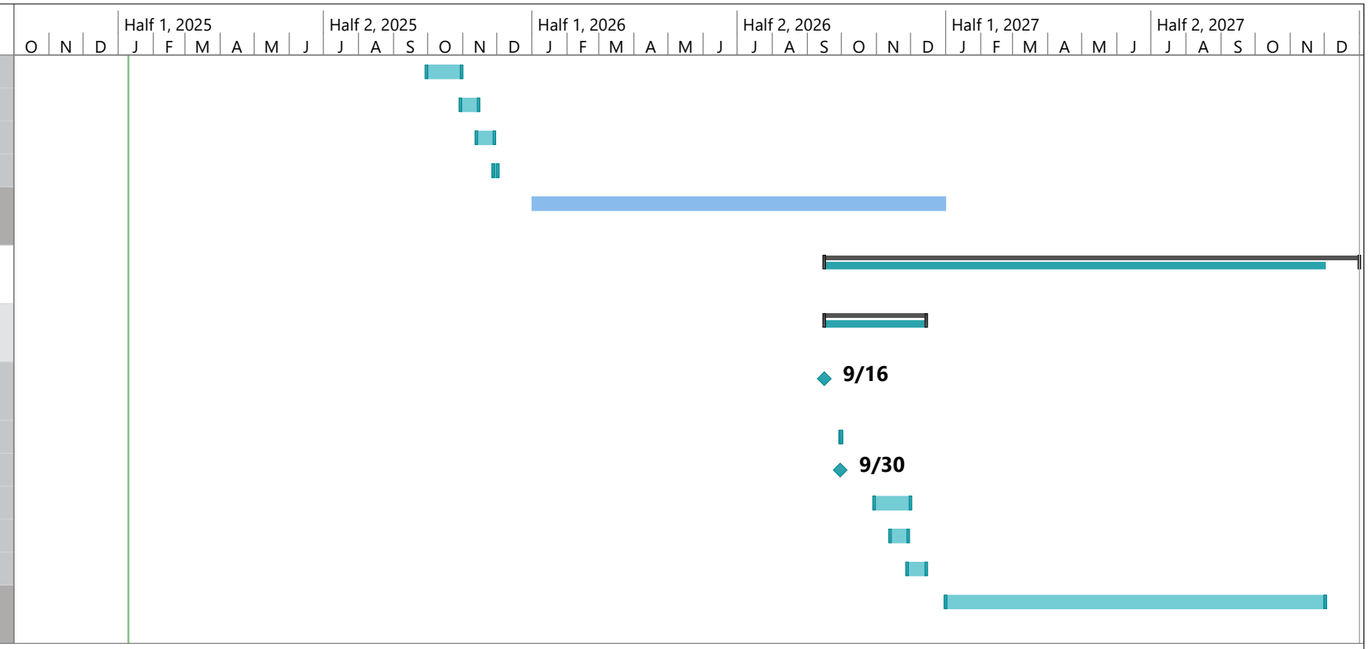

Project: AGTL Gantt Chart
Date: Fri 1/10/25

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone
