

Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Arkwright CCR	19-Oct-15 A	11-Feb-39
Arkwright CCR	19-Oct-15 A	11-Feb-39
AP-1	19-Oct-15 A	10-Aug-38
Site Regulatory	19-Oct-15 A	10-Aug-38
Front End Planning	01-Jan-16 A	10-Feb-26
Construction	01-Jun-23 A	17-May-32
IPCC	11-Aug-31	10-Aug-33
PCC	10-Aug-33	10-Aug-38
AP-2 DAS	19-Oct-15 A	13-Mar-36
Site Regulatory	19-Oct-15 A	13-Mar-36
Front End Planning	01-Jan-16 A	10-Feb-26
Construction	14-Apr-26	17-May-32
IPCC	13-Mar-29	16-Mar-31
PCC	16-Mar-31	13-Mar-36
AP-3	01-Jan-16 A	11-Feb-39
Site Regulatory	20-Nov-18 A	11-Feb-39
Front End Planning	01-Jan-16 A	10-Feb-26
Construction/Active/Close&Cap	14-Apr-26	17-May-32
IPCC	12-Feb-32	13-Feb-34
PCC	13-Feb-34	10-Feb-39

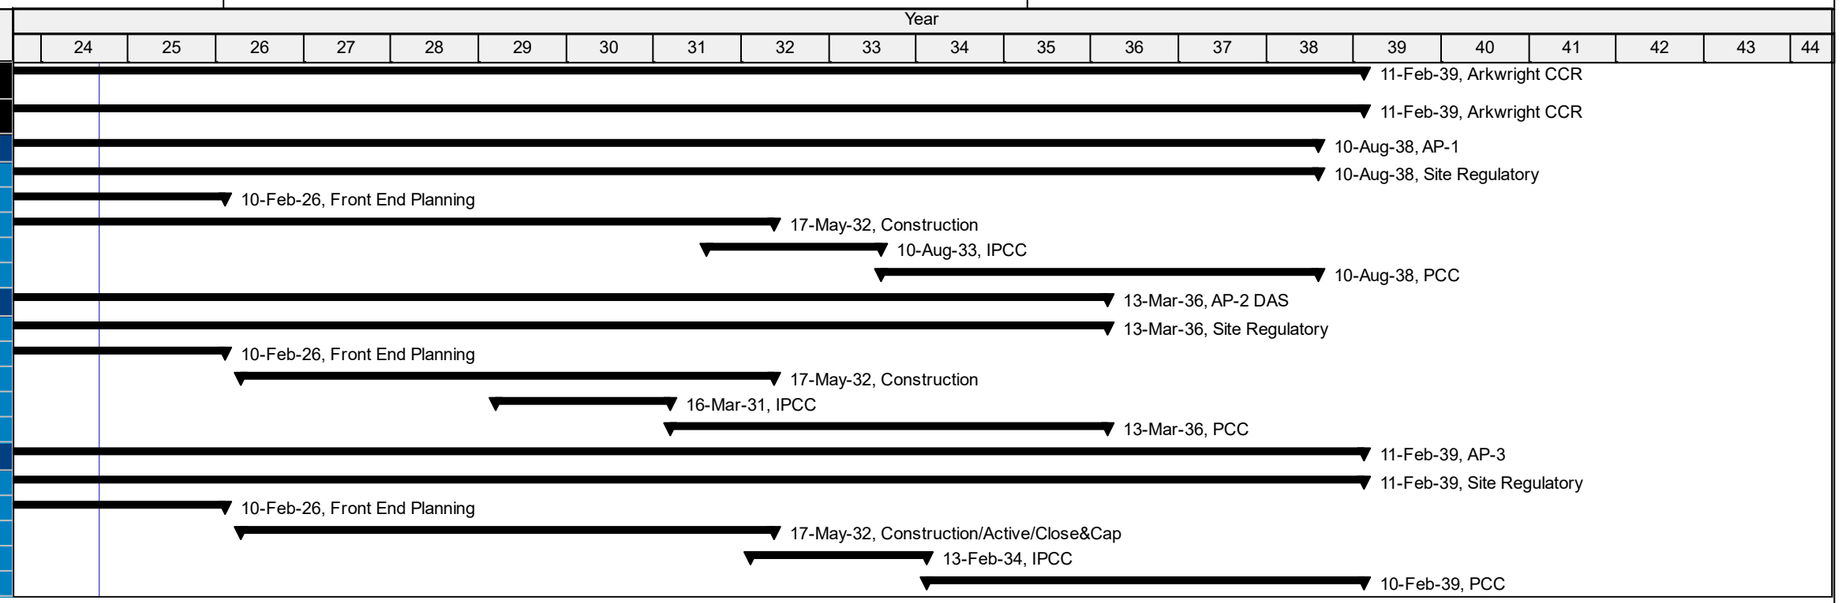


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Bowen CCR	12-May-08 A	24-Mar-72
Bowen CCR	12-May-08 A	24-Mar-72
AP-1	19-Oct-15 A	18-Oct-68
Site Regulatory	19-Oct-15 A	18-Oct-68
CCR Final Permit Effective	17-Feb-22 A	17-Feb-22 A
Front End Planning	01-Jan-16 A	08-Dec-20 A
Construction	14-Dec-17 A	20-Oct-36
IPCC	21-Oct-36	19-Oct-38
PCC	19-Oct-38	18-Oct-68
Bowen Landfill	12-May-08 A	01-Jan-72
Site Regulatory	12-May-08 A	01-Jan-72
CCR Final Permit Effective	08-Dec-22 A	08-Dec-22 A
LF Cells 1 & 2	02-Jan-20 A	01-Jan-72
Active Landfill	02-Jan-20 A	31-Dec-37
Cell Closure/Capping	01-Jan-38	30-Dec-39
IPCC	31-Dec-39	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 3 & 4	02-Jan-20 A	01-Jan-72
Active Landfill	02-Jan-20 A	31-Mar-23 A
Cell Closure/Capping	31-Mar-23 A	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 5 & 6	29-Apr-22 A	24-Mar-72
Construction/Active for Closure	29-Apr-22 A	23-Mar-40
Cell Closure/Capping	25-Mar-38	24-Mar-40
IPCC	24-Mar-40	25-Mar-42
PCC	25-Mar-42	24-Mar-72
LF Cells 7 & 8	01-Jan-30	01-Jan-72
Active Landfill	01-Jan-30	31-Dec-37
Cell Closure/Capping	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	01-Jan-72
LF Cells 9 & 10	01-Jan-23 A	01-Jan-72
Active Landfill	01-Jan-23 A	31-Dec-31
Cell Closure/Capping	01-Jan-32	31-Dec-33
IPCC	01-Jan-34	31-Dec-41
PCC	01-Jan-42	01-Jan-72

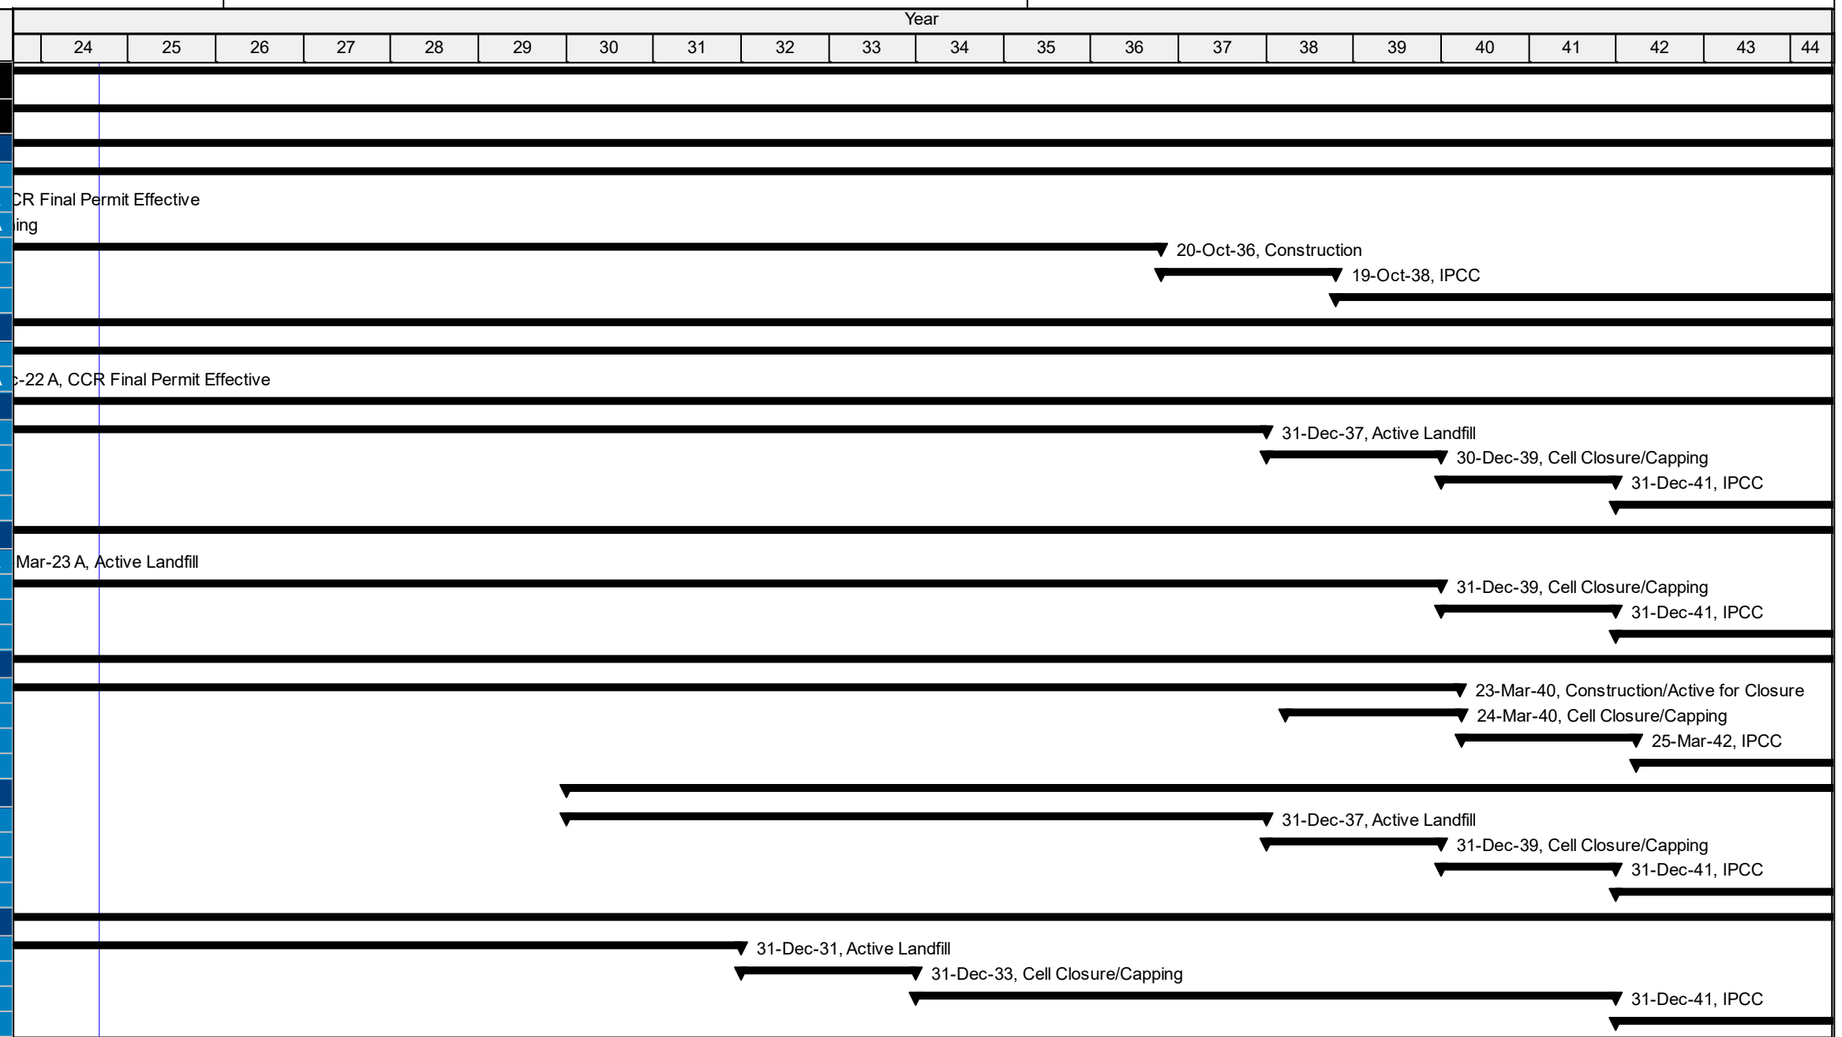


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Branch CCR	19-Oct-15 A	25-May-73
Branch CCR	19-Oct-15 A	25-May-73
AP-B/AP-C/AP-D	19-Oct-15 A	24-Sep-46
Site Regulatory	19-Oct-15 A	24-Sep-46
PCC	23-Sep-41	22-Sep-46
AP-B	17-Sep-25	22-Sep-41
Site Regulatory	22-Sep-39	21-Dec-39
Front End Planning	17-Sep-25	16-Jun-36
Construction	29-May-26	29-Jun-40
IPCC	23-Sep-39	22-Sep-41
AP-C	15-Jun-29	22-Sep-41
Site Regulatory	24-Dec-36	24-Mar-37
Front End Planning	15-Jun-29	13-Dec-29
Construction	28-Feb-30	01-Sep-37
IPCC	25-Dec-36	22-Sep-41
AP-D	05-Sep-24	22-Sep-41
Site Regulatory	10-Jun-30	08-Sep-30
Front End Planning	05-Sep-24	19-Mar-26
Construction	01-May-25	04-Jun-31
IPCC	11-Jun-30	22-Sep-41
AP-E	19-Oct-15 A	23-Sep-46
Site Regulatory	19-Oct-15 A	23-Sep-46
Front End Planning	01-Jan-16 A	23-Oct-25
Construction	01-Mar-19 A	17-Jun-41
IPCC	23-Sep-39	22-Sep-41
PCC	23-Sep-41	23-Sep-46
Branch LF	01-Jan-16 A	25-May-73
Site Regulatory	28-Feb-17 A	25-May-73
CCR Final Permit Effective	25-Jan-23 A	25-Jan-23 A
Front End Planning	01-Jan-16 A	12-Jul-23 A
Construction/Active/Close&Cap	10-Apr-23 A	17-Jun-41
IPCC	25-May-41	24-May-43
PCC	25-May-43	24-May-73
Beneficial Use	12-Jun-23 A	14-Jun-41

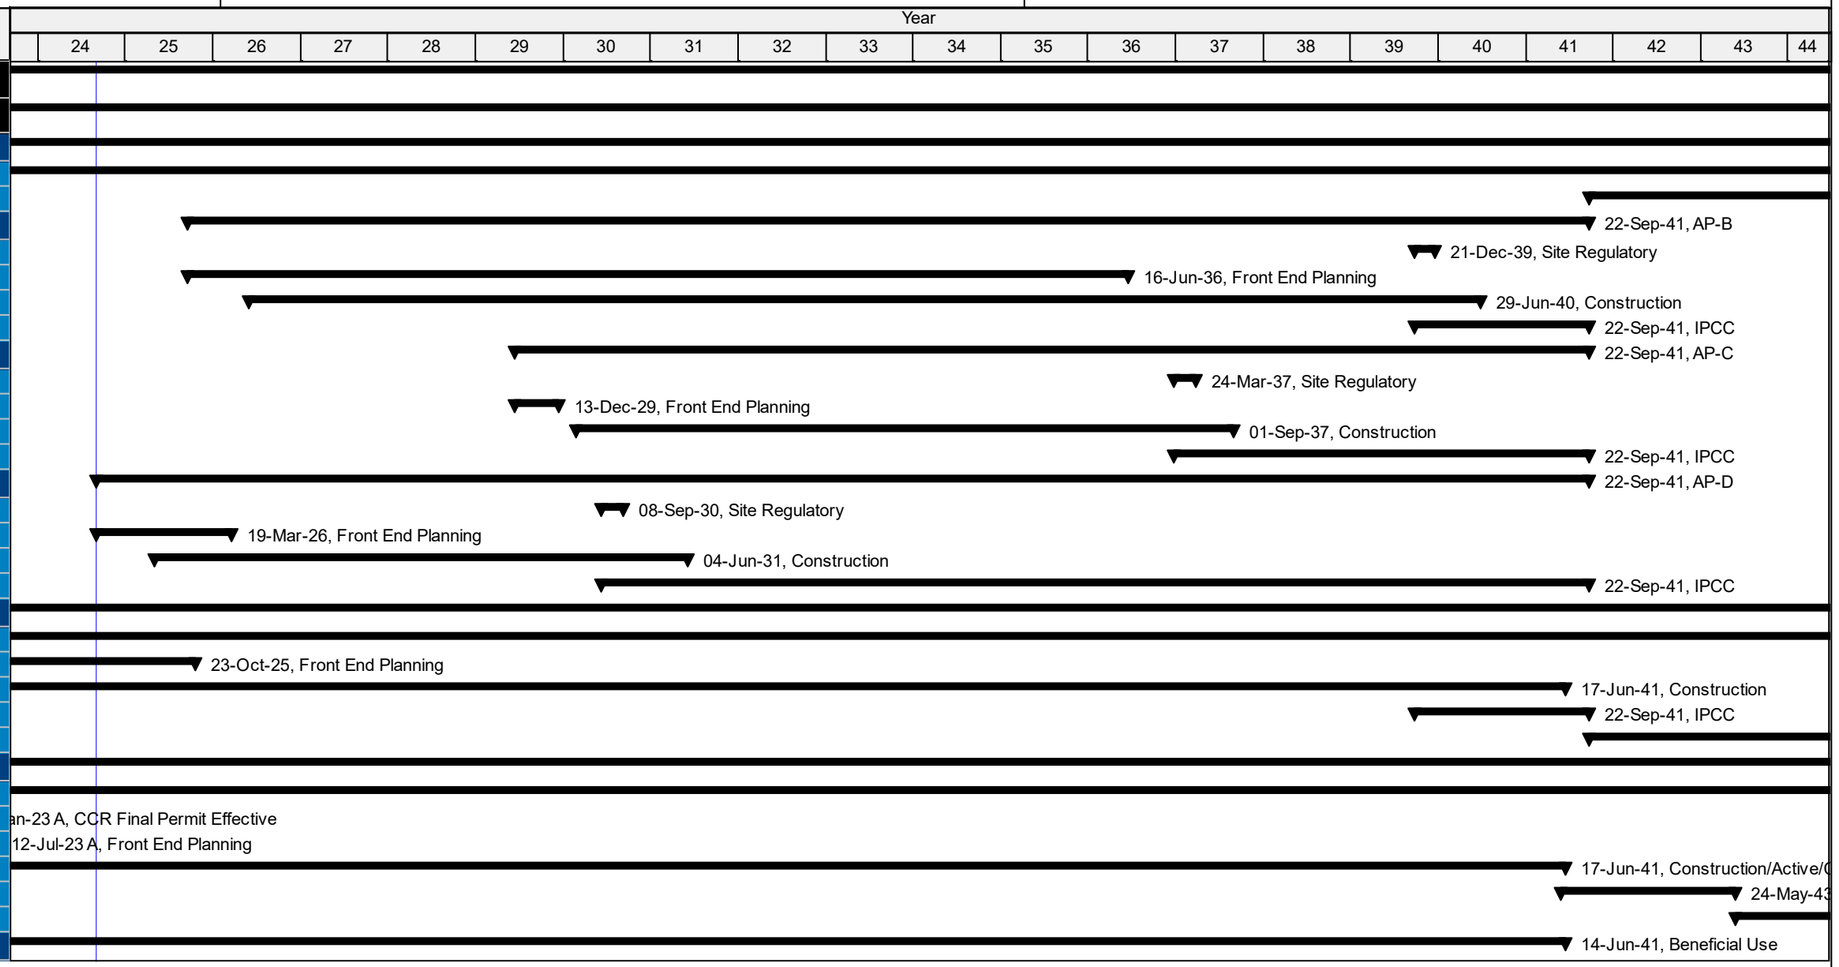


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Hammond CCR	01-Jan-08 A	21-Dec-65
Hammond CCR	01-Jan-08 A	21-Dec-65
AP-1	19-Oct-15 A	21-Aug-32
Site Regulatory	19-Oct-15 A	23-Aug-27
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	11-Jan-21 A	30-Jul-26
IPCC	22-Aug-25	21-Aug-27
PCC	23-Aug-27	21-Aug-32
AP-2	19-Oct-15 A	02-Oct-31
Site Regulatory	19-Oct-15 A	02-Oct-31
CCR Final Permit Effective	22-Jun-20 A	22-Jun-20 A
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	04-Jan-21 A	27-Aug-25
IPCC	01-Oct-24	01-Oct-26
PCC	01-Oct-26	01-Oct-31
AP-3	19-Oct-15 A	05-Sep-54
Site Regulatory	19-Oct-15 A	04-Sep-54
CCR Final Permit Effective	01-Jan-24 A	01-Jan-24 A
Front End Planning	01-Jan-16 A	25-May-16 A
Construction	26-May-16 A	30-Oct-24
IPCC	13-Nov-18 A	05-Sep-24
PCC	05-Sep-24	05-Sep-54
AP-4	19-Oct-15 A	13-Jun-40
Site Regulatory	19-Oct-15 A	13-Jun-40
CCR Final Permit Effective	27-Jan-21 A	27-Jan-21 A
Front End Planning	01-Jan-16 A	01-Nov-27
Construction	11-Jan-21 A	20-Apr-34
IPCC	14-Jun-33	13-Jun-35
PCC	14-Jun-35	12-Jun-40
Huffaker Rd LF	01-Jan-08 A	21-Dec-65
Site Regulatory	01-Jan-08 A	21-Dec-65
Huffaker Rd A/B	01-Jan-08 A	20-Dec-65
Active Landfill	01-Jan-08 A	21-May-26
Cell Closure/Capping	22-May-24 A	11-Feb-26
IPCC	20-Feb-26	20-Dec-35
PCC	21-Dec-35	20-Dec-65
Huffaker Rd Cell E	05-Aug-27	20-Dec-65
Active Landfill	21-Feb-33	26-Aug-33
Cell/Closure Capping	05-Aug-27	20-Mar-34
IPCC	20-Dec-33	20-Dec-35
PCC	21-Dec-35	20-Dec-65
Huffaker Rd Cell F	29-Jul-25	20-Dec-65
Front End Planning	29-Jul-25	16-Apr-26
Construction/Active/Close&Cap	13-May-26	21-Mar-34

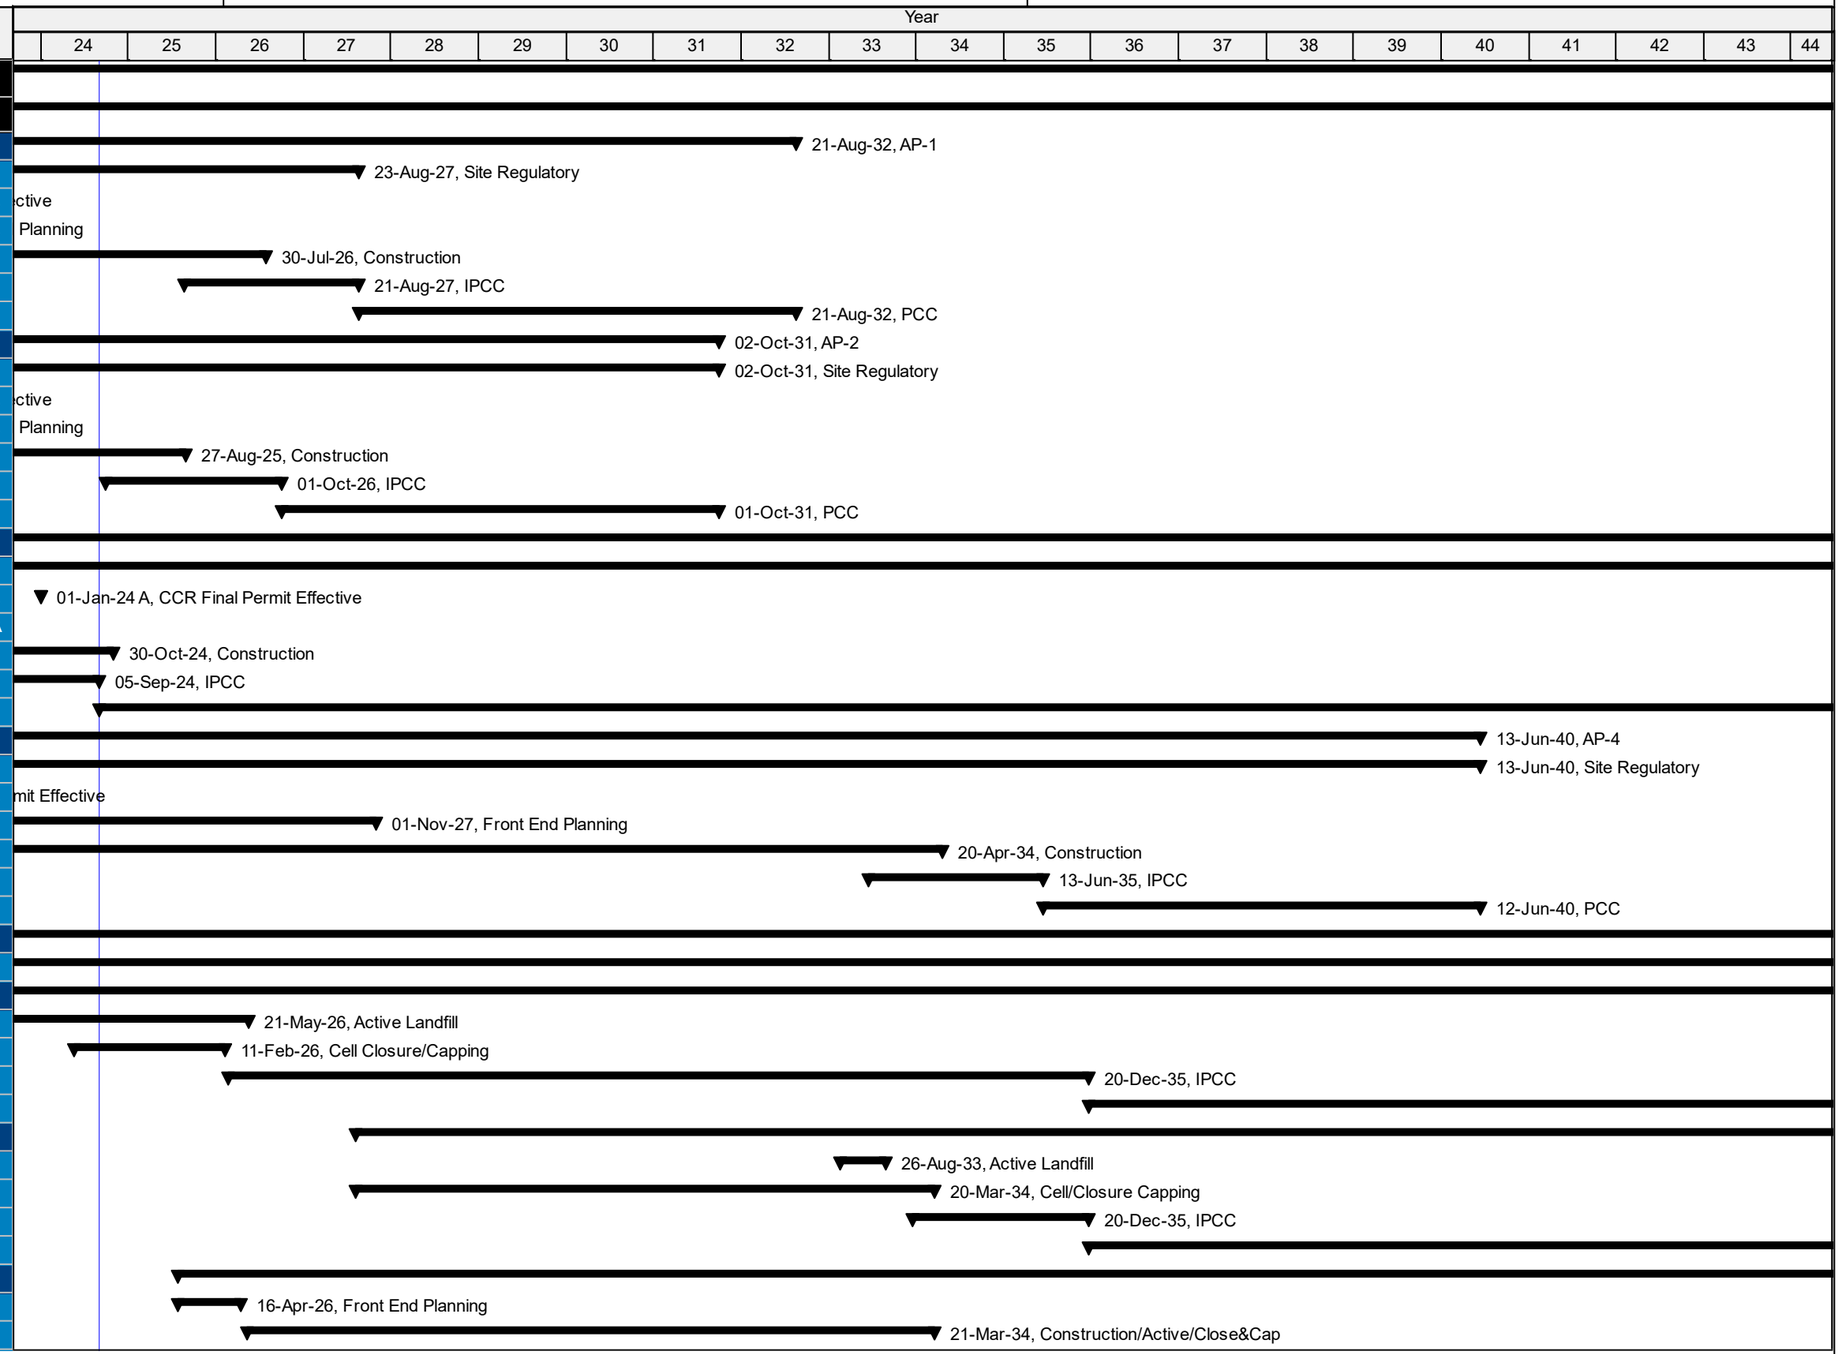


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
IPCC	21-Dec-33	20-Dec-35
PCC	21-Dec-35	20-Dec-65




Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Kraft CCR	19-Oct-15 A	11-Oct-55
Kraft CCR	19-Oct-15 A	11-Oct-55
Grumman Rd.	19-Oct-15 A	11-Oct-55
Site Regulatory	19-Oct-15 A	11-Oct-55
Front End Planning	05-Nov-15 A	01-Aug-23 A
Construction	27-Feb-17 A	29-Feb-24 A
IPCC	03-Jan-20 A	07-Oct-25
PCC	08-Oct-25	09-Oct-55

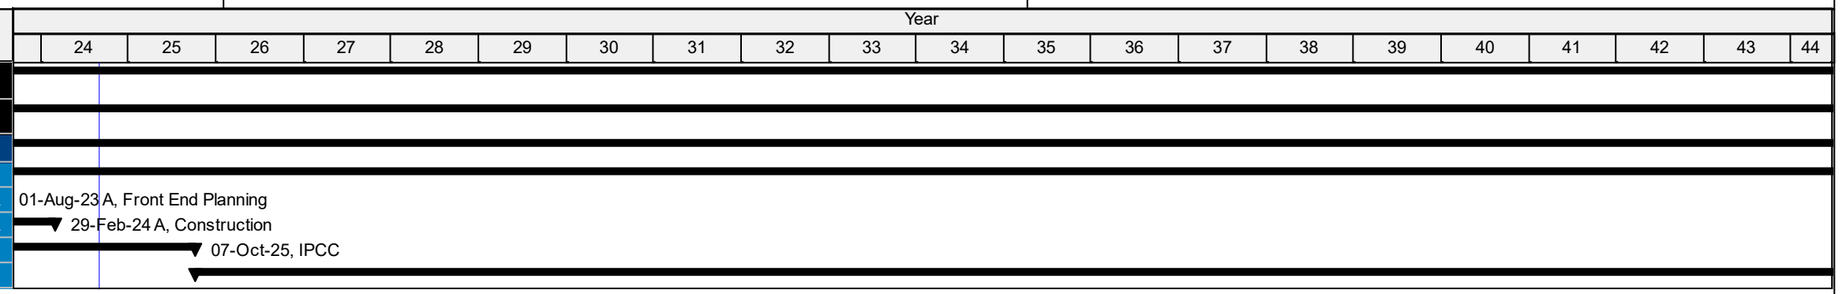


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
McDonough CCR	19-Oct-15 A	08-Oct-58
McDonough CCR	19-Oct-15 A	08-Oct-58
AP-1	19-Oct-15 A	08-Oct-58
Site Regulatory	19-Oct-15 A	08-Oct-58
Front End Planning	01-Jan-16 A	16-Jul-25
Construction	18-Jan-16 A	08-Oct-26
IPCC	09-Oct-26	10-Oct-28
PCC	10-Oct-28	08-Oct-58
AP-2/AP-3/AP-4	19-Oct-15 A	18-Jun-57
Site Regulatory	19-Oct-15 A	18-Jun-57
Front End Planning	01-Jan-16 A	12-Feb-16 A
Construction	19-Jan-16 A	17-Oct-25
IPCC	19-Jun-25	21-Jun-27
PCC AP-2/3/4	21-Jun-27	18-Jun-57

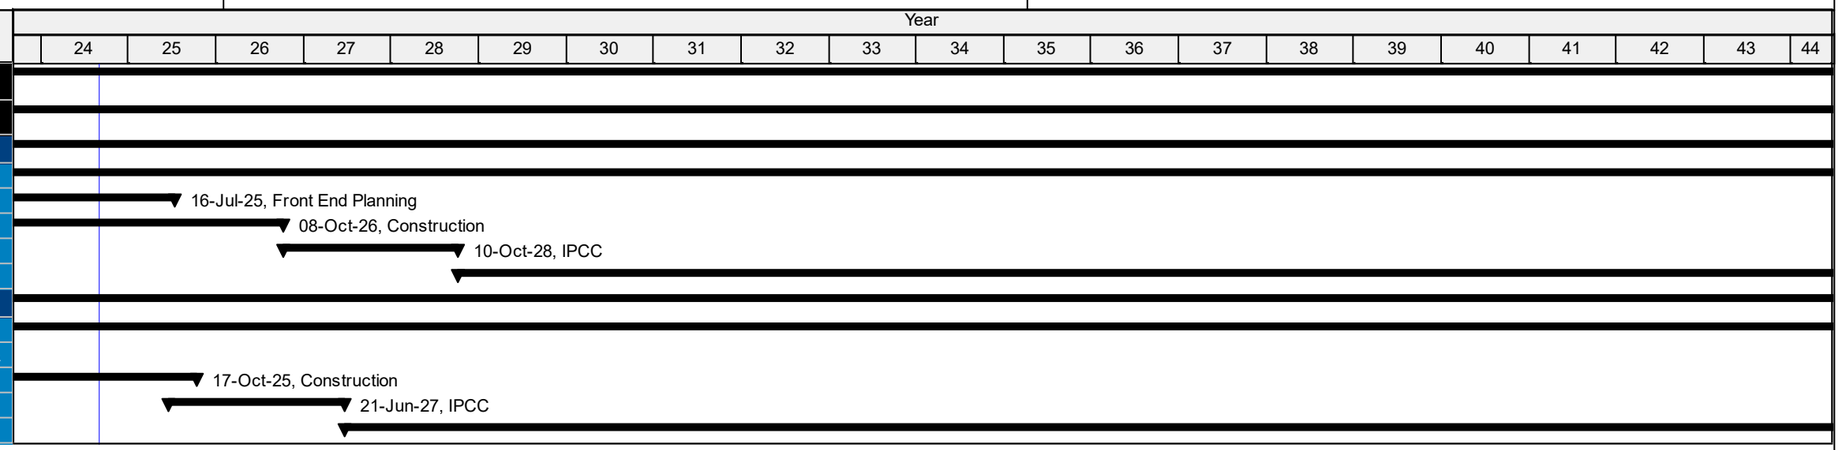


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
McIntosh CCR	21-Mar-08 A	14-Oct-55
McIntosh CCR	21-Mar-08 A	14-Oct-55
AP-1	19-Oct-15 A	05-Oct-26
Site Regulatory	19-Oct-15 A	05-Oct-26
CCR Final Permit Effective	06-Feb-20 A	06-Feb-20 A
Front End Planning	01-Jan-16 A	06-Feb-20 A
Construction	01-Oct-19 A	06-Jul-22 A
IPCC	08-Sep-21 A	05-Oct-21 A
PCC	06-Oct-21 A	05-Oct-26
LF3	21-Mar-08 A	22-Mar-38
Site Regulatory	21-Mar-08 A	22-Mar-38
CCR Draft Permit	31-Jan-23 A	31-Jan-23 A
PCC	21-Mar-08 A	21-Mar-38
LF4	19-Oct-15 A	14-Oct-55
Site Regulatory	19-Oct-15 A	14-Oct-55
CCR Draft Permit	24-Feb-23 A	24-Feb-23 A
LF4 Cell 1	27-Nov-18 A	14-Oct-55
IPCC	27-Nov-18 A	14-Oct-25
PCC	14-Oct-25	14-Oct-55
LF4 Cell 2A	23-Feb-21 A	14-Oct-55
Construct/Active/Close&Cap	23-Feb-21 A	15-Mar-23 A
IPCC	20-Oct-22 A	14-Oct-25
PCC	14-Oct-25	14-Oct-55

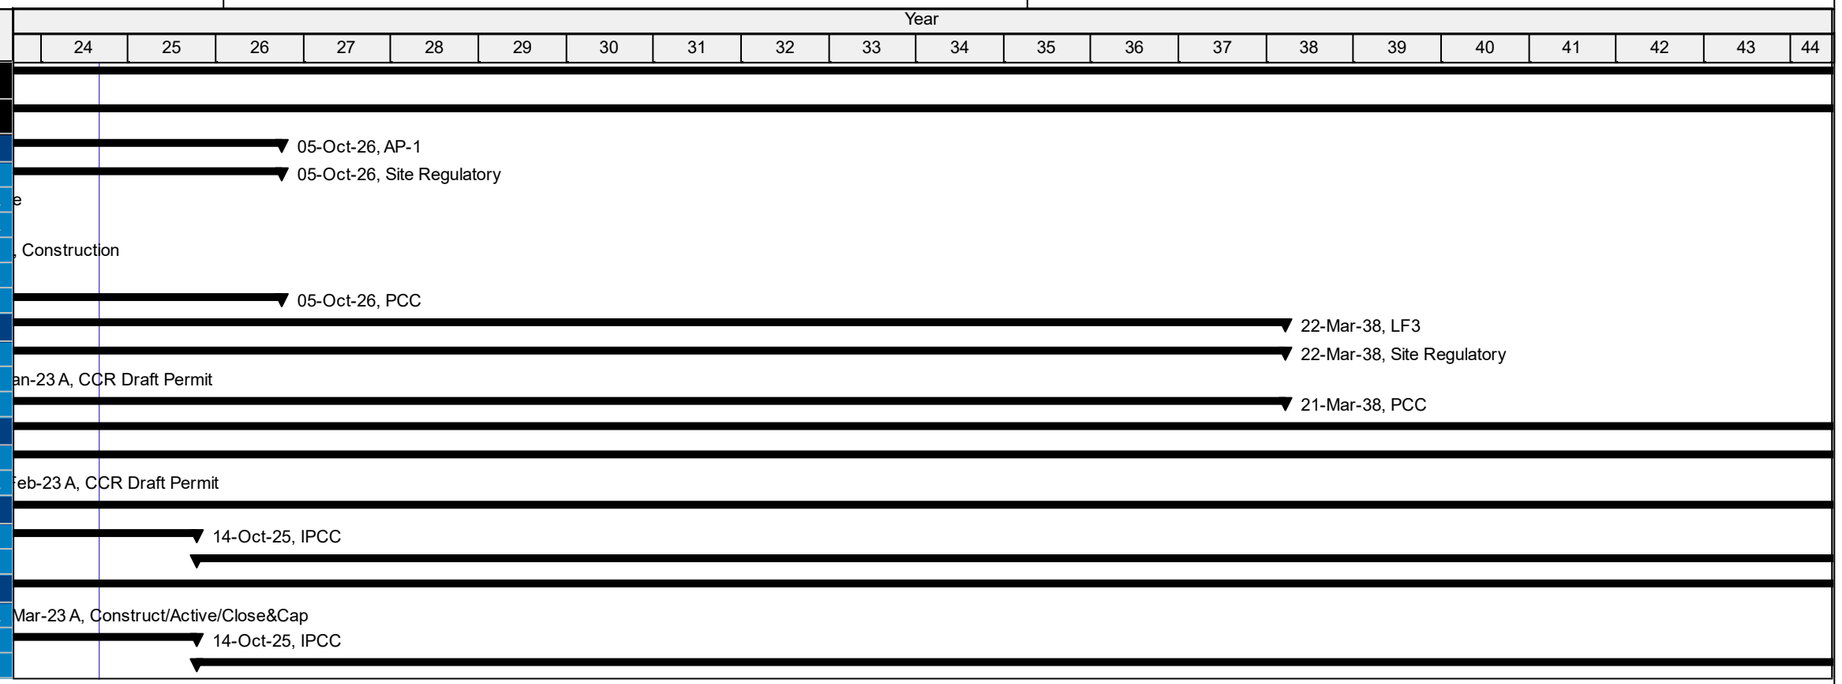


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
McManus CCR	19-Oct-15 A	18-Jun-36
McManus CCR	19-Oct-15 A	18-Jun-36
McManus AP-1	19-Oct-15 A	18-Jun-36
Site Regulatory	19-Oct-15 A	18-Jun-36
CCR Final Permit Effective	18-Jun-21 A	18-Jun-21 A
Front End Planning	01-Jan-16 A	08-Dec-16 A
Construction	22-Jan-16 A	28-Jul-20 A
IPCC	28-Nov-19 A	18-Jun-21 A
PCC	18-Jun-21 A	18-Jun-36

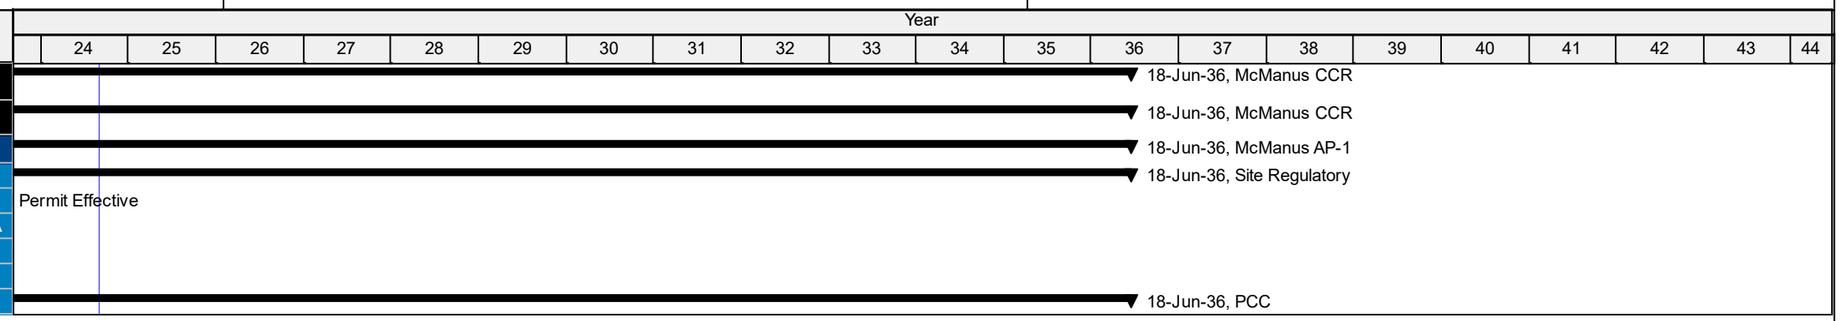


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Mitchell CCR	19-Oct-15 A	25-Apr-35
Mitchell CCR	19-Oct-15 A	25-Apr-35
Mitchell AP-1/AP-2/AP-A	19-Oct-15 A	25-Apr-35
Site Regulatory	19-Oct-15 A	25-Apr-35
CCR Final Permit Effective	28-Jun-22 A	28-Jun-22 A
Front End Planning	01-Jan-16 A	19-Feb-21 A
Construction	17-Sep-19 A	23-Apr-28
IPCC	23-Apr-28	24-Apr-30
PCC	25-Apr-30	23-Apr-35

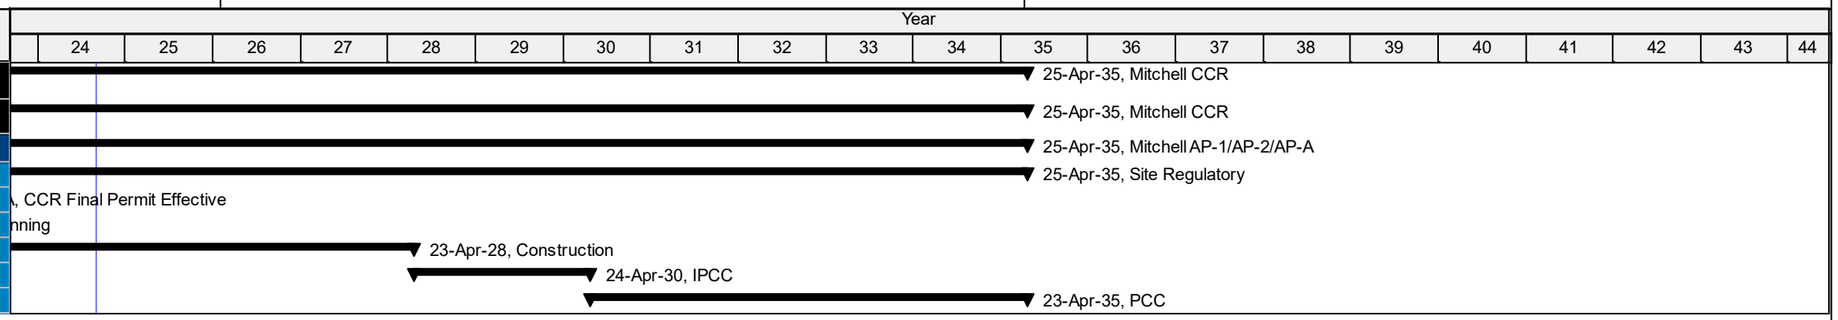


Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Scherer CCR	01-Jan-10 A	01-Jan-79
Scherer CCR	01-Jan-10 A	01-Jan-79
Scherer AP-1	19-Oct-15 A	17-Jun-65
Site Regulatory	19-Oct-15 A	17-Jun-65
Front End Planning	01-Jan-16 A	28-Jan-26
Construction	06-Jul-21 A	22-Jun-33
IPCC	18-Jun-33	17-Jun-35
PCC	18-Jun-35	17-Jun-65
Scherer LF	01-Jan-10 A	01-Jan-79
Site Regulatory	01-Jan-10 A	01-Jan-79
PCC	02-Jan-20 A	10-Mar-50
LF Cell 1	02-Jan-20 A	31-Dec-78
Active Landfill	02-Jan-20 A	31-Dec-44
Cell Closure/Capping	31-Dec-44	31-Dec-46
IPCC	31-Dec-46	30-Dec-48
PCC	30-Dec-48	31-Dec-78
PAC/ASH CELL	02-Jan-20 A	01-Jan-79
Active Landfill	02-Jan-20 A	31-Dec-26
Cell Closure/Capping	31-Dec-26	31-Dec-28
IPCC - PAC/Ash Cell	31-Dec-28	31-Dec-48
PCC (+30 Years) - PAC/Ash Cell	31-Dec-48	01-Jan-79

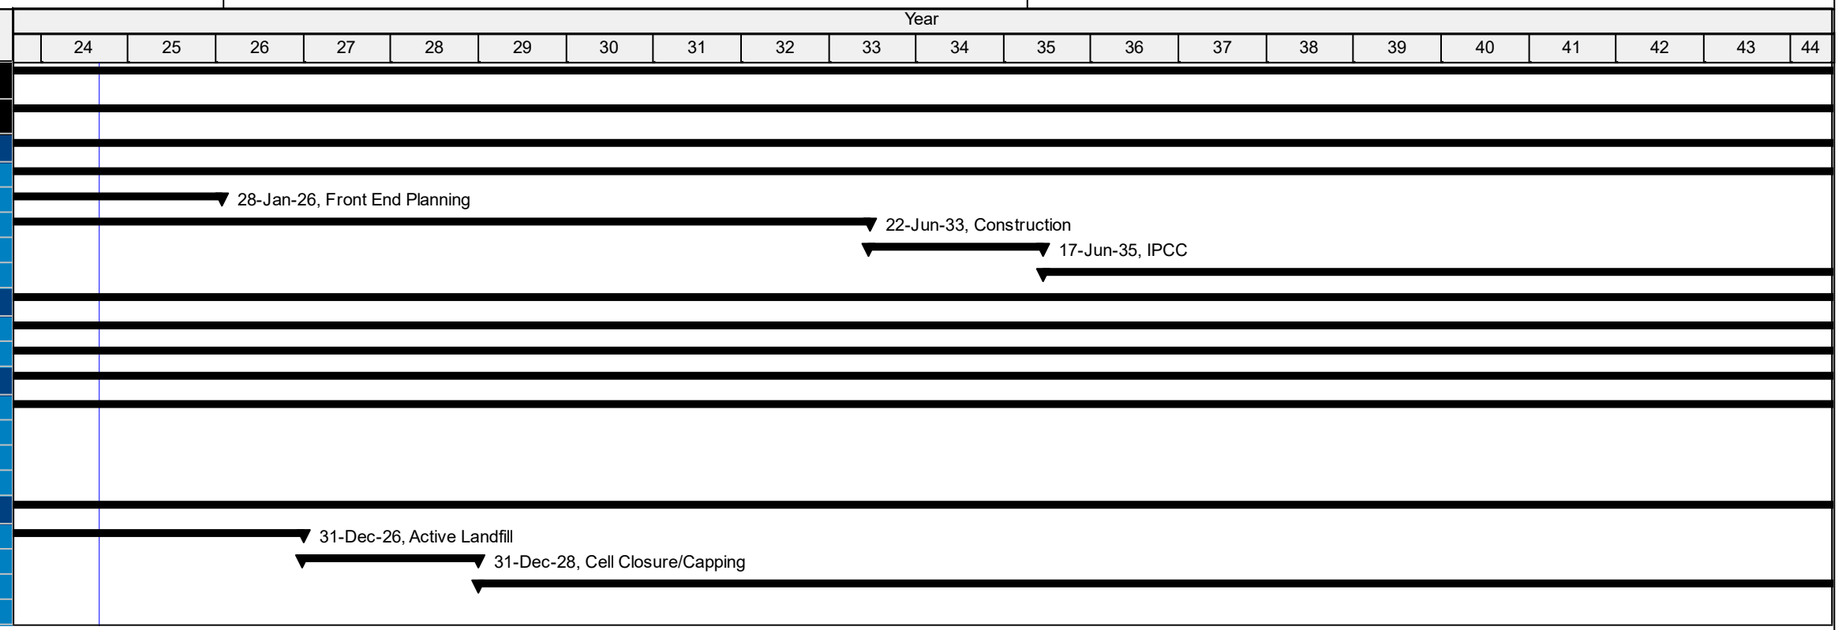

Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Wansley CCR	01-Jan-12 A	28-Jun-67
Wansley CCR	01-Jan-12 A	28-Jun-67
Wansley AP-1	19-Oct-15 A	26-Oct-41
Site Regulatory	19-Oct-15 A	26-Oct-41
Front End Planning	01-Jan-16 A	26-Aug-24 A
Construction	19-Apr-21 A	02-May-35
IPCC	26-Oct-34	26-Oct-36
PCC	26-Oct-36	26-Oct-41
Wansley Landfill	01-Jan-12 A	28-Jun-67
Site Regulatory	01-Jan-12 A	28-Jun-67
CCR Final Permit Effective LF Cell 1	07-Jan-23 A	07-Jan-23 A
Front End Planning	22-Jul-22 A	19-Feb-26
Construct Cell/Active for Closure	29-Jan-24 A	27-Oct-26
Cell Closure/Capping	19-Apr-34	19-Apr-34
Landfill Cells 1/2/3	01-Jan-12 A	28-Jun-67
Active for Closure	01-Jan-12 A	20-Mar-30
Cell Closure/Capping	26-Aug-24 A	28-Jun-35
IPCC	28-Jun-35	28-Jun-37
PCC	28-Jun-37	28-Jun-67
Landfill Cell 4	04-Jun-26	28-Jun-67
Site Regulatory	04-Jun-26	24-Aug-26
Construct Cell/Active for Closure	24-Aug-26	18-Aug-28
Cell Closure/Capping	28-Oct-26	28-Jun-35
IPCC	28-Jun-35	28-Jun-37
PCC	28-Jun-37	28-Jun-67

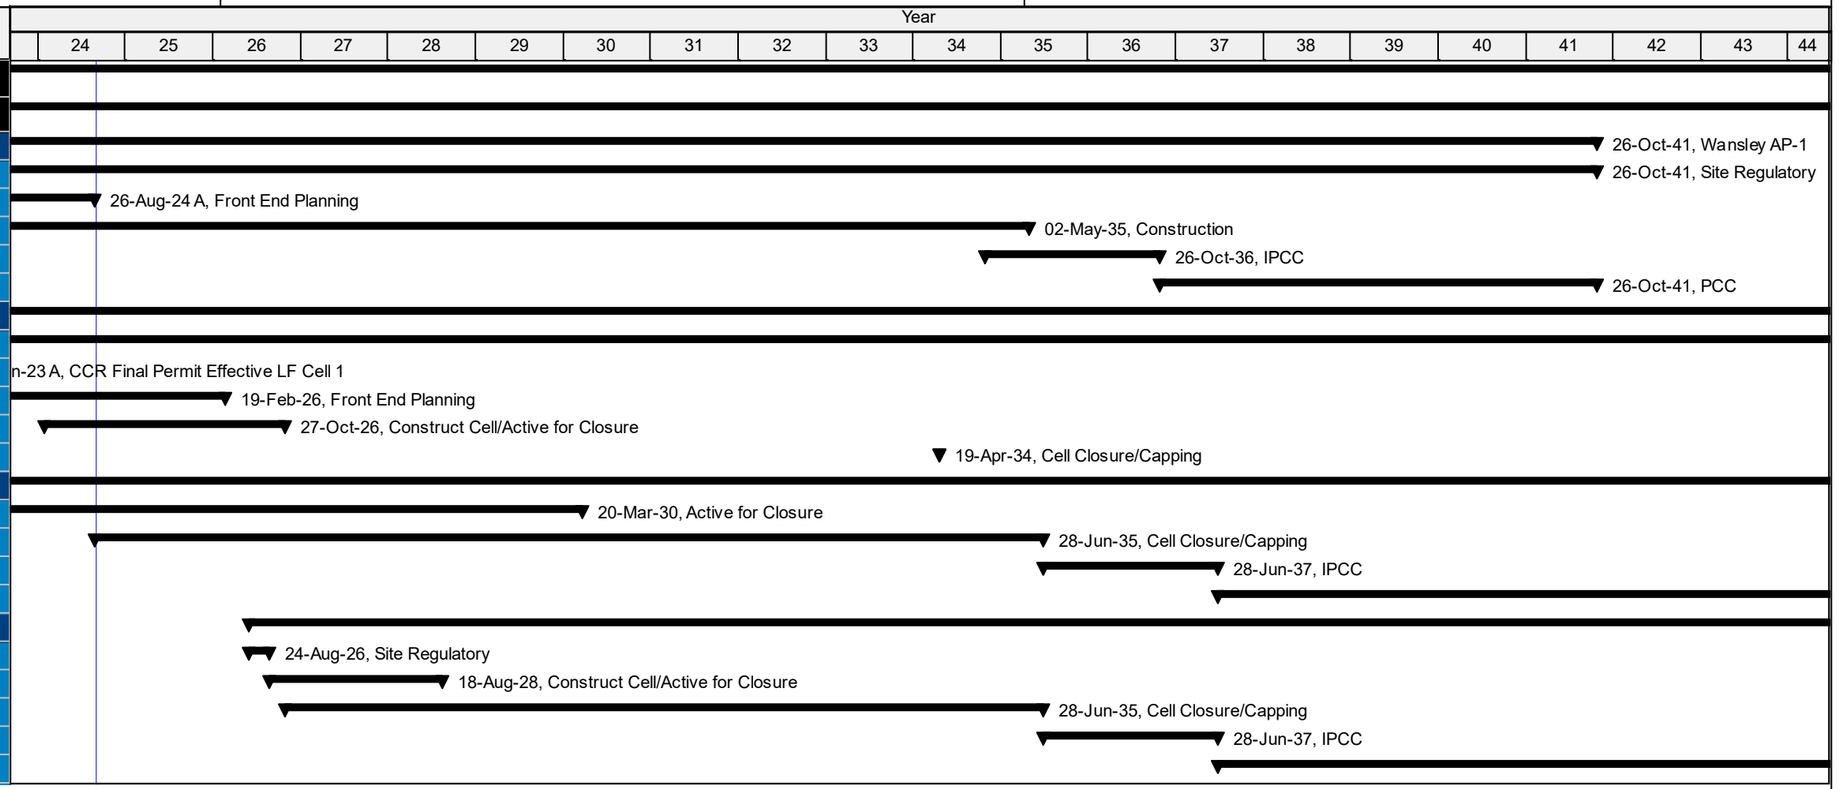

Ash Pond Closure Portfolio - 1Q25
Gantt Chart by Plant

Activity ID	Start	Finish
Yates CCR	04-May-15 A	21-Jan-60
Yates CCR	04-May-15 A	21-Jan-60
Yates AP-1	04-May-15 A	01-Feb-27
Site Regulatory	19-Oct-15 A	01-Feb-27
CCR Final Permit Effective	06-Jan-22 A	06-Jan-22 A
Front End Planning	04-May-15 A	21-Jul-16 A
Construction	04-May-15 A	20-Jun-25
IPCC	27-Nov-19 A	31-Jan-22 A
PCC	31-Jan-22 A	01-Feb-27
Yates AP-2	19-Oct-15 A	19-Feb-29
Site Regulatory	19-Oct-15 A	19-Feb-29
CCR Final Permit Effective	09-Aug-23 A	09-Aug-23 A
Front End Planning	01-Jan-16 A	20-Nov-19 A
Construction	05-Sep-19 A	20-Jun-25
IPCC	24-Apr-23 A	19-Feb-24 A
PCC	20-Feb-24 A	19-Feb-29
Yates AMA (AP-3/AP-B/AP-B'/AP-A)	19-Oct-15 A	21-Jan-60
Site Regulatory	19-Oct-15 A	21-Jan-60
Front End Planning	01-Jan-16 A	30-Apr-18 A
Construction	19-Aug-16 A	21-Jan-28
IPCC	21-Jan-28	20-Jan-30
PCC	20-Jan-30	21-Jan-60
Yates Gypsum Landfill	22-Jul-15 A	13-Sep-24
Site Regulatory	22-Jul-15 A	13-Sep-24
CCR Final Permit Effective	05-Jan-22 A	05-Jan-22 A
IPCC	19-Jan-17 A	14-Feb-22 A
PCC	14-Feb-22 A	13-Sep-24
Yates R-6/AP-C	29-May-15 A	05-Nov-56
Site Regulatory	29-May-15 A	05-Nov-56
Front End Planning	29-May-15 A	21-Jul-16 A
Construction	29-May-15 A	20-Jun-25
IPCC	05-Nov-24	05-Nov-26
PCC	05-Nov-26	05-Nov-56

