
Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Arkwright CCR	19-Oct-15 A	28-Jul-39
Arkwright CCR	19-Oct-15 A	28-Jul-39
AP-1	19-Oct-15 A	28-Jul-39
Site Regulatory	19-Oct-15 A	28-Jul-39
Front End Planning	01-Jan-16 A	10-Nov-26
Construction	01-Jun-23 A	02-Sep-32
IPCC	28-Jul-32	27-Jul-34
PCC	28-Jul-34	28-Jul-39
AP-2 DAS	19-Oct-15 A	23-Nov-37
Site Regulatory	19-Oct-15 A	23-Nov-37
Front End Planning	01-Jan-16 A	10-Nov-26
Construction	27-Jan-27	02-Sep-32
IPCC	21-Nov-30	22-Nov-32
PCC	23-Nov-32	21-Nov-37
AP-3	01-Jan-16 A	01-Mar-39
Site Regulatory	20-Nov-18 A	01-Mar-39
Front End Planning	01-Jan-16 A	10-Nov-26
Construction	26-Feb-26	02-Sep-32
IPCC	01-Mar-32	02-Mar-34
PCC	03-Mar-34	01-Mar-39

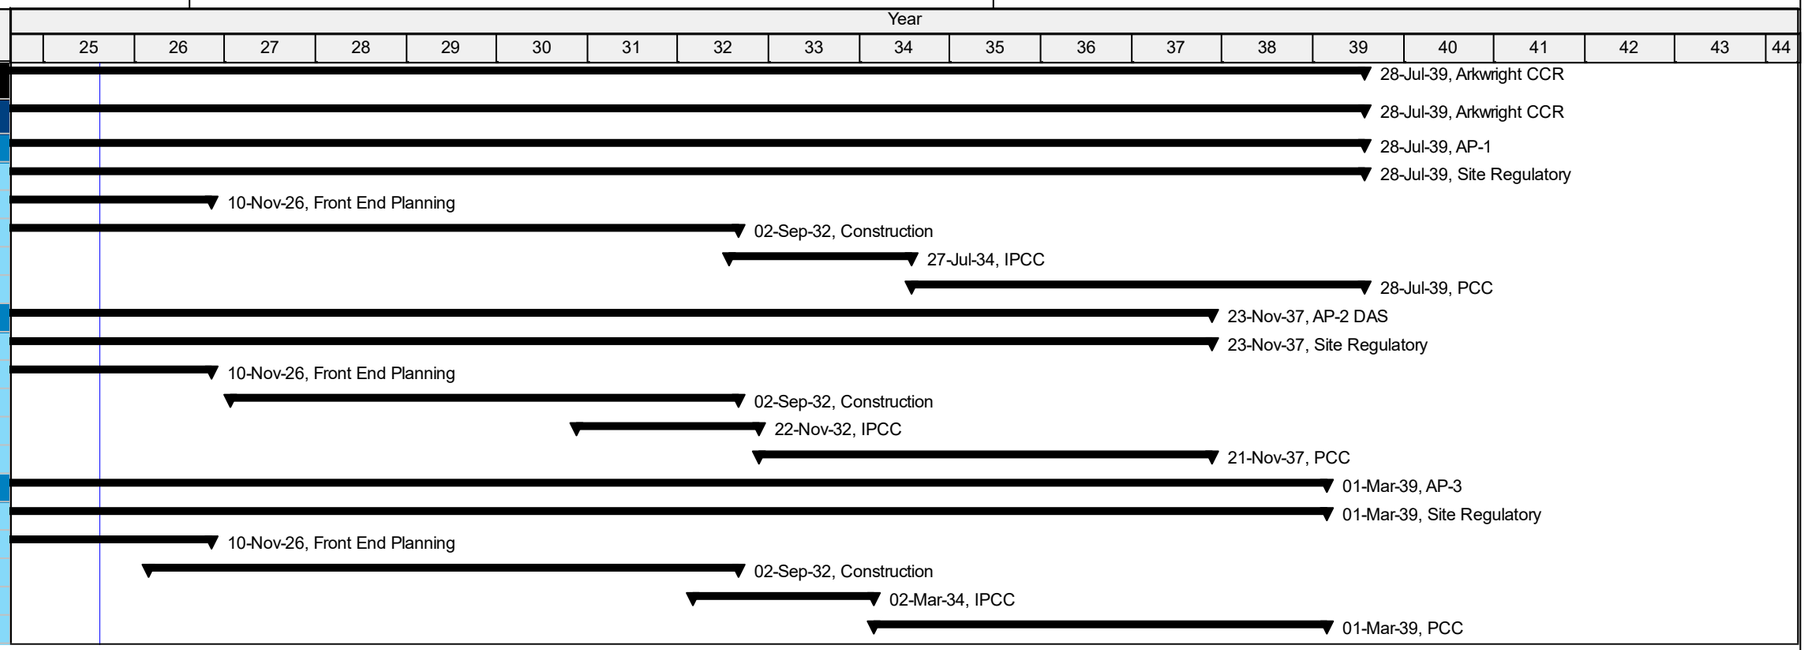


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Bowen CCR	12-May-08 A	31-Dec-71
Bowen CCR	12-May-08 A	31-Dec-71
AP-1	19-Oct-15 A	11-Aug-68
Site Regulatory	19-Oct-15 A	11-Aug-68
Front End Planning	01-Jan-16 A	08-Dec-20 A
Construction	14-Dec-17 A	13-Aug-36
IPCC	14-Aug-36	12-Aug-38
PCC	12-Aug-38	11-Aug-68
Bowen Landfill	12-May-08 A	31-Dec-71
Site Regulatory	12-May-08 A	31-Dec-71
LF Cells 1 & 2	02-Jan-20 A	31-Dec-71
Active Landfill	02-Jan-20 A	31-Dec-37
Construction/Active/Close&Cap	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
LF Cells 3 & 4	02-Jan-20 A	31-Dec-71
Active Landfill	02-Jan-20 A	31-Dec-37
Construction/Active/Close&Cap	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
LF Cells 5 & 6	02-Jan-20 A	31-Dec-71
Active Landfill	02-Jan-20 A	31-Dec-37
Construction/Active/Close&Cap	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
LF Cells 7 & 8	01-Jan-30	31-Dec-71
Active Landfill	01-Jan-30	31-Dec-37
Construction/Active/Close&Cap	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
LF Cells 9 & 10	18-Sep-20 A	31-Dec-71
Active Landfill	18-Sep-20 A	31-Dec-37
Construction/Active/Close&Cap	01-Jan-38	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
Benificial Use	20-Jun-22 A	26-Apr-34

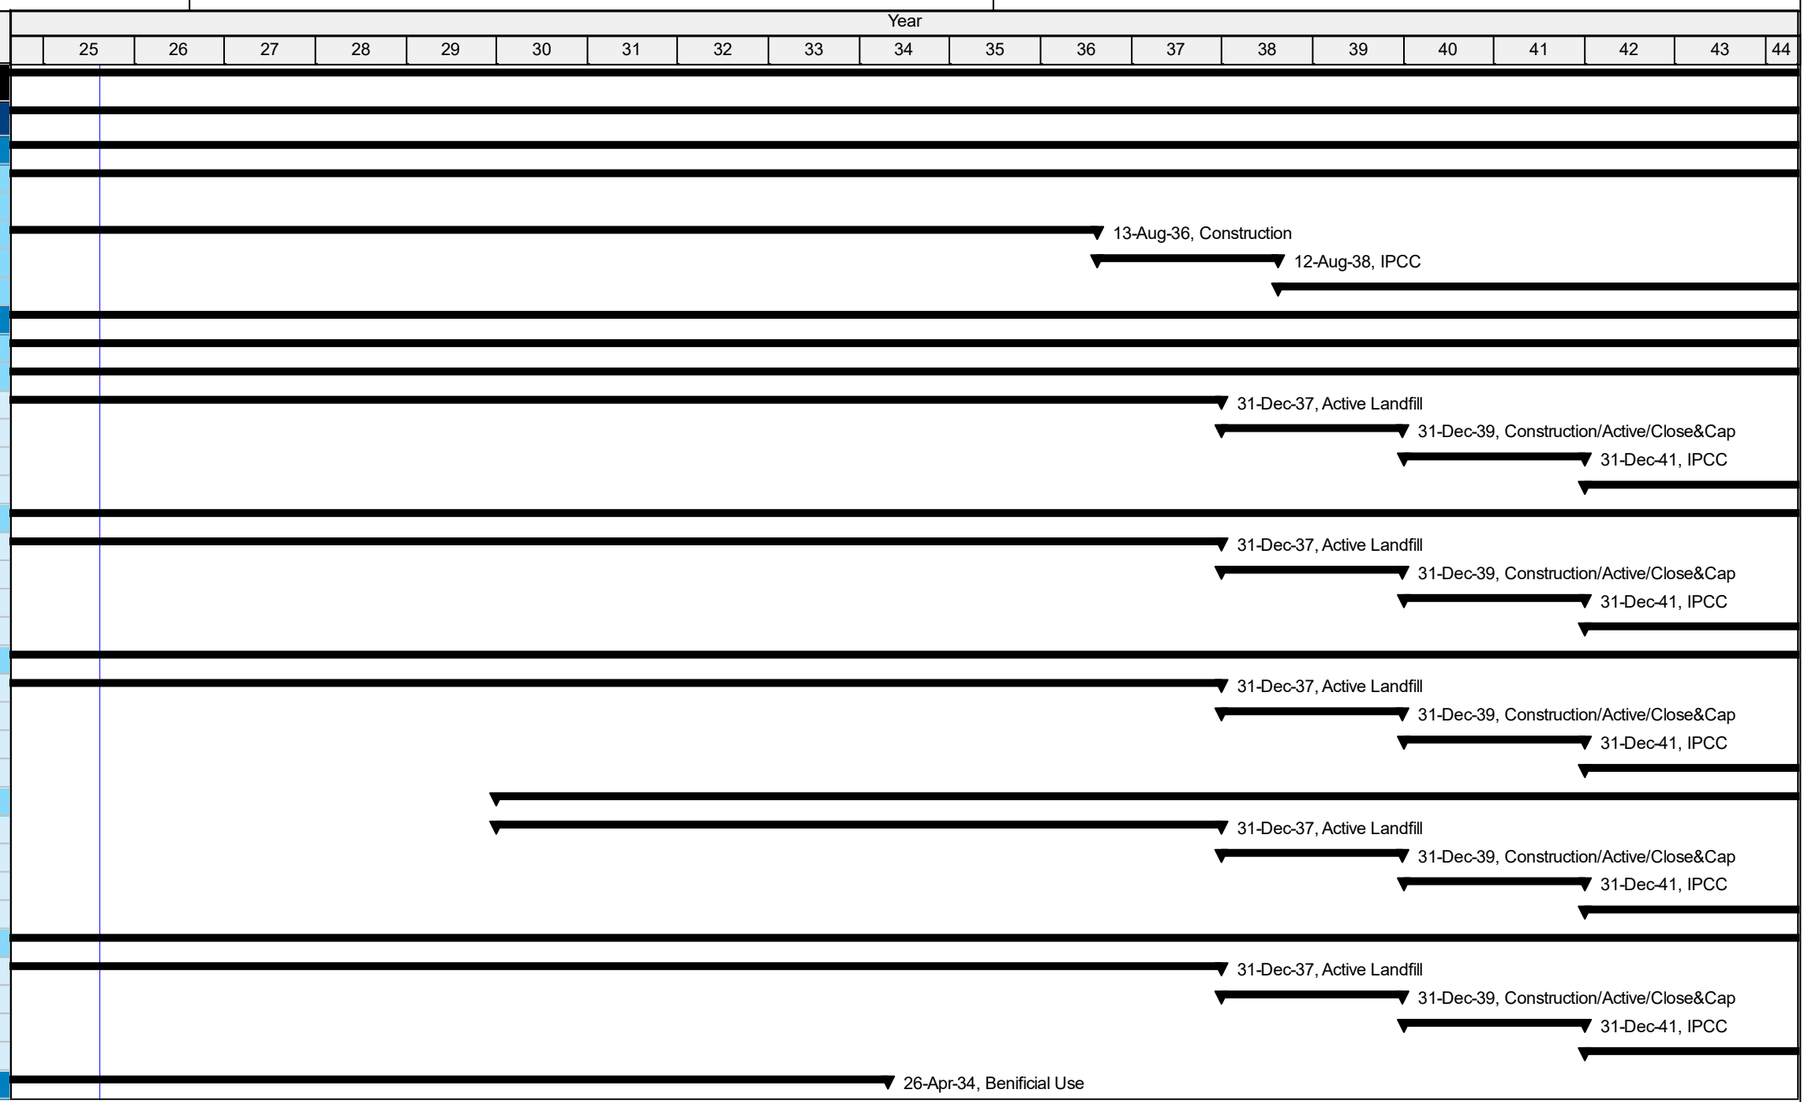


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Branch CCR	19-Oct-15 A	25-May-73
Branch CCR	19-Oct-15 A	25-May-73
AP-B/AP-C/AP-D	19-Oct-15 A	24-Sep-46
Site Regulatory	19-Oct-15 A	24-Sep-46
PCC	23-Sep-41	22-Sep-46
AP-B	21-Apr-27	22-Sep-46
Site Regulatory	22-Sep-39	21-Dec-39
Front End Planning	21-Apr-27	16-Jun-36
Construction	30-Dec-27	29-Jun-40
IPCC	23-Sep-39	22-Sep-41
PCC	23-Sep-41	22-Sep-46
AP-C	15-Jun-29	22-Sep-46
Site Regulatory	24-Dec-36	24-Mar-37
Front End Planning	15-Jun-29	13-Dec-29
Construction	27-Feb-30	01-Sep-37
IPCC	25-Dec-36	22-Sep-41
PCC	23-Sep-41	22-Sep-46
AP-D	05-Dec-24 A	22-Sep-46
Site Regulatory	06-Jan-32	05-Apr-32
Front End Planning	05-Dec-24 A	19-Oct-27
Construction	06-Sep-25	05-Jan-33
IPCC	07-Jan-32	22-Sep-41
PCC	23-Sep-41	22-Sep-46
AP-E	19-Oct-15 A	07-Mar-47
Site Regulatory	19-Oct-15 A	07-Mar-47
Front End Planning	01-Jan-16 A	09-Dec-32
Construction	01-Mar-19 A	14-Jun-41
IPCC	06-Mar-40	06-Mar-42
PCC	07-Mar-42	07-Mar-47
Branch LF Cells 1-6	01-Jan-16 A	25-May-73
Site Regulatory	28-Feb-17 A	25-May-73
Front End Planning	01-Jan-16 A	12-Jul-23 A
Construction/Active/Close&Cap	10-Apr-23 A	14-Jun-41
IPCC	25-May-41	24-May-43
PCC	25-May-43	24-May-73
Beneficial Use	12-Jun-23 A	17-Jun-41

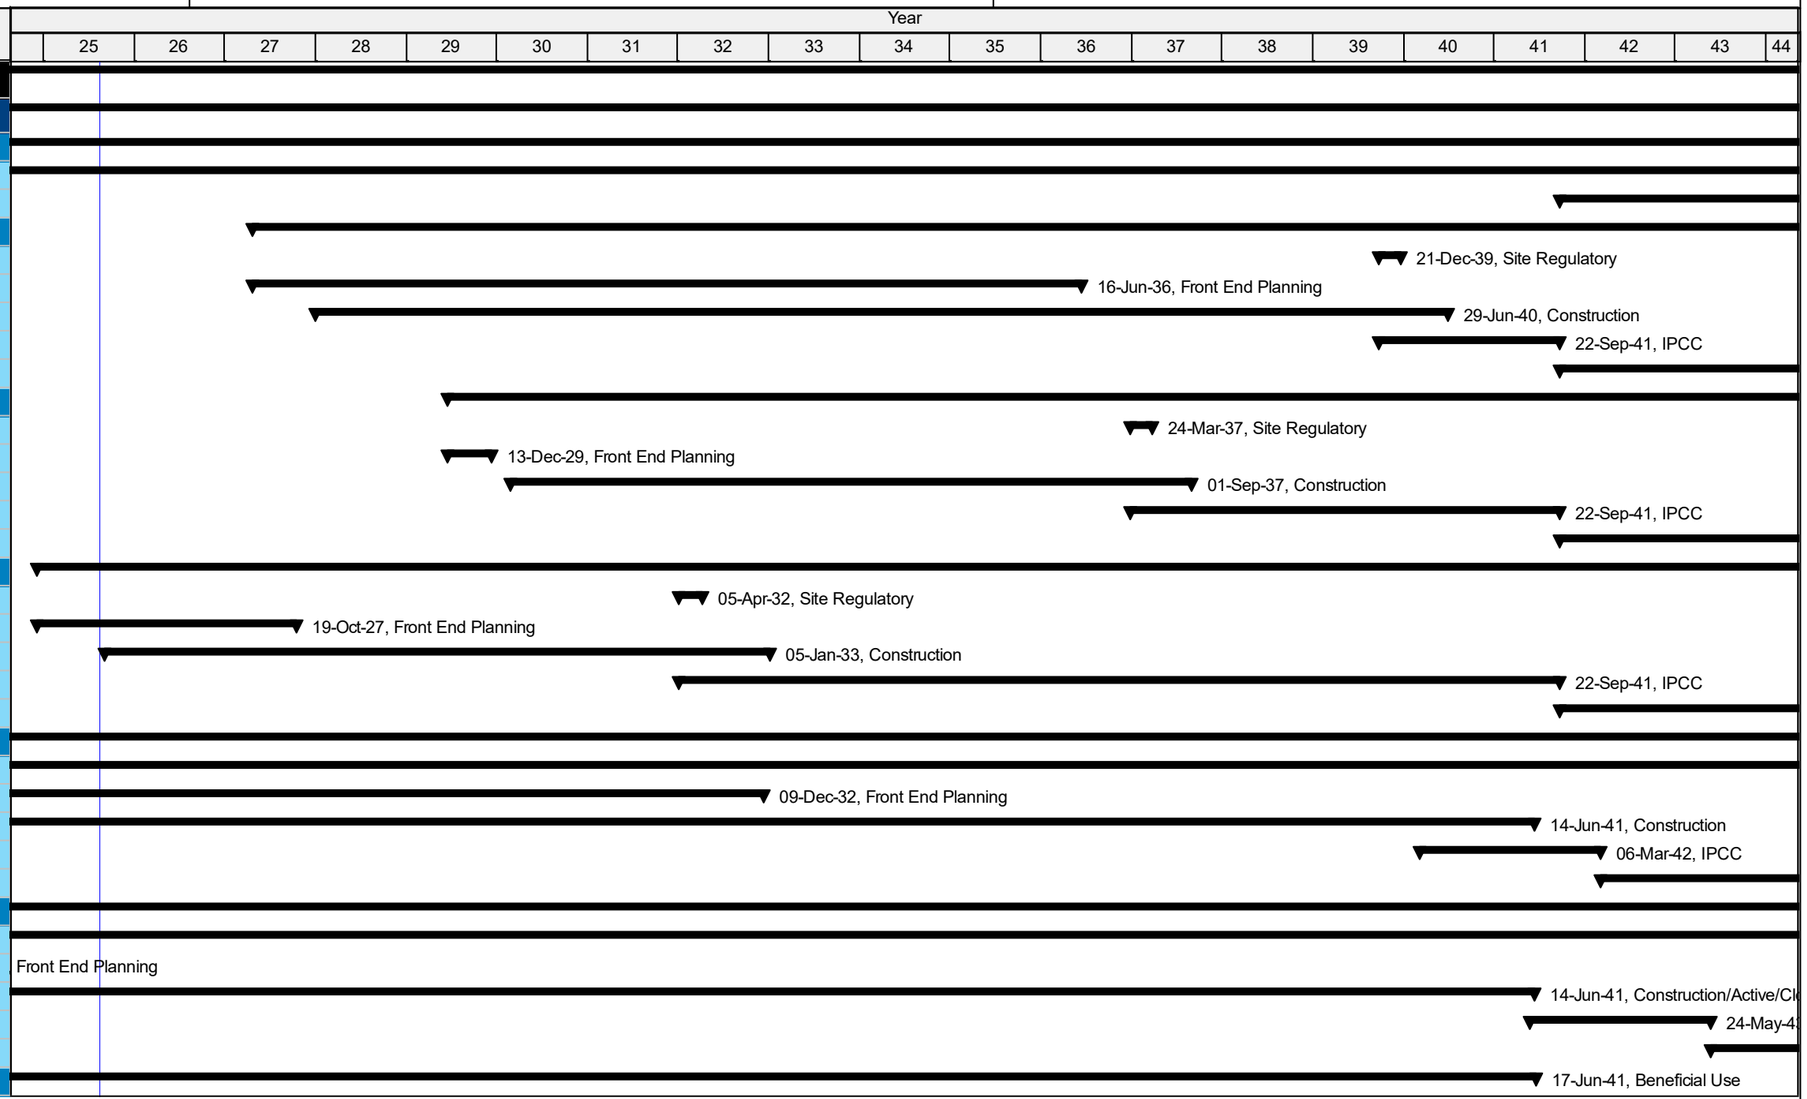


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Hammond CCR	01-Jan-08 A	27-May-66
Hammond CCR	01-Jan-08 A	27-May-66
AP-1	19-Oct-15 A	29-Dec-34
Site Regulatory	19-Oct-15 A	29-Dec-34
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	11-Jan-21 A	08-Mar-28
IPCC	22-Nov-25	21-Nov-27
PCC	22-Nov-27	20-Nov-32
AP-2	19-Oct-15 A	02-Jan-35
Site Regulatory	19-Oct-15 A	02-Jan-35
Front End Planning	01-Jan-16 A	30-Jun-21 A
Construction	04-Jan-21 A	20-Feb-26
IPCC	25-Sep-24 A	31-Dec-24 A
PCC	01-Jan-25 A	31-Dec-34
AP-3	19-Oct-15 A	30-Mar-56
Site Regulatory	19-Oct-15 A	30-Mar-56
Front End Planning	01-Jan-16 A	25-May-16 A
Construction	26-May-16 A	22-Nov-24 A
IPCC	13-Nov-18 A	31-Mar-26
PCC	01-Apr-26	30-Mar-56
AP-4	19-Oct-15 A	05-Nov-40
Site Regulatory	19-Oct-15 A	05-Nov-40
Front End Planning	01-Jan-16 A	31-Mar-28
Construction	09-Aug-21 A	07-Dec-34
IPCC	05-Nov-33	04-Nov-35
PCC	05-Nov-35	04-Nov-40
Huffaker Rd LF	01-Jan-08 A	27-May-66
Site Regulatory	01-Jan-08 A	27-May-66
Huffaker Rd A/B	01-Jan-08 A	26-May-66
Active Landfill	01-Jan-08 A	27-Jun-25 A
Cell Closure/Capping	22-May-24 A	01-Sep-26
IPCC	04-Jun-26	25-May-36
PCC	26-May-36	26-May-66
Huffaker Rd Cell E	19-Dec-22 A	26-May-66
Active Landfill		
Front End Planning	19-Dec-22 A	09-Sep-26
Construction/Active/Close&Cap	06-Oct-26	26-May-34
IPCC	27-May-34	25-May-36
PCC	26-May-36	26-May-66
Huffaker Rd Cell F	13-Feb-26	26-May-66
Front End Planning	13-Feb-26	09-Sep-26
Construction/Active/Close&Cap	06-Oct-26	24-Aug-34
IPCC	26-May-34	25-May-36
PCC	26-May-36	26-May-66

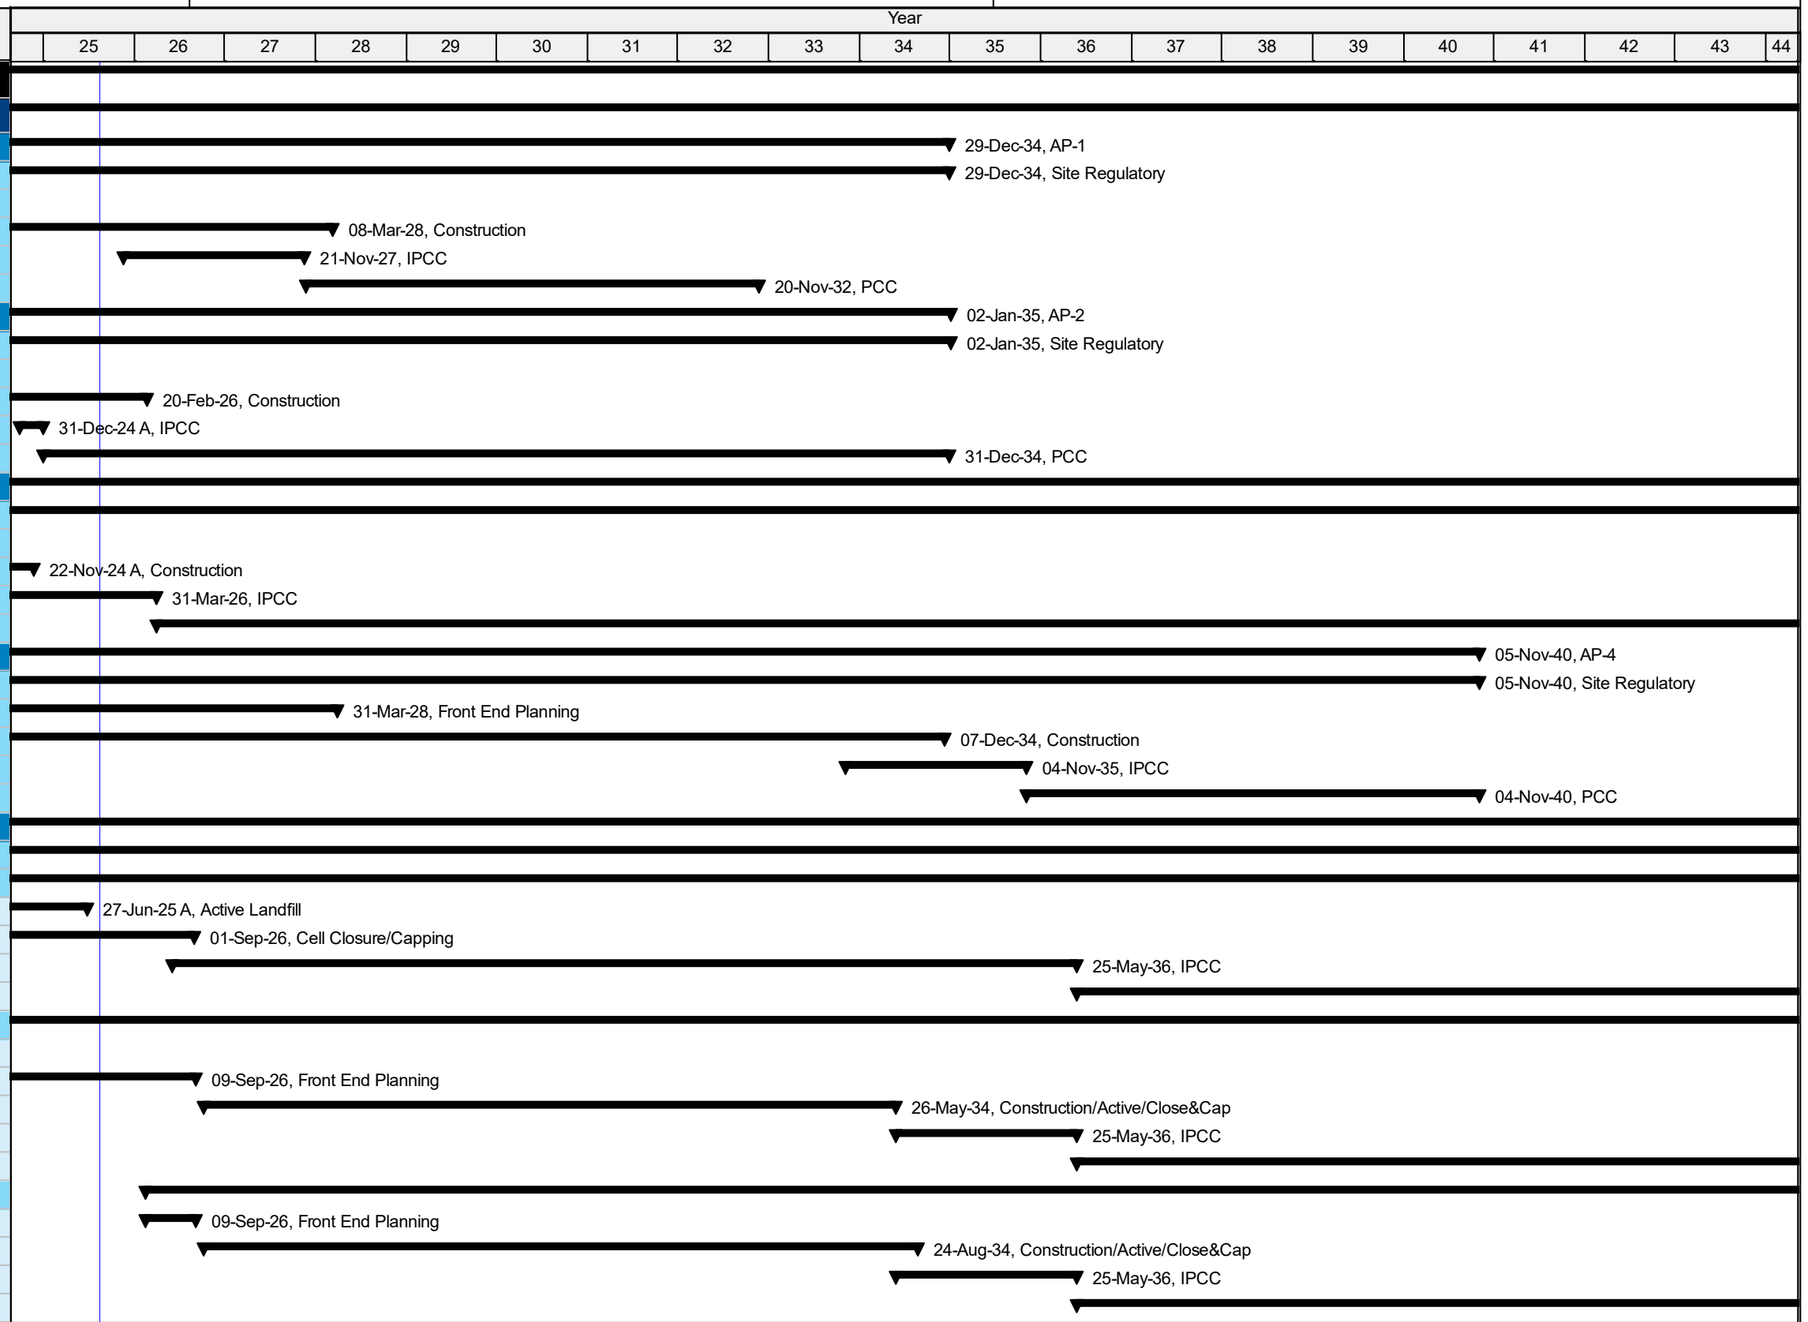


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Kraft CCR	05-Nov-15 A	23-Nov-55
Kraft CCR	05-Nov-15 A	23-Nov-55
Grumman Rd.	05-Nov-15 A	23-Nov-55
Site Regulatory	30-Nov-17 A	23-Nov-55
Front End Planning	05-Nov-15 A	01-Aug-23 A
Construction	27-Feb-17 A	23-Feb-24 A
IPCC	03-Jan-20 A	21-Nov-25
PCC	22-Nov-25	23-Nov-55

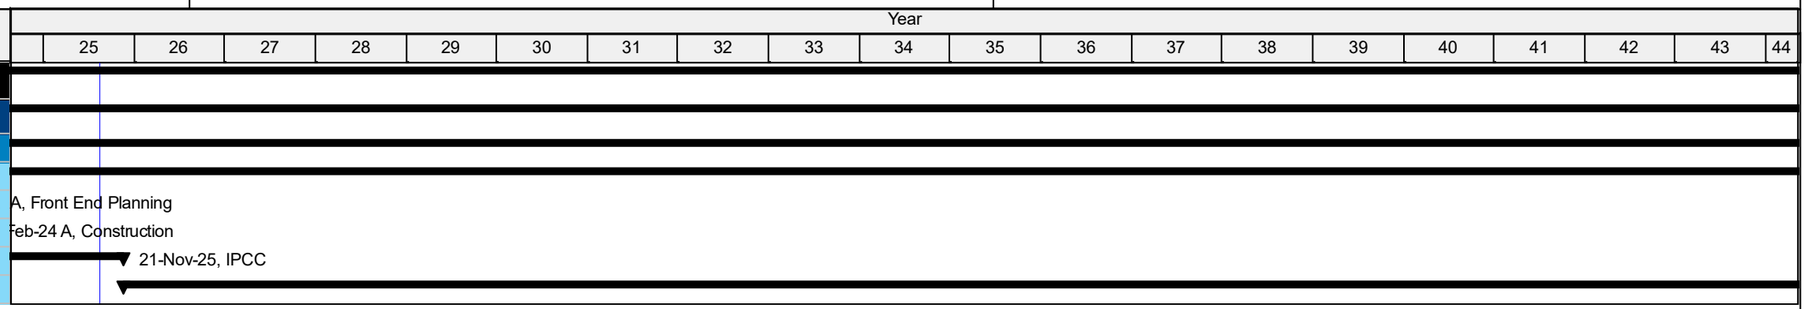


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
McDonough CCR	19-Oct-15 A	27-Jan-59
McDonough CCR	19-Oct-15 A	27-Jan-59
AP-1	19-Oct-15 A	27-Jan-59
Site Regulatory	19-Oct-15 A	27-Jan-59
Front End Planning	01-Jan-16 A	24-Oct-25
Construction	18-Jan-16 A	30-Mar-27
IPCC	27-Jan-27	24-Jan-29
PCC	25-Jan-29	27-Jan-59
AP-2/AP-3/AP-4	19-Oct-15 A	20-Nov-57
Site Regulatory	19-Oct-15 A	20-Nov-57
Front End Planning	01-Jan-16 A	12-Feb-16 A
Construction	19-Jan-16 A	11-Nov-26
IPCC	25-Nov-25	24-Nov-27
PCC AP-2/3/4	30-Nov-27	20-Nov-57

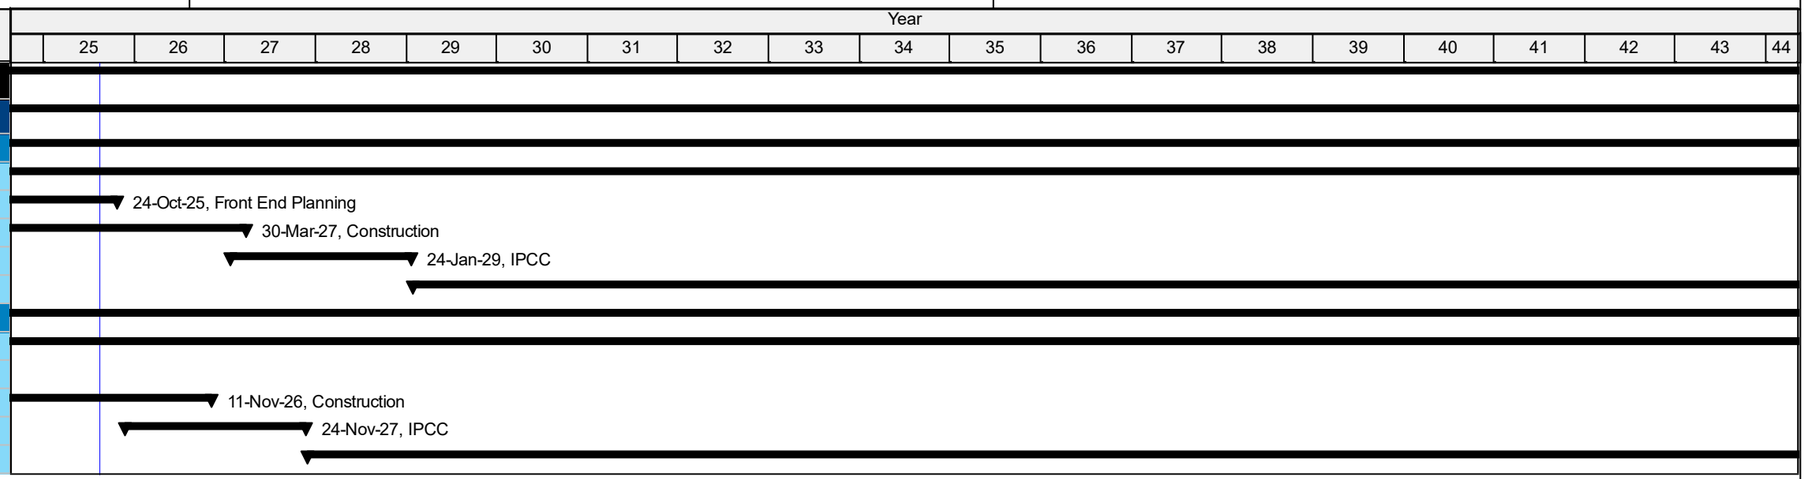


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
McIntosh CCR	21-Mar-08 A	15-Oct-57
McIntosh CCR	21-Mar-08 A	15-Oct-57
AP-1	19-Oct-15 A	31-Aug-38
Site Regulatory	19-Oct-15 A	31-Aug-38
Front End Planning	01-Jan-16 A	06-Feb-20 A
Construction	20-Nov-19 A	06-Jul-22 A
IPCC	08-Sep-21 A	05-Oct-21 A
PCC	06-Oct-21 A	31-Aug-38
McIntosh LF	21-Mar-08 A	15-Oct-57
LF3	21-Mar-08 A	21-Mar-38
Site Regulatory	21-Mar-08 A	21-Mar-38
PCC	21-Mar-08 A	21-Mar-38
LF4	19-Oct-15 A	15-Oct-57
Site Regulatory	19-Oct-15 A	15-Oct-57
Construct/Active/Close&Cap	23-Feb-21 A	15-Mar-23 A
IPCC	27-Nov-18 A	13-Oct-27
PCC	14-Oct-27	15-Oct-57

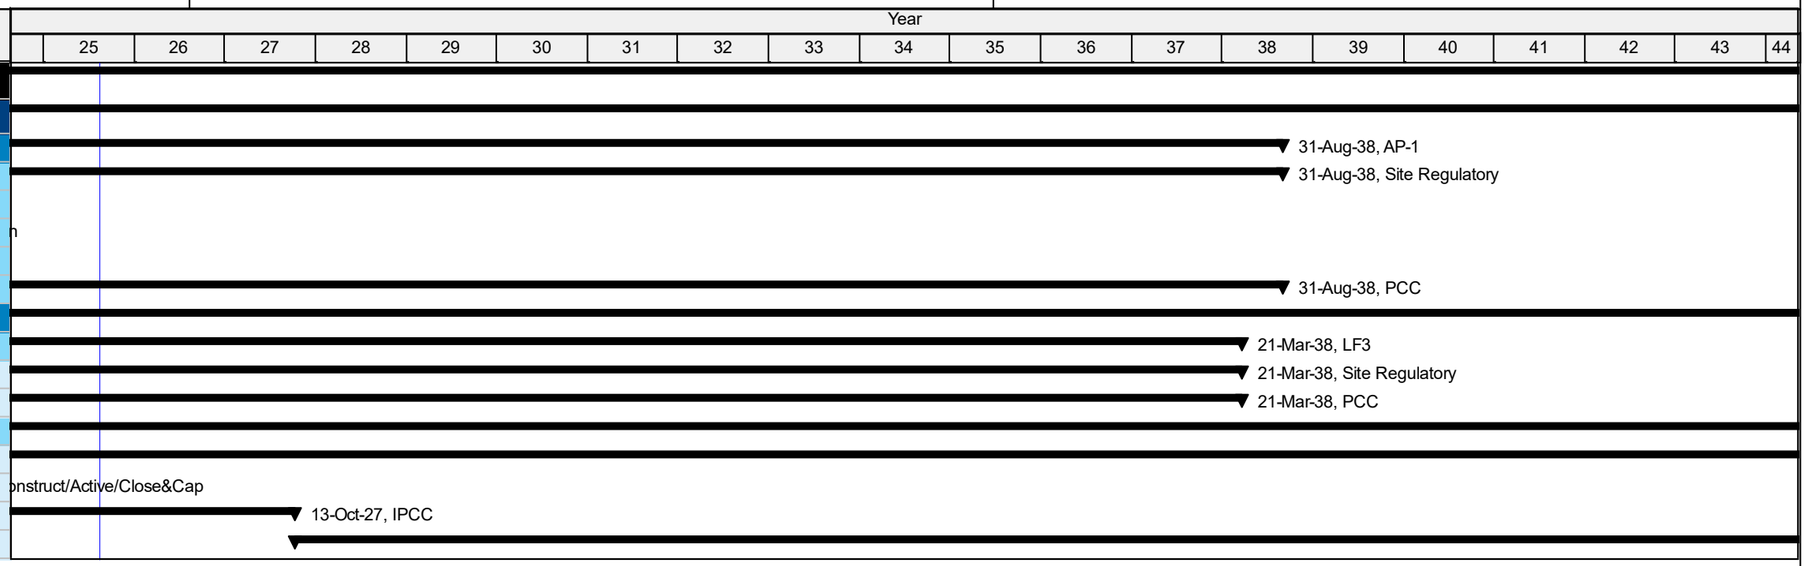


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
McManus CCR	19-Oct-15 A	18-Jun-36
McManus CCR	19-Oct-15 A	18-Jun-36
McManus AP-1	19-Oct-15 A	18-Jun-36
Site Regulatory	19-Oct-15 A	18-Jun-36
Front End Planning	01-Jan-16 A	08-Dec-16 A
Construction	22-Jan-16 A	31-Jul-21 A
IPCC	28-Nov-19 A	18-Jun-21 A
PCC	18-Jun-21 A	18-Jun-36

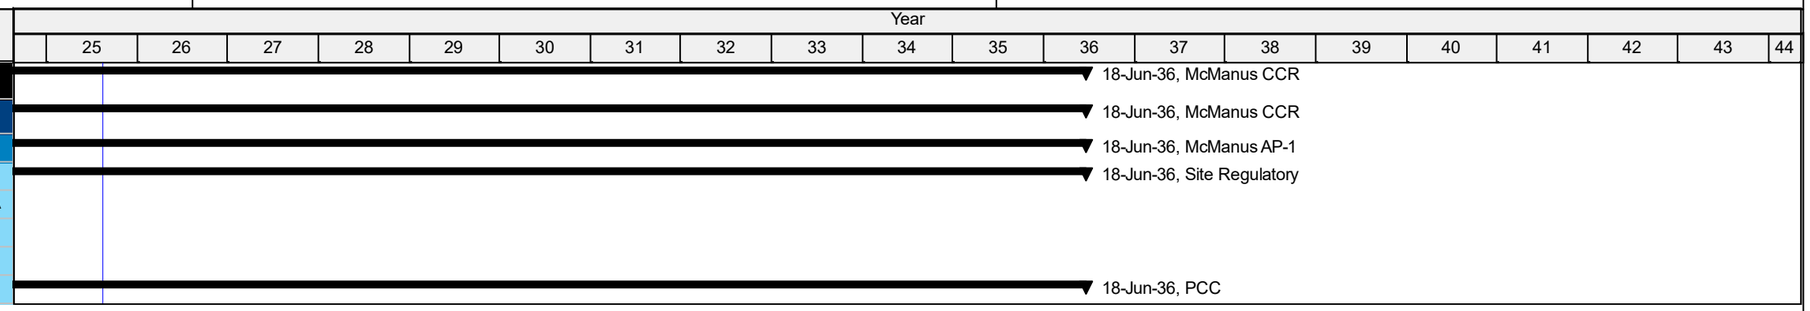


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Mitchell CCR	19-Oct-15 A	25-May-35
Mitchell CCR	19-Oct-15 A	25-May-35
Mitchell AP-1/AP-2/AP-A	19-Oct-15 A	25-May-35
Site Regulatory	19-Oct-15 A	25-May-35
Front End Planning	01-Jan-16 A	19-Feb-21 A
Construction	17-Sep-19 A	26-May-28
IPCC	27-May-28	25-May-30
PCC	26-May-30	24-May-35

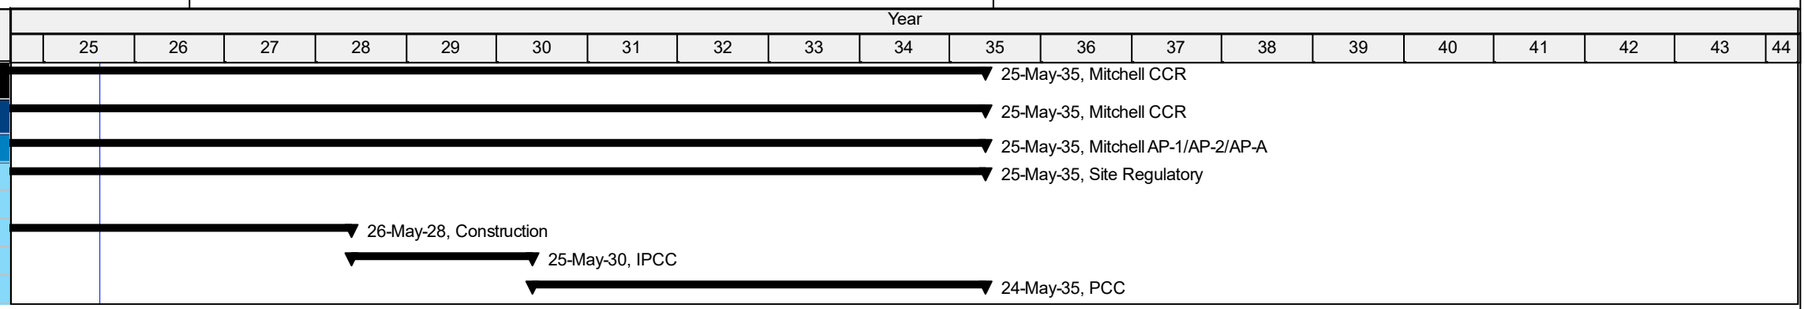


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Scherer CCR	01-Jan-10 A	31-Dec-71
Scherer CCR	01-Jan-10 A	31-Dec-71
Scherer AP-1	19-Oct-15 A	07-Dec-65
Site Regulatory	19-Oct-15 A	06-Dec-65
Front End Planning	01-Jan-16 A	03-Mar-27
Construction	06-Jul-21 A	13-Dec-33
IPCC	07-Dec-33	07-Dec-35
PCC	07-Dec-35	07-Dec-65
Scherer LF	01-Jan-10 A	31-Dec-71
Site Regulatory	01-Jan-10 A	31-Dec-60
LF Cell 1	02-Jan-20 A	31-Dec-71
Active Landfill	02-Jan-20 A	31-Dec-37
Cell Closure/Capping	01-Jan-39	31-Dec-39
IPCC	01-Jan-40	31-Dec-41
PCC	01-Jan-42	31-Dec-71
PAC/ASH CELL	02-Jan-20 A	31-Dec-60
Active Landfill	02-Jan-20 A	31-Dec-26
Cell Closure/Capping	01-Jan-27	31-Dec-28
IPCC	01-Jan-29	31-Dec-30
PCC	01-Jan-31	31-Dec-60
LF Cell C/D	02-Jan-20 A	31-Dec-49
PCC	02-Jan-20 A	31-Dec-49

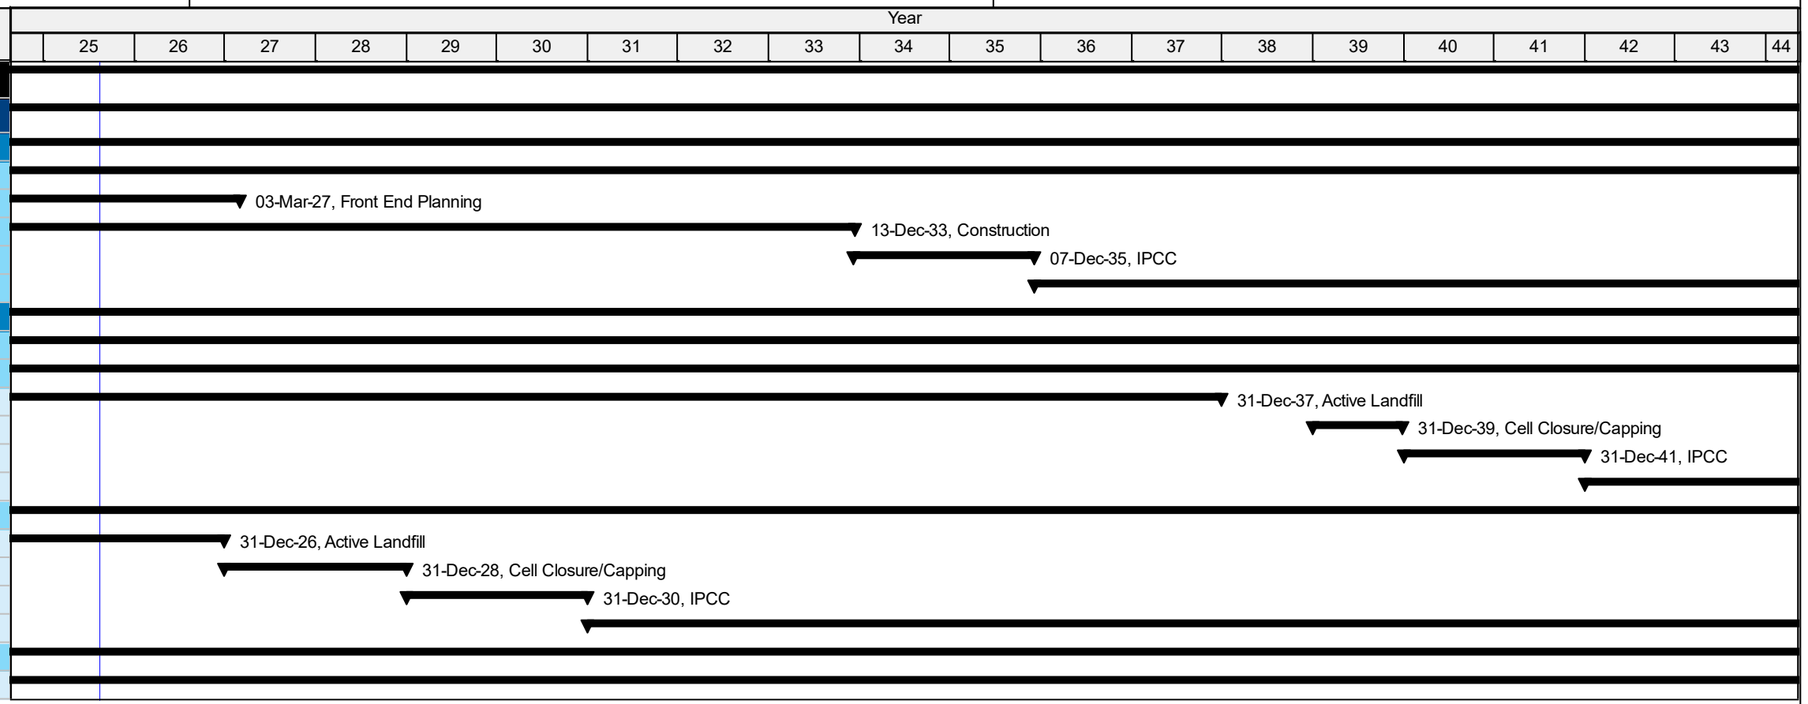


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Wansley CCR	01-Jan-12 A	29-Mar-67
Wansley CCR	01-Jan-12 A	29-Mar-67
Wansley AP-1	19-Oct-15 A	07-Oct-41
Site Regulatory	19-Oct-15 A	07-Oct-41
Front End Planning	01-Jan-16 A	26-Aug-24 A
Construction	19-Apr-21 A	05-Mar-35
IPCC	06-Oct-34	06-Oct-36
PCC	07-Oct-36	06-Oct-41
Wansley Landfill	01-Jan-12 A	29-Mar-67
Site Regulatory	01-Jan-12 A	29-Mar-67
Front End Planning	22-Jul-22 A	31-Oct-25
Construct Cell/Active for Closure	29-Jan-24 A	26-Oct-26
Cell Closure/Capping	08-Jun-34	08-Jun-34
IPCC	29-Mar-35	29-Mar-37
PCC	30-Mar-37	29-Mar-67
Landfill Cells 1/2/3	01-Jan-12 A	29-Mar-67
Active for Closure	01-Jan-12 A	20-Mar-30
Cell Closure/Capping	26-Aug-24 A	28-Mar-35
IPCC	29-Mar-35	29-Mar-37
PCC	30-Mar-37	29-Mar-67
Landfill Cell 4	02-Oct-26	29-Mar-67
Construct Cell/Active for Closure	02-Oct-26	28-Jul-28
Cell Closure/Capping	26-Oct-26	28-Mar-35
IPCC	29-Mar-35	29-Mar-37
PCC	30-Mar-37	29-Mar-67

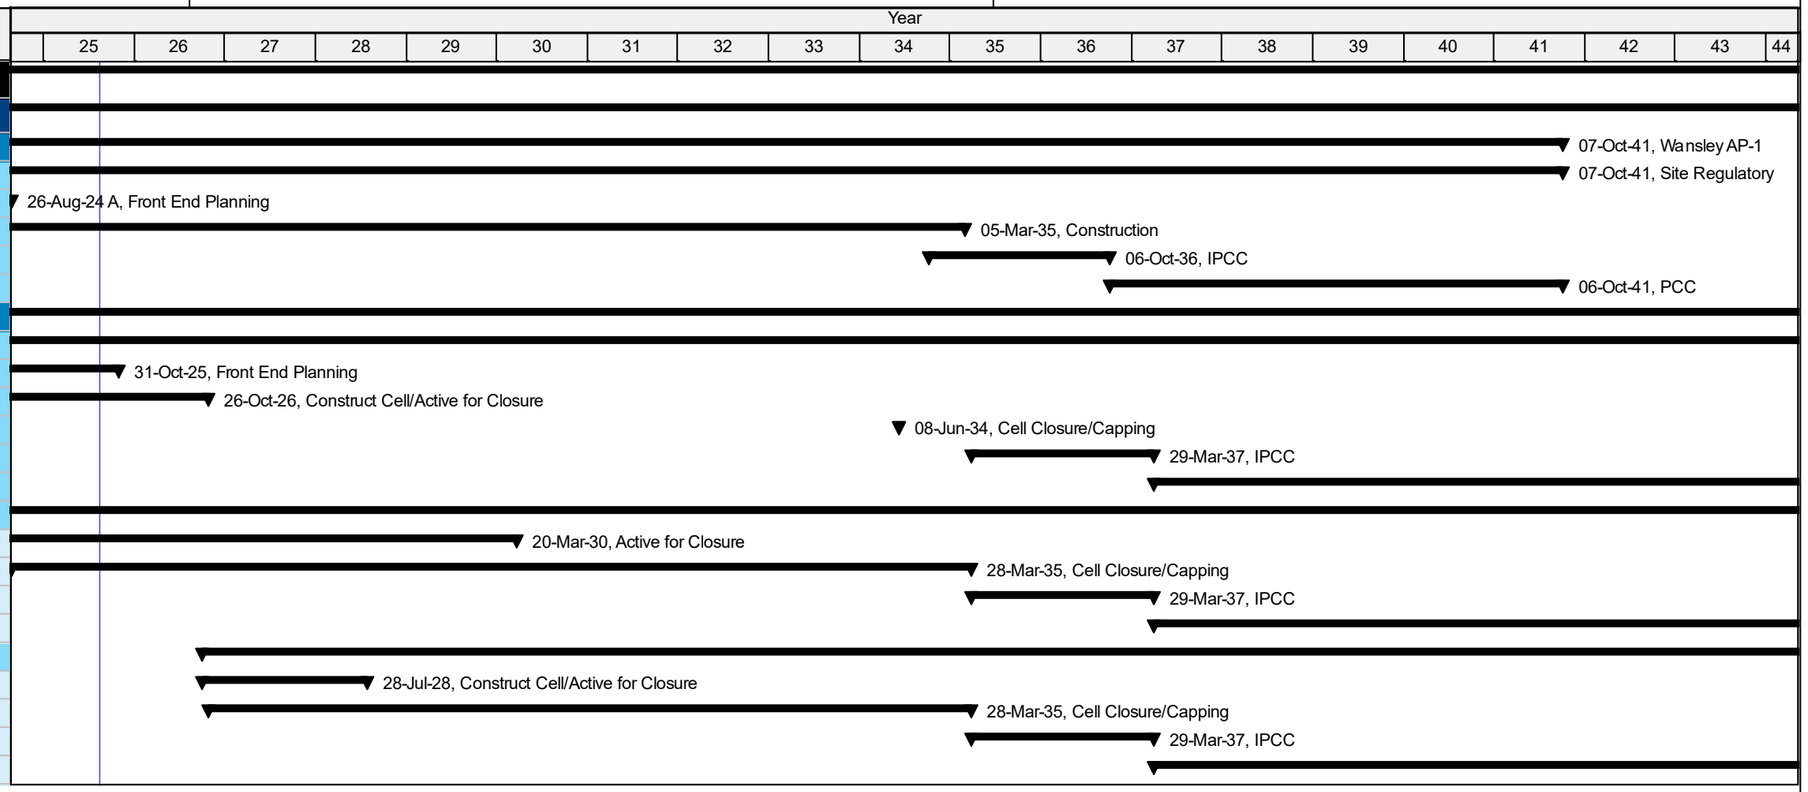


Summary

© Oracle Corporation

Portfolio - Summary - 1Q26

Activity ID	Start	Finish
Yates CCR	04-May-15 A	22-Jan-60
Yates CCR	04-May-15 A	22-Jan-60
Yates AP-1	04-May-15 A	01-Feb-27
Site Regulatory	19-Oct-15 A	01-Feb-27
Front End Planning	04-May-15 A	21-Jul-16 A
Construction	04-May-15 A	16-Oct-25
IPCC	27-Nov-19 A	31-Jan-22 A
PCC	31-Jan-22 A	01-Feb-27
Yates AP-2	19-Oct-15 A	19-Feb-29
Site Regulatory	19-Oct-15 A	19-Feb-29
Front End Planning	01-Jan-16 A	20-Nov-19 A
Construction	05-Sep-19 A	16-Oct-25
IPCC	24-Apr-23 A	19-Feb-24 A
PCC	20-Feb-24 A	19-Feb-29
Yates AMA (AP-3/AP-B/AP-B'/AP-A)	19-Oct-15 A	22-Jan-60
Site Regulatory	19-Oct-15 A	22-Jan-60
Front End Planning	01-Jan-16 A	30-Apr-18 A
Construction	19-Aug-16 A	21-Jan-28
IPCC	21-Jan-28	20-Jan-30
PCC	21-Jan-30	22-Jan-60
Yates Gypsum Landfill	22-Jul-15 A	24-Nov-24 A
Site Regulatory	22-Jul-15 A	24-Nov-24 A
IPCC	19-Jan-17 A	14-Feb-22 A
PCC	14-Feb-22 A	24-Nov-24 A
Yates R-6/AP-C	29-May-15 A	01-Nov-57
Site Regulatory	29-May-15 A	01-Nov-57
Front End Planning	29-May-15 A	21-Jul-16 A
Construction	29-May-15 A	30-Oct-25
IPCC	31-Oct-25	31-Oct-27
PCC	01-Nov-27	01-Nov-57

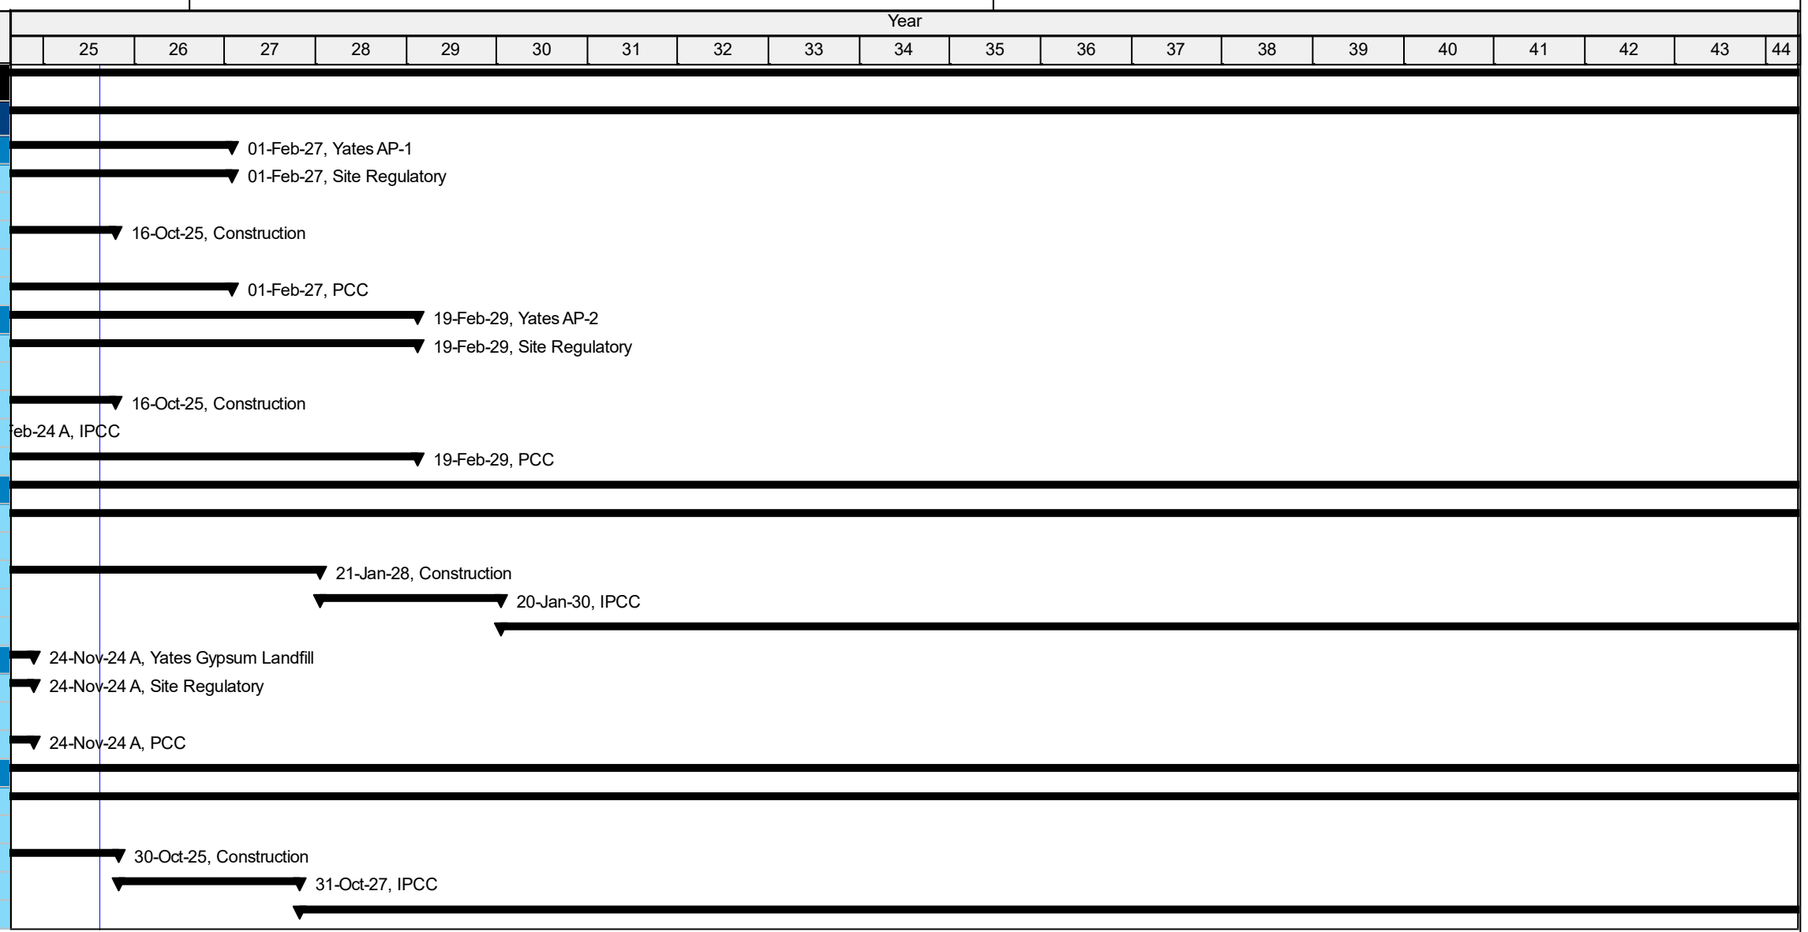

Summary

© Oracle Corporation
