
ID	% Complete	Task Name	Start	Finish	Duration
0	**54%**	**Whitesville Rd Beltline Replacement Full**	**Wed 10/1/25**	**Tue 5/25/27**	**430 days**
1	**77%**	**Design**	**Wed 10/1/25**	**Fri 10/9/26**	**268 days**
2	**100%**	**RFP**	**Wed 10/1/25**	**Mon 11/17/25**	**34 days**
3	100%	Q&A	Wed 10/1/25	Wed 10/8/25	6 days
4	100%	Responses	Thu 10/9/25	Mon 10/13/25	3 days
5	100%	Bids due	Tue 10/14/25	Fri 10/17/25	4 days
6	100%	Review and Award	Mon 10/20/25	Mon 11/17/25	21 days
7	**74%**	**Production**	**Tue 11/18/25**	**Fri 10/9/26**	**234 days**
8	100%	30% Design - Phase 1 & 2	Tue 11/18/25	Tue 12/9/25	16 days
9	100%	60% Design - Phase 1 & 2	Wed 12/10/25	Tue 12/16/25	5 days
10	100%	90% Design - Phase 1	Wed 12/17/25	Tue 12/23/25	5 days
11	77%	90% Design - Phase 2	Wed 12/17/25	Fri 8/28/26	183 days
12	100%	IFC - Phase 1	Wed 12/24/25	Tue 2/24/26	45 days
13	0%	IFC - Phase 2	Mon 8/31/26	Fri 10/9/26	30 days
14	**72%**	**Material Procurement**	**Wed 10/1/25**	**Mon 10/12/26**	**269 days**
15	100%	Pipe RFQ	Wed 10/1/25	Fri 11/14/25	33 days
16	100%	PH1 Delivery	Mon 11/17/25	Mon 4/13/26	106 days
17	43%	PH2 Delivery	Tue 4/14/26	Mon 10/12/26	130 days
18	**50%**	**Construction Phase 1**	**Mon 2/16/26**	**Thu 10/29/26**	**184 days**
19	**100%**	**RFP**	**Mon 2/16/26**	**Thu 4/9/26**	**39 days**
20	100%	Q&A	Mon 2/16/26	Wed 3/4/26	13 days
21	100%	Responses	Thu 3/5/26	Fri 3/6/26	2 days
22	100%	Bids due	Mon 3/9/26	Thu 3/12/26	4 days
23	100%	Review and Award	Fri 3/13/26	Thu 4/9/26	20 days
24	**40%**	**Production**	**Mon 4/13/26**	**Thu 10/29/26**	**144 days**
43	**0%**	**Construction Phase 2**	**Mon 7/20/26**	**Tue 5/25/27**	**222 days**

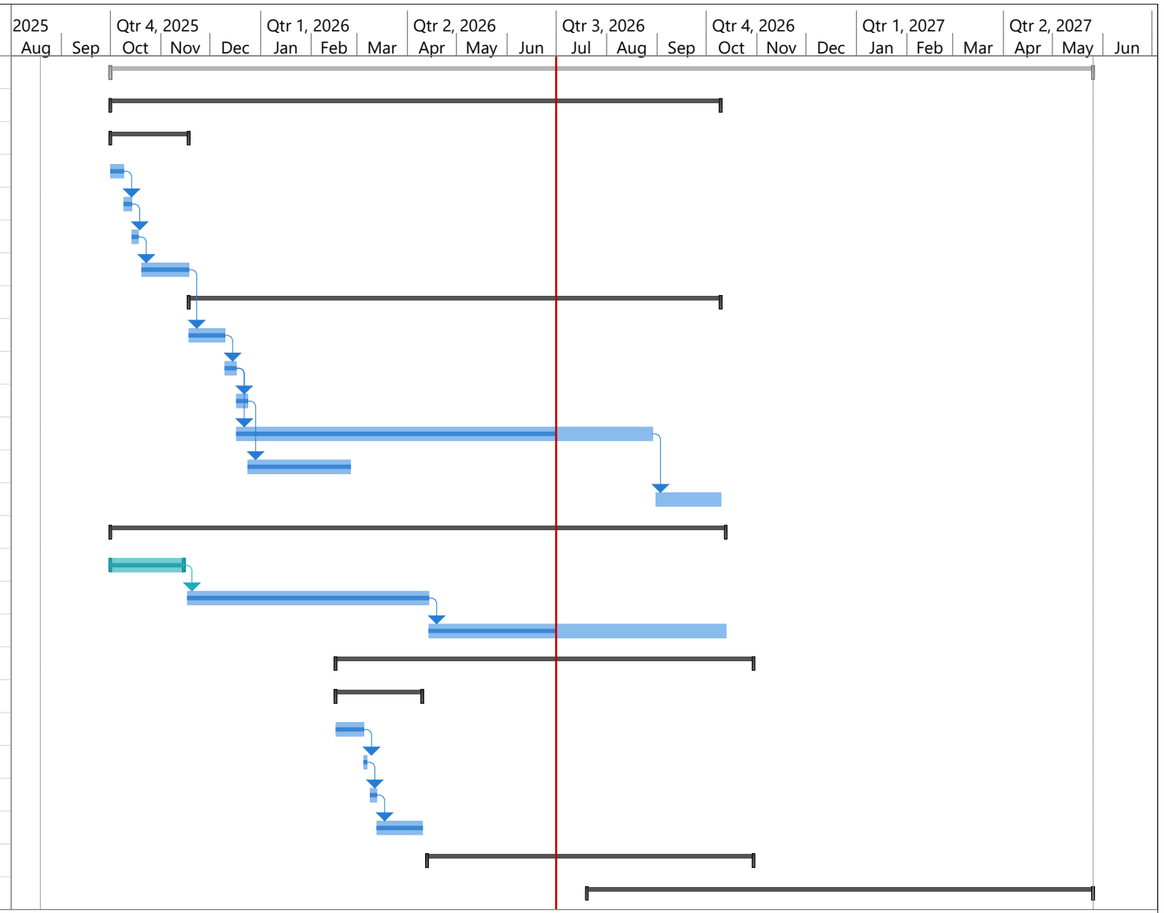

Project: Whitesville Rd Beltline
Date: Mon 8/10/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
