
ID	% Complete	Task Name	Duration	Start	Finish
0	**16%**	**Whitesville Rd Beltline Replacement Full**	**430 days**	**Wed 10/1/25**	**Tue 5/25/27**
1	**30%**	**Design**	**203 days**	**Wed 10/1/25**	**Fri 7/10/26**
2	**100%**	**RFP**	**34 days**	**Wed 10/1/25**	**Mon 11/17/25**
3	100%	Q&A	6 days	Wed 10/1/25	Wed 10/8/25
4	100%	Responses	3 days	Thu 10/9/25	Mon 10/13/25
5	100%	Bids due	4 days	Tue 10/14/25	Fri 10/17/25
6	100%	Review and Award	21 days	Mon 10/20/25	Mon 11/17/25
7	**19%**	**Production**	**169 days**	**Tue 11/18/25**	**Fri 7/10/26**
8	100%	30% Design - Phase 1 & 2	16 days	Tue 11/18/25	Tue 12/9/25
9	100%	60% Design - Phase 1 & 2	5 days	Wed 12/10/25	Tue 12/16/25
10	100%	90% Design - Phase 1	5 days	Wed 12/17/25	Tue 12/23/25
11	9%	90% Design - Phase 2	118 days	Wed 12/17/25	Fri 5/29/26
12	10%	IFC - Phase 1	45 days	Wed 12/24/25	Tue 2/24/26
13	0%	IFC - Phase 2	30 days	Mon 6/1/26	Fri 7/10/26
14	**25%**	**Material Procurement**	**261 days**	**Wed 10/1/25**	**Wed 9/30/26**
15	100%	Pipe RFQ	33 days	Wed 10/1/25	Fri 11/14/25
16	34%	50% Delivery (PH1)	98 days	Mon 11/17/25	Wed 4/1/26
17	0%	100% Delivery (PH2)	130 days	Thu 4/2/26	Wed 9/30/26
18	**0%**	**Construction Phase 1**	**168 days**	**Mon 2/16/26**	**Wed 10/7/26**
19	**0%**	**RFP**	**29 days**	**Mon 2/16/26**	**Thu 3/26/26**
20	0%	Q&A	13 days	Mon 2/16/26	Wed 3/4/26
21	0%	Responses	2 days	Thu 3/5/26	Fri 3/6/26
22	0%	Bids due	4 days	Mon 3/9/26	Thu 3/12/26
23	0%	Review and Award	10 days	Fri 3/13/26	Thu 3/26/26
24	0%	Execution	133 days	Mon 4/6/26	Wed 10/7/26
25	**0%**	**Construction Phase 2**	**222 days**	**Mon 7/20/26**	**Tue 5/25/27**
26	**0%**	**RFP**	**37 days**	**Mon 7/20/26**	**Tue 9/8/26**
27	0%	Q&A	10 days	Mon 7/20/26	Fri 7/31/26
28	0%	Responses	5 days	Mon 8/3/26	Fri 8/7/26
29	0%	Bids due	5 days	Mon 8/10/26	Fri 8/14/26
30	0%	Review and Award	17 days	Mon 8/17/26	Tue 9/8/26
31	0%	Execution	165 days	Wed 10/7/26	Tue 5/25/27

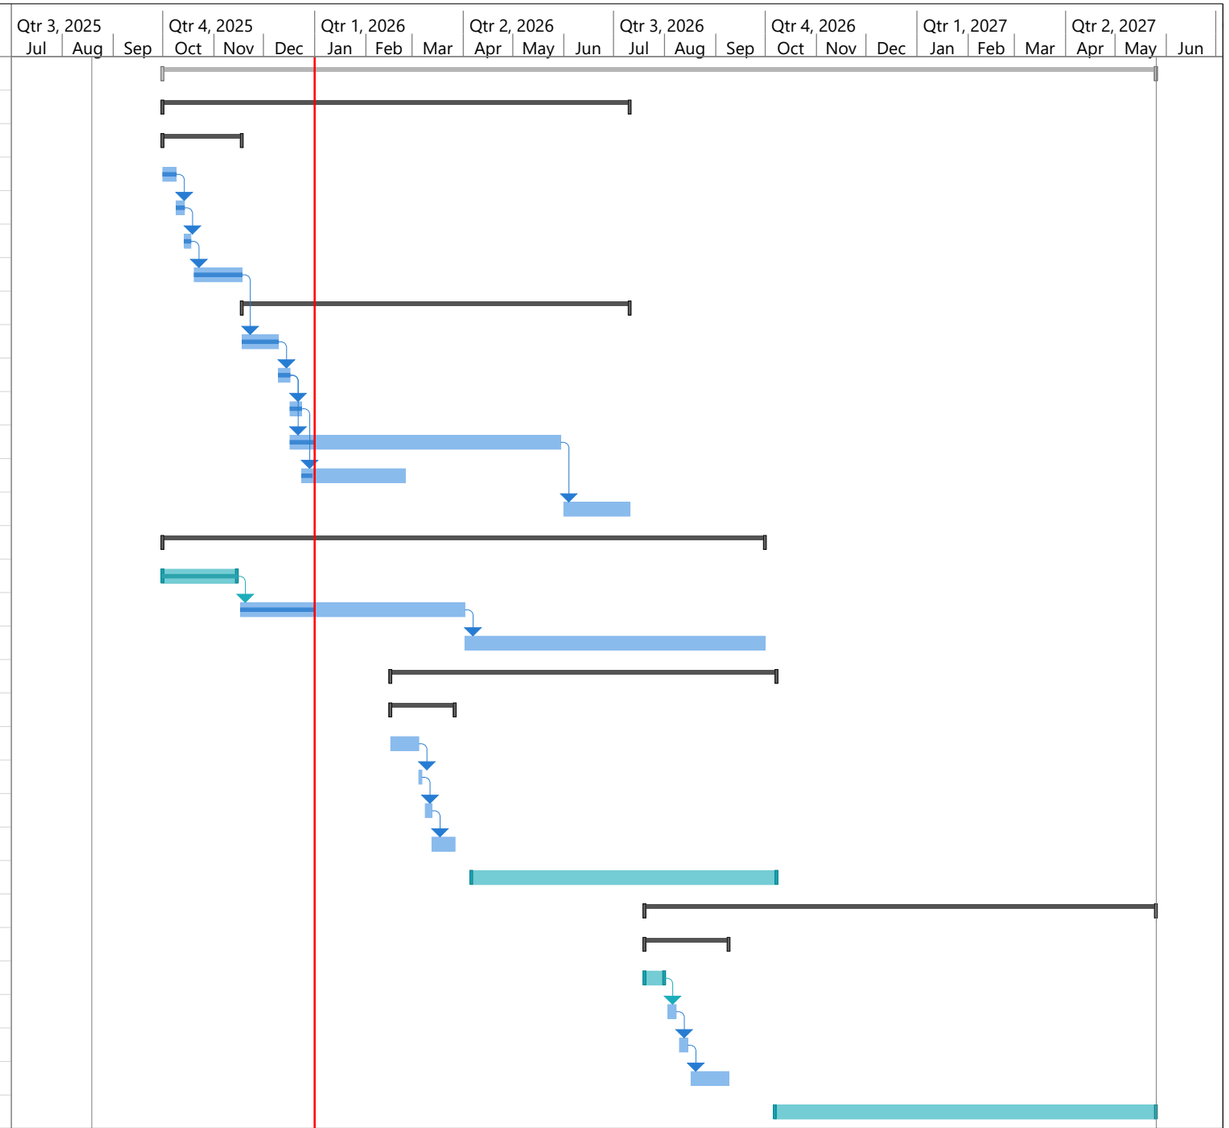

Project: Whitesville Rd Beltline
Date: Fri 3/13/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
