
ID	% Complete	Task Name	Start	Finish	Duration
1	**70%**	**Project: AGTL Schedule**	**Mon 12/30/2**	**Fri 3/31/28**	**850 days**
2	**100%**	**Phase A**	**Mon 12/30/2**	**Sun 5/31/26**	**370 days**
3	100%	Enigneering Design Phase A	Mon 12/30/2	Wed 6/11/25	118 days
4	100%	Local Permitting	Tue 2/11/25	Mon 7/28/25	120 days
5	100%	Environmental Permitting	Tue 2/4/25	Tue 6/10/25	91 days
6	100%	Material Procurement	Mon 1/20/25	Thu 11/20/25	219 days
7	100%	Land Acquisition	Mon 3/17/25	Mon 7/21/25	91 days
8	100%	Construction RFP Process	Mon 3/17/25	Tue 6/3/25	57 days
9	100%	Phase A Construction	Wed 6/4/25	Wed 12/31/25	151 days
10	100%	Restoration	Wed 10/1/25	Sun 5/31/26	174 days
11	**59%**	**Phase B & C**	**Thu 2/13/25**	**Fri 3/31/28**	**817 days**
12	100%	Survey Phase B & C	Wed 8/20/25	Mon 3/9/26	144 days
13	69%	Land Acquisition B & C	Wed 8/20/25	Sun 11/15/26	324 days
14	100%	Geotech Phase B	Mon 1/26/26	Tue 3/31/26	47 days
15	100%	Cathodic Protection Design	Thu 2/13/25	Wed 9/10/25	150 days
16	100%	Engineering Design Phase B	Wed 6/4/25	Tue 6/30/26	280 days
17	100%	Local Permitting Phase B	Thu 6/26/25	Mon 4/13/26	208 days
18	100%	Environmental Permitting	Thu 12/4/25	Tue 6/2/26	129 days
19	82%	Material Procurement Phase B	Mon 1/5/26	Thu 8/6/26	154 days
20	100%	Construction RFP Process Phase B	Tue 4/14/26	Mon 5/25/26	30 days
21	11%	Phase B Construction	Mon 6/8/26	Thu 12/31/26	149 days
22	0%	Phase B Restoration	Wed 9/9/26	Wed 3/31/27	146 days
23	85%	Engineering Design Phase C	Wed 6/4/25	Wed 9/9/26	331 days
24	7%	Local Permitting Phase C	Mon 6/15/26	Fri 2/5/27	170 days
25	0%	Material Procurement Phase C	Mon 10/12/2	Wed 4/21/27	138 days
26	0%	Construction RFP Process Phase C	Mon 2/1/27	Wed 4/7/27	48 days
27	0%	Phase C Construction	Thu 4/29/27	Fri 12/31/27	177 days
28	0%	Phase C Restoration	Sun 8/1/27	Fri 3/31/28	176 days

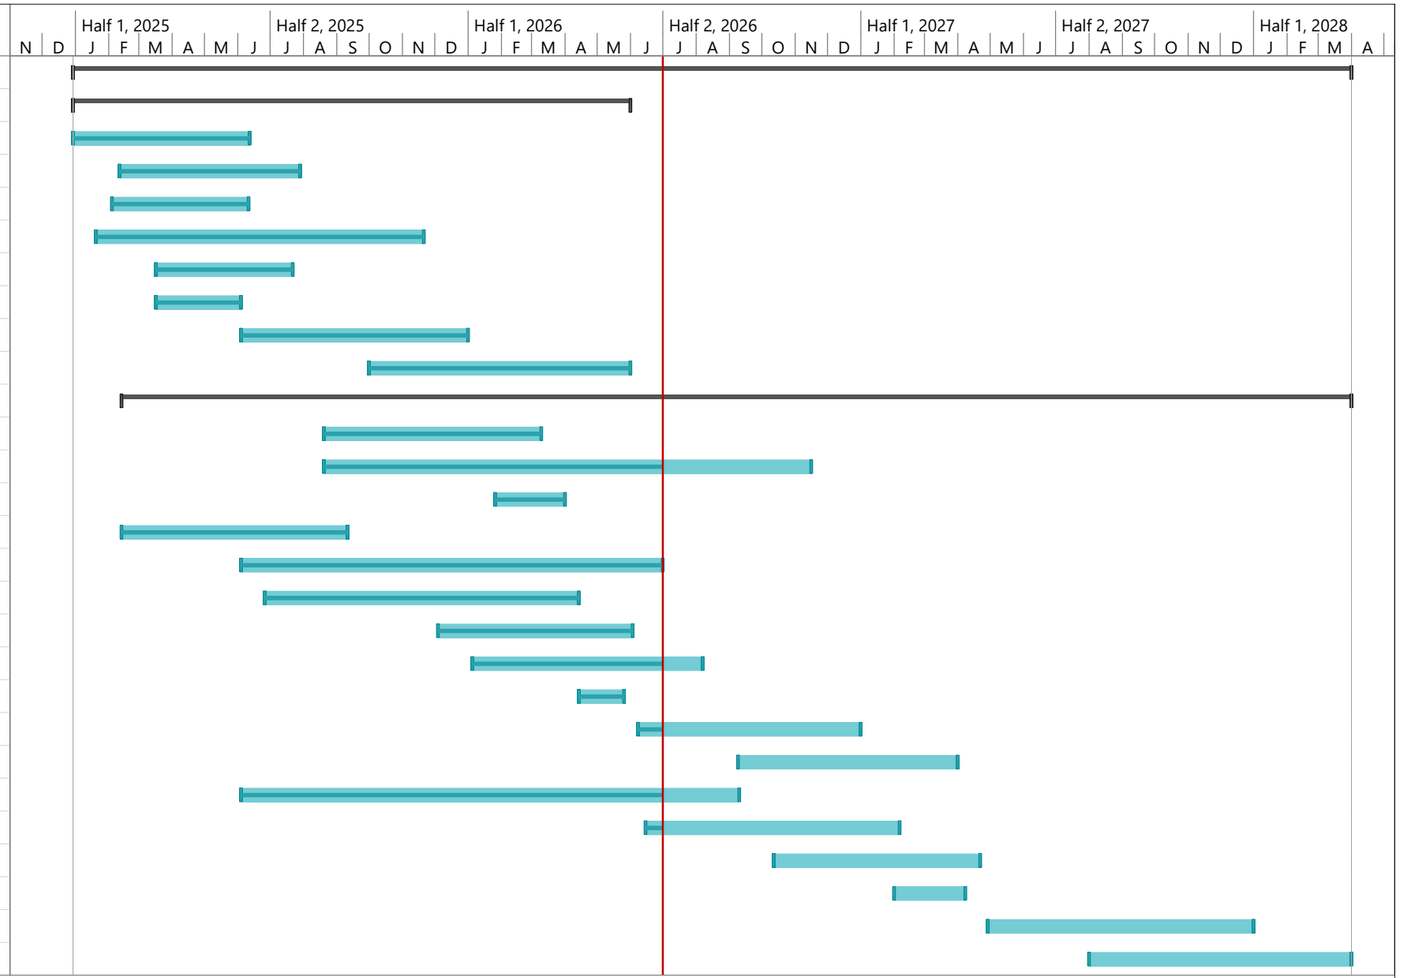

Project: AGTL Gantt
Date: Mon 8/10/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
